



Department of Transportation

POLLY TROTTERBERG, Commissioner

March 10, 2016

Alex Bell



RE: FOIL Request # 2015-15620

Dear Mr. Bell:

Pursuant to your request for records under Article 6 of the New York State Public Officers Law (“FOIL”), enclosed are the responsive records.

For any further correspondence, please reference the FOIL Request number noted above.

Sincerely,

David Garfinkel
FOIL Unit




Columbus Avenue
Bicycle Path and Mobility Enhancements
Community Board 7

Commissioner Janette Sadik-Khan, New York City Department of Transportation
January 8, 2013




Project Background

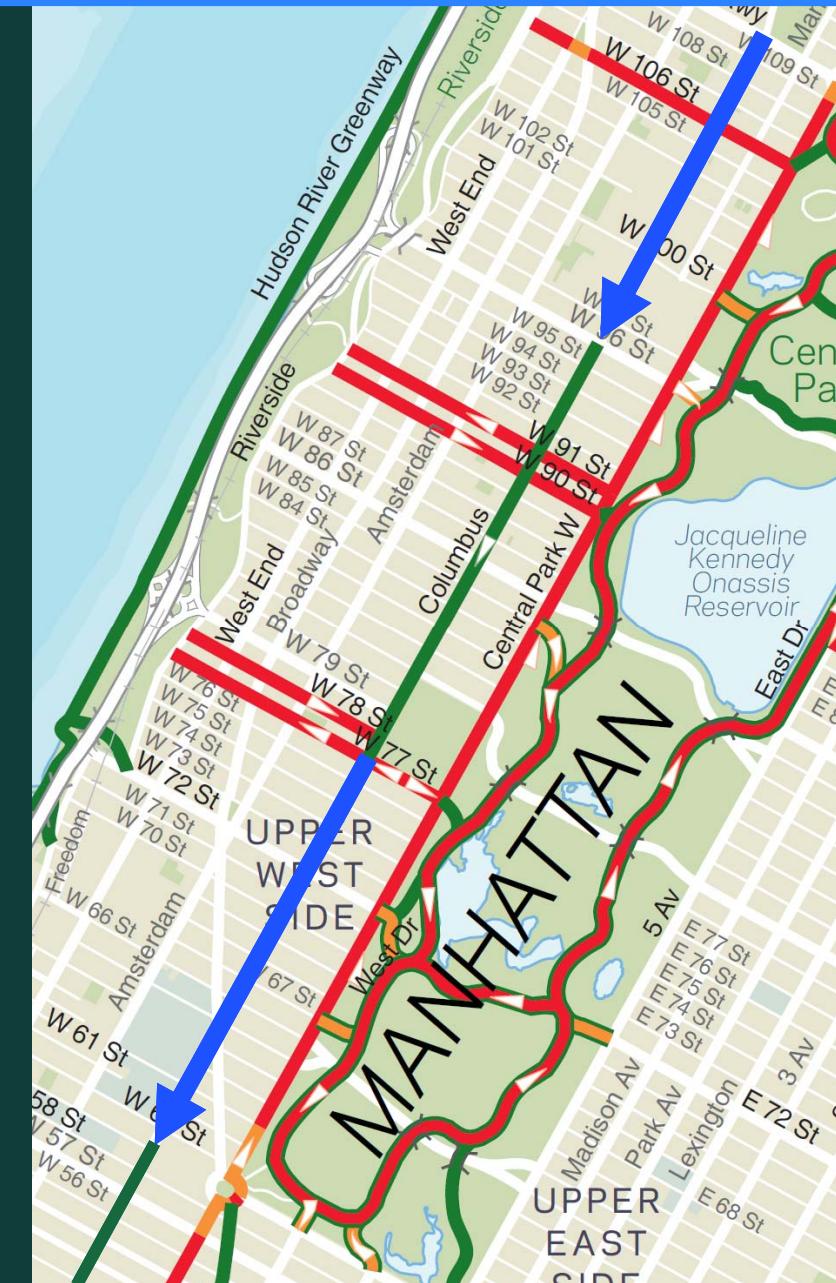

- Extend design on Columbus Avenue
 - W 110 St to W 96 St: Protected Path
 - W 77 St to W 69th St: Protected Path
 - W 69th St to W 63rd St: Enhanced Shared Lane
 - W 63rd St to W 59th St: Protected Path
- Provide connections to existing bicycle facilities
 - 106th St
 - 9th Avenue
 - Columbus Avenue
- Tailor design to improve traffic flow in congested areas
- Provide loading zones for businesses with need

Business Outreach

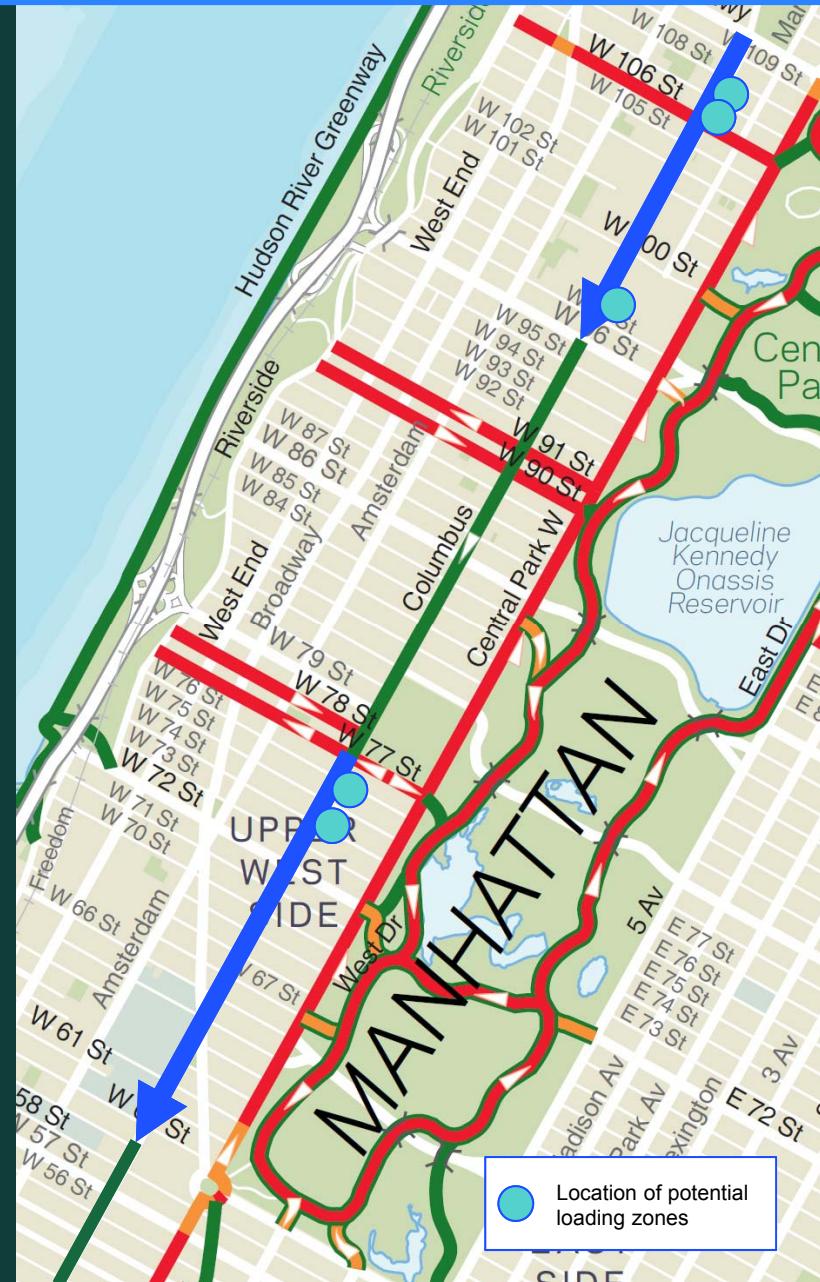

- Visited all surrounding businesses to review their need for potential loading regulations
- Spoke with 189 businesses
- 5 New loading zones/extension recommended
 - 107-108: WS Movers
 - 106-105: Adel Wine, 99 Cent Store
 - 98-97: Duane Reade
 - 76-75: Duane Reade
 - 74-73: Pioneer Supermarket

Rush Hour Regulation Changes

- Low vehicle volumes from 110th to 96th St
 - *868 cars during peak hour (8:00-9:00am)
- Removal of rush hour regulations, 7-10am M-F
- Return of 105 car parking spaces (110th to 96th)



Parking/Loading Changes

Parking Regulation Changes	Parking Space Equivalents (Approx.)		
	110 th to 96 th	77 th to 65 th	Total
Spaces Converted to Daytime Loading Zones	19	11	30
Spaces Gained from Rush Hour Lane Removal	105	0	105


- Loading zones are available for overnight and weekend community parking

East Side Repurposed Parking Space (west side not affected by islands & turn lanes)	Parking Space Equivalents (Approx.)		
	110 th to 96 th	77 th to 65 th	Total
Turn Lanes/ Mixing Zones	23	22	45
Pedestrian Islands	9	7	16
Total Spaces Repurposed	32	29	61
Total Existing Parking Spaces	149	108	257
Percent of Spaces Repurposed	21%	27%	24%

- W 96th St to W 77th St:
 - (6) parking spots gained with new mixing zone length


Note: Upper Section, 17 islands, 4 mixing zones, 1 turn lane; Lower 12 islands, 3 mixing zone, 1 turn lane

Turning Conflict

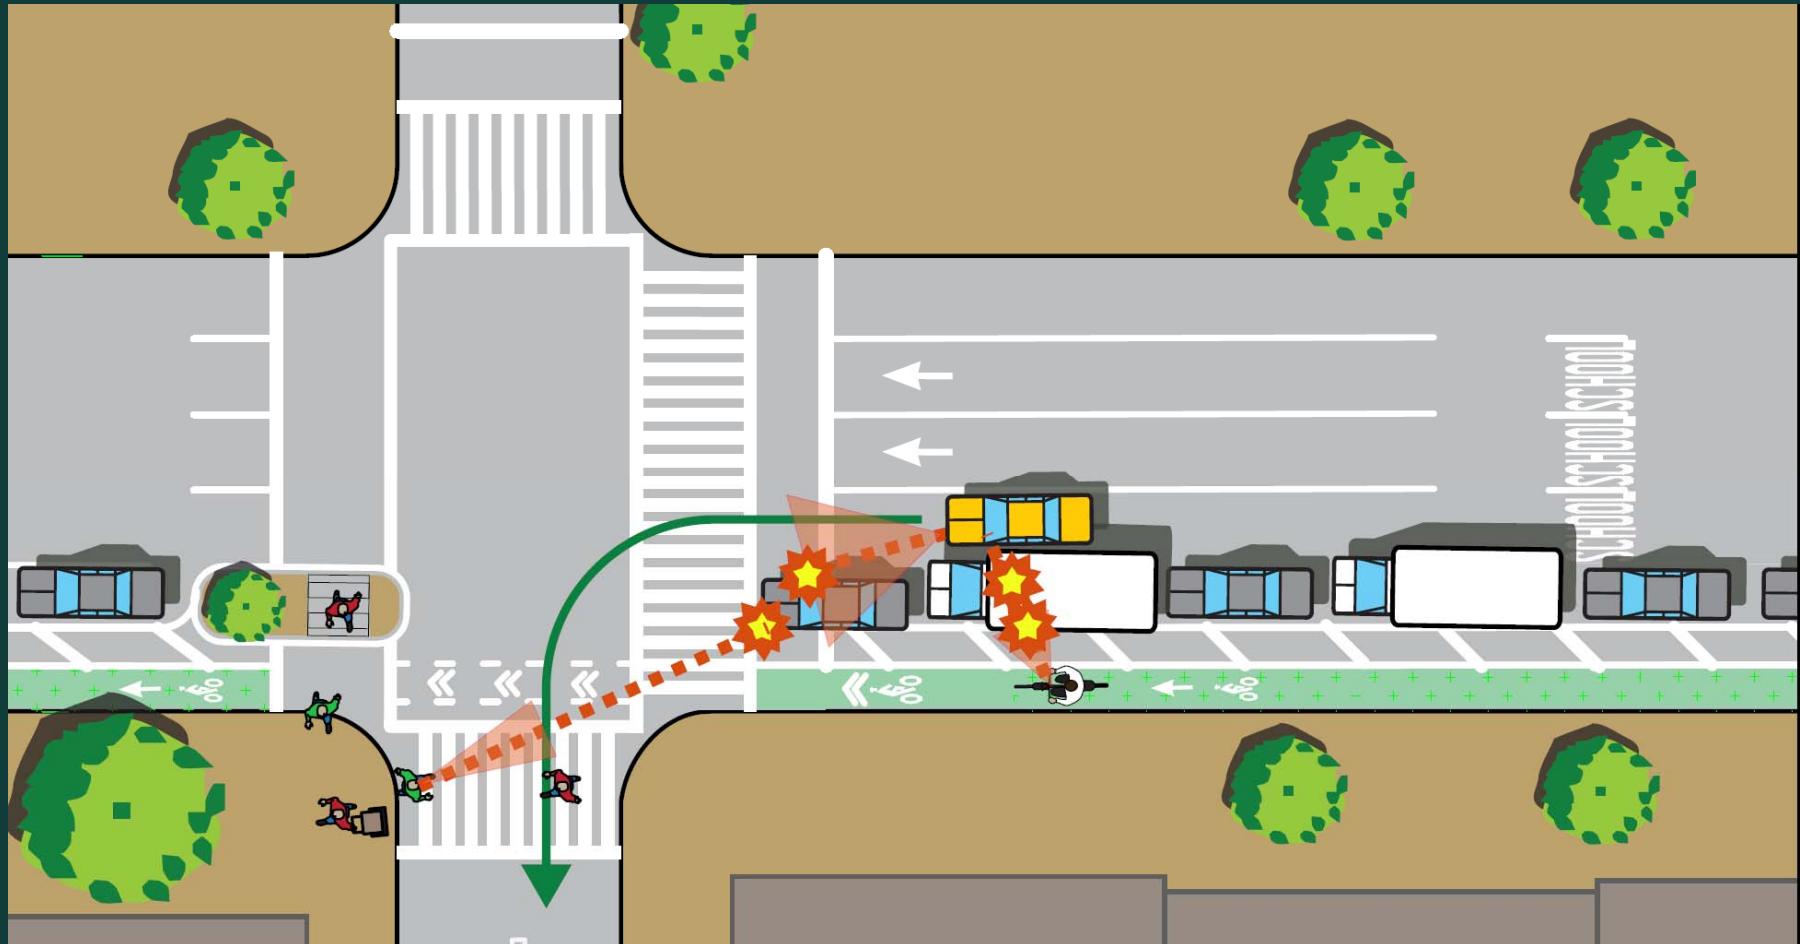

- Turning Conflict is Real & Potentially Deadly
 - Citywide, left turning pedestrian killed/severely injured crashes outnumber right turning crashes by 3 to 1

Protected Bicycle Path Mixing Zone

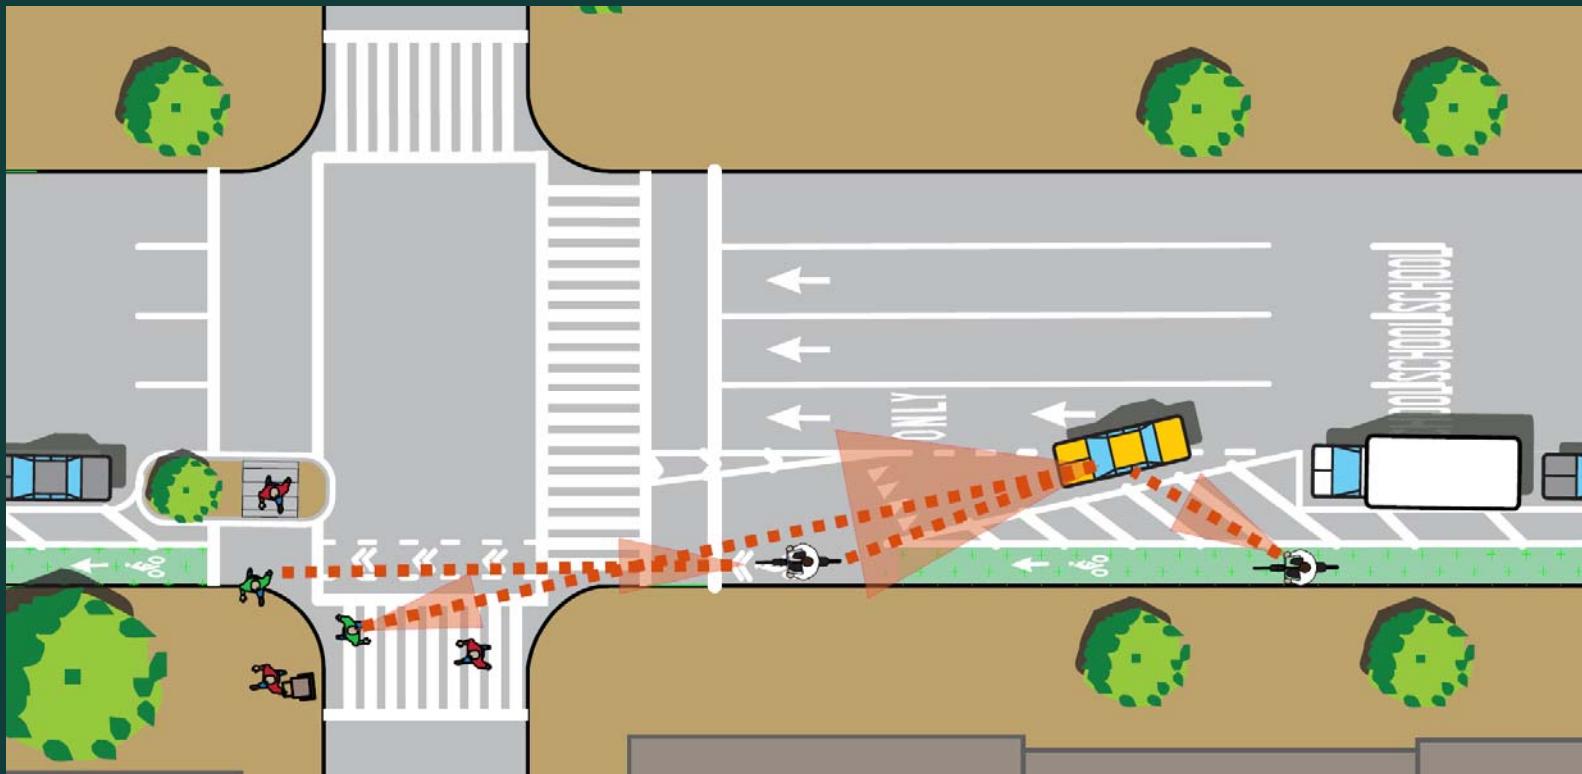


- **Mixing Zone Provides Space to Negotiate Conflict**
 - Informs cyclist that vehicle is turning, no guesswork
 - Removes vehicle from traffic stream/eliminates “back pressure”
 - Gentle approach angle, vehicle gradually approaches cyclist, no abrupt “hook” turns
- **Mixing Zone Provides Visibility**
 - Eliminates visual obstruction of parked cars
 - Angle improves drivers’ peripheral vision
 - Cyclist & Motorist can see each other and avoid crash




nyc.gov/dot

Thank
You

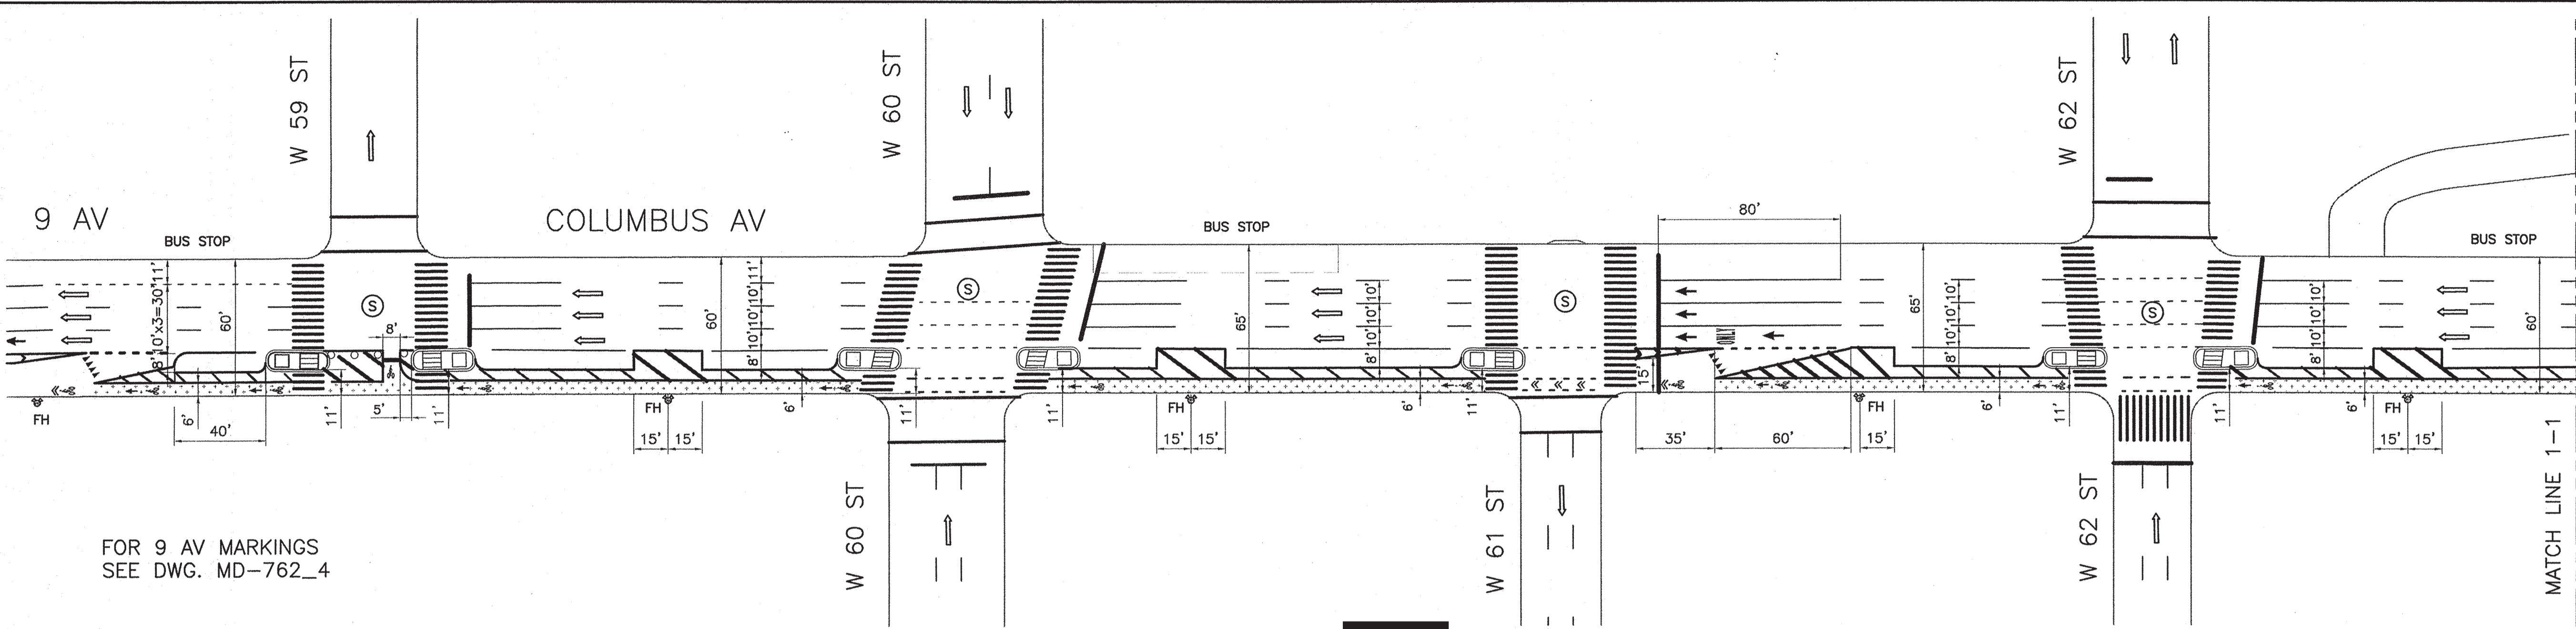

FOR 9 AV MARKINGS
SEE DWG. MD-762_4

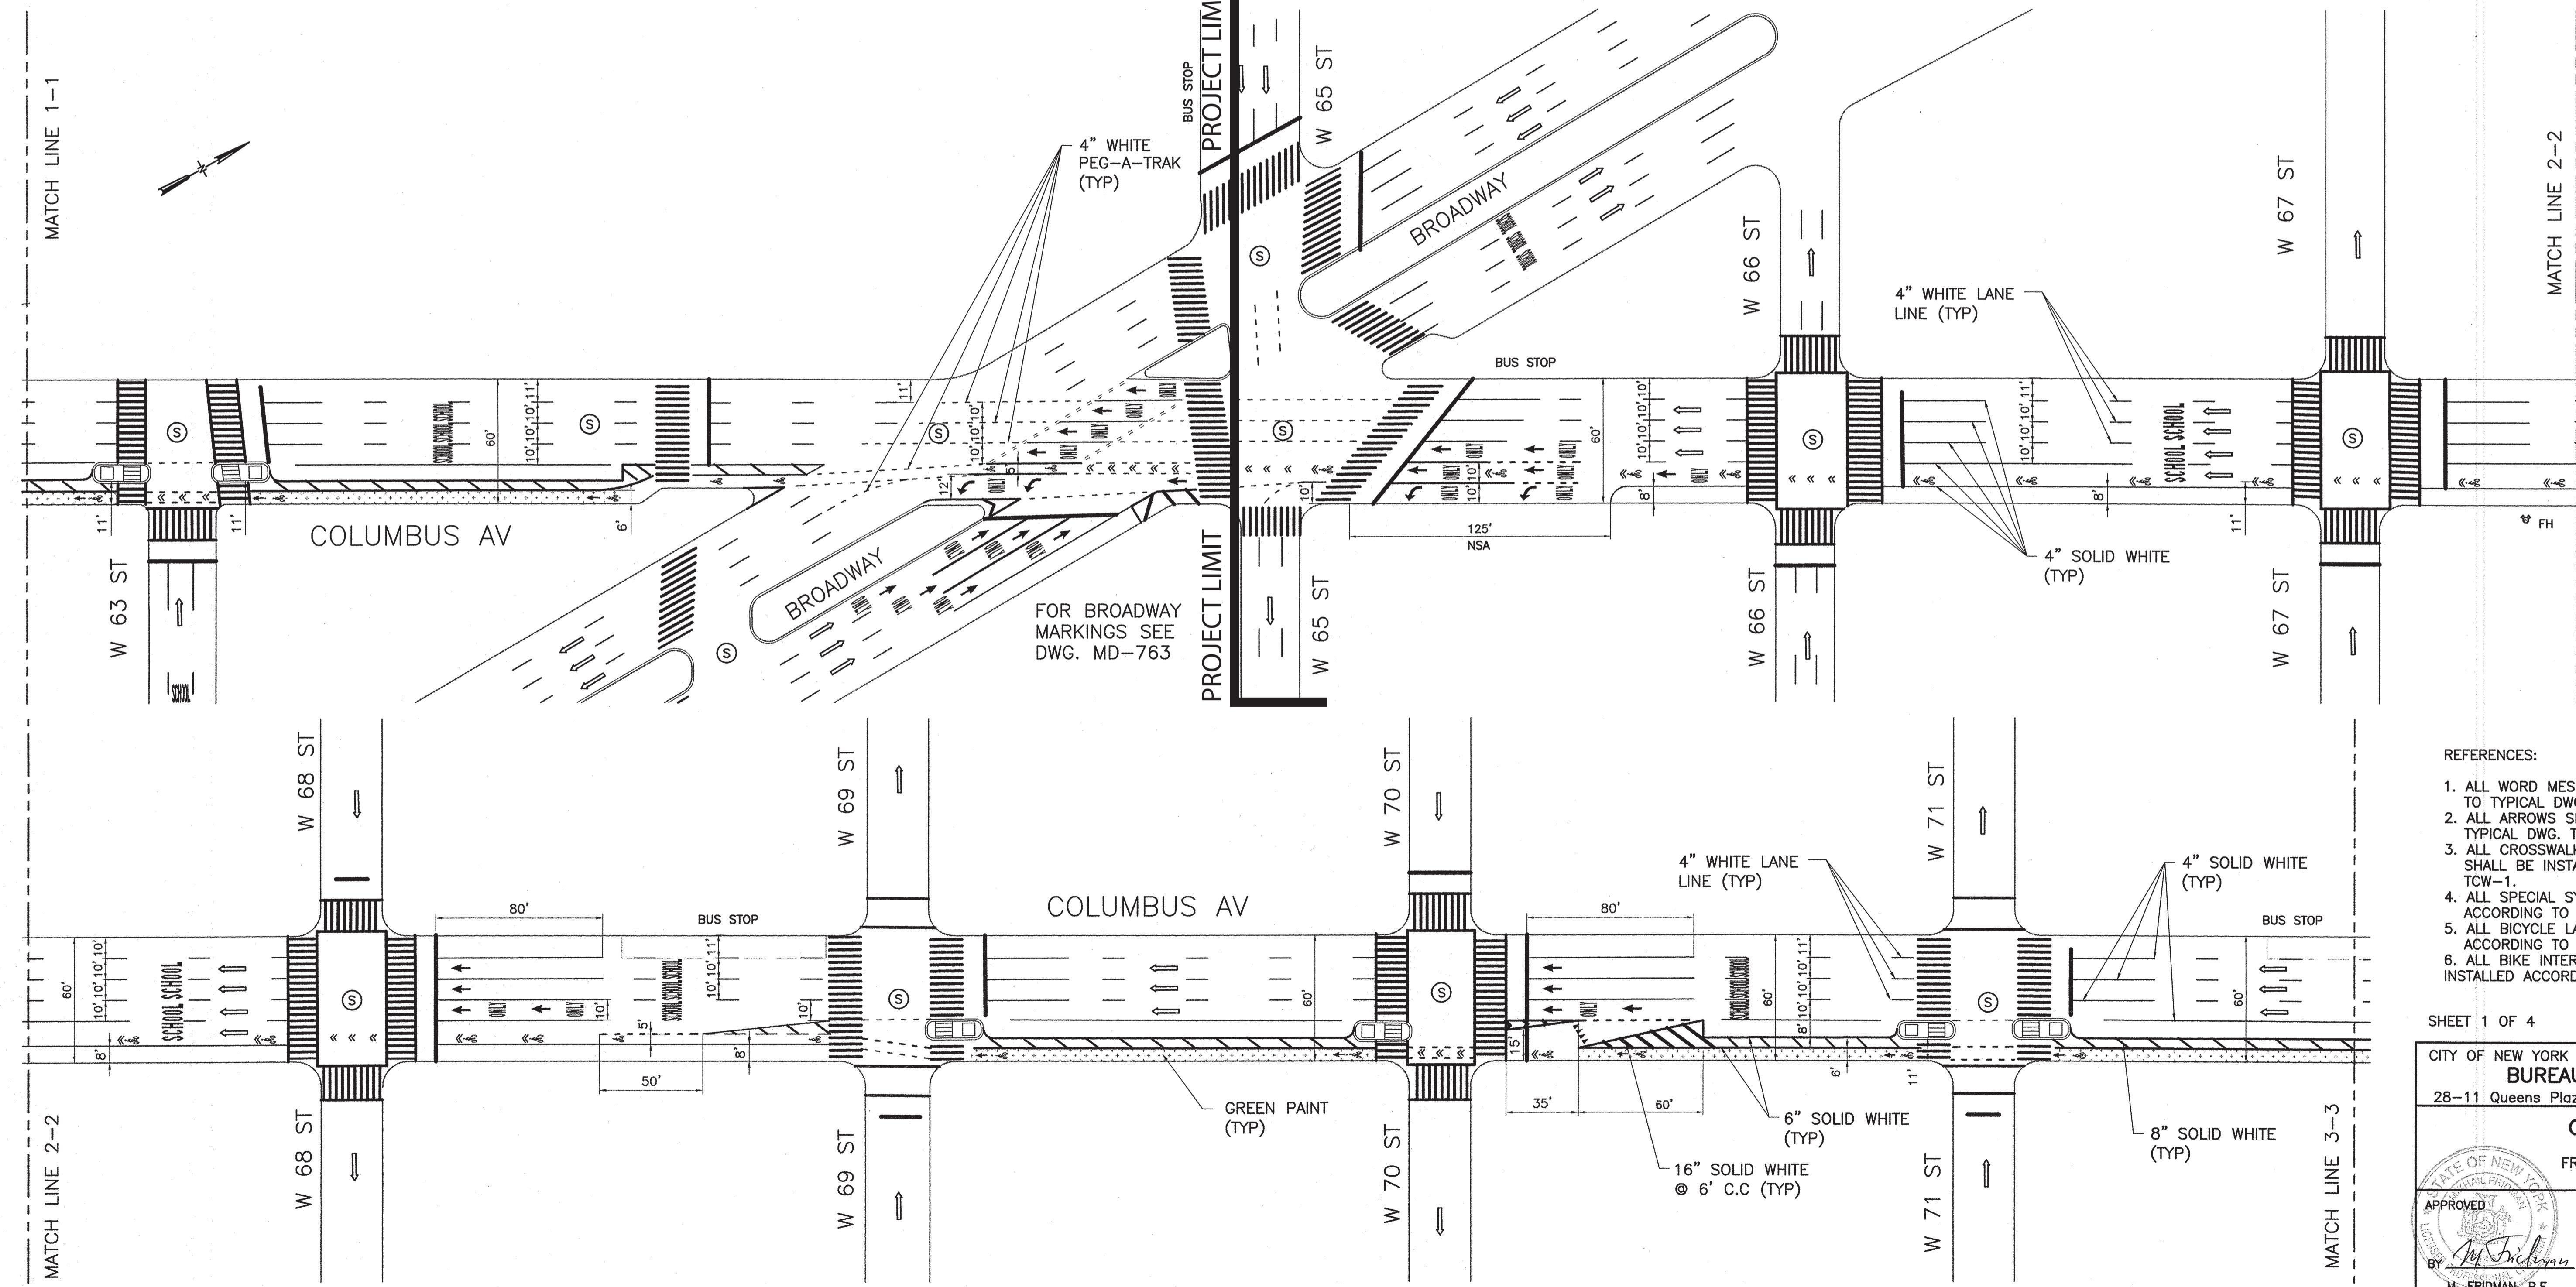

REPLACES DWG. MD-1136_1

REFERENCES:

- ALL WORD MESSAGES SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TWM-1.
 - ALL ARROWS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TAR-1.
 - ALL CROSSWALKS, STOP BARS AND LINEAR MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TCW-1.
 - ALL SPECIAL SYMBOL MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TSS-1.
 - ALL BICYCLE LANE MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TBB-1.
 - ALL BIKE INTERSECTIONS MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TRI-1

SHEET 1 OF 4

CITY OF NEW YORK DEPARTMENT OF TRANSPORTATION
BUREAU OF TRAFFIC OPERATIONS


COLUMBUS AVENUE

COLUMBUS AVENUE


FROM W 59 ST TO W 71 ST	
 APPROVED  BY M. FRIDMAN, P.E.	
Drawn by	M. FRIDMAN
Checked by	J. AHSAN
Borough	MANHATTAN
Scale	1"=40'
Date	05/01/2013
DRAWING NO. MD-1136_1R	

REVISIONS		
DATE	APPD	DESCRIPTION

REPLACES DWG. MD-1136_2

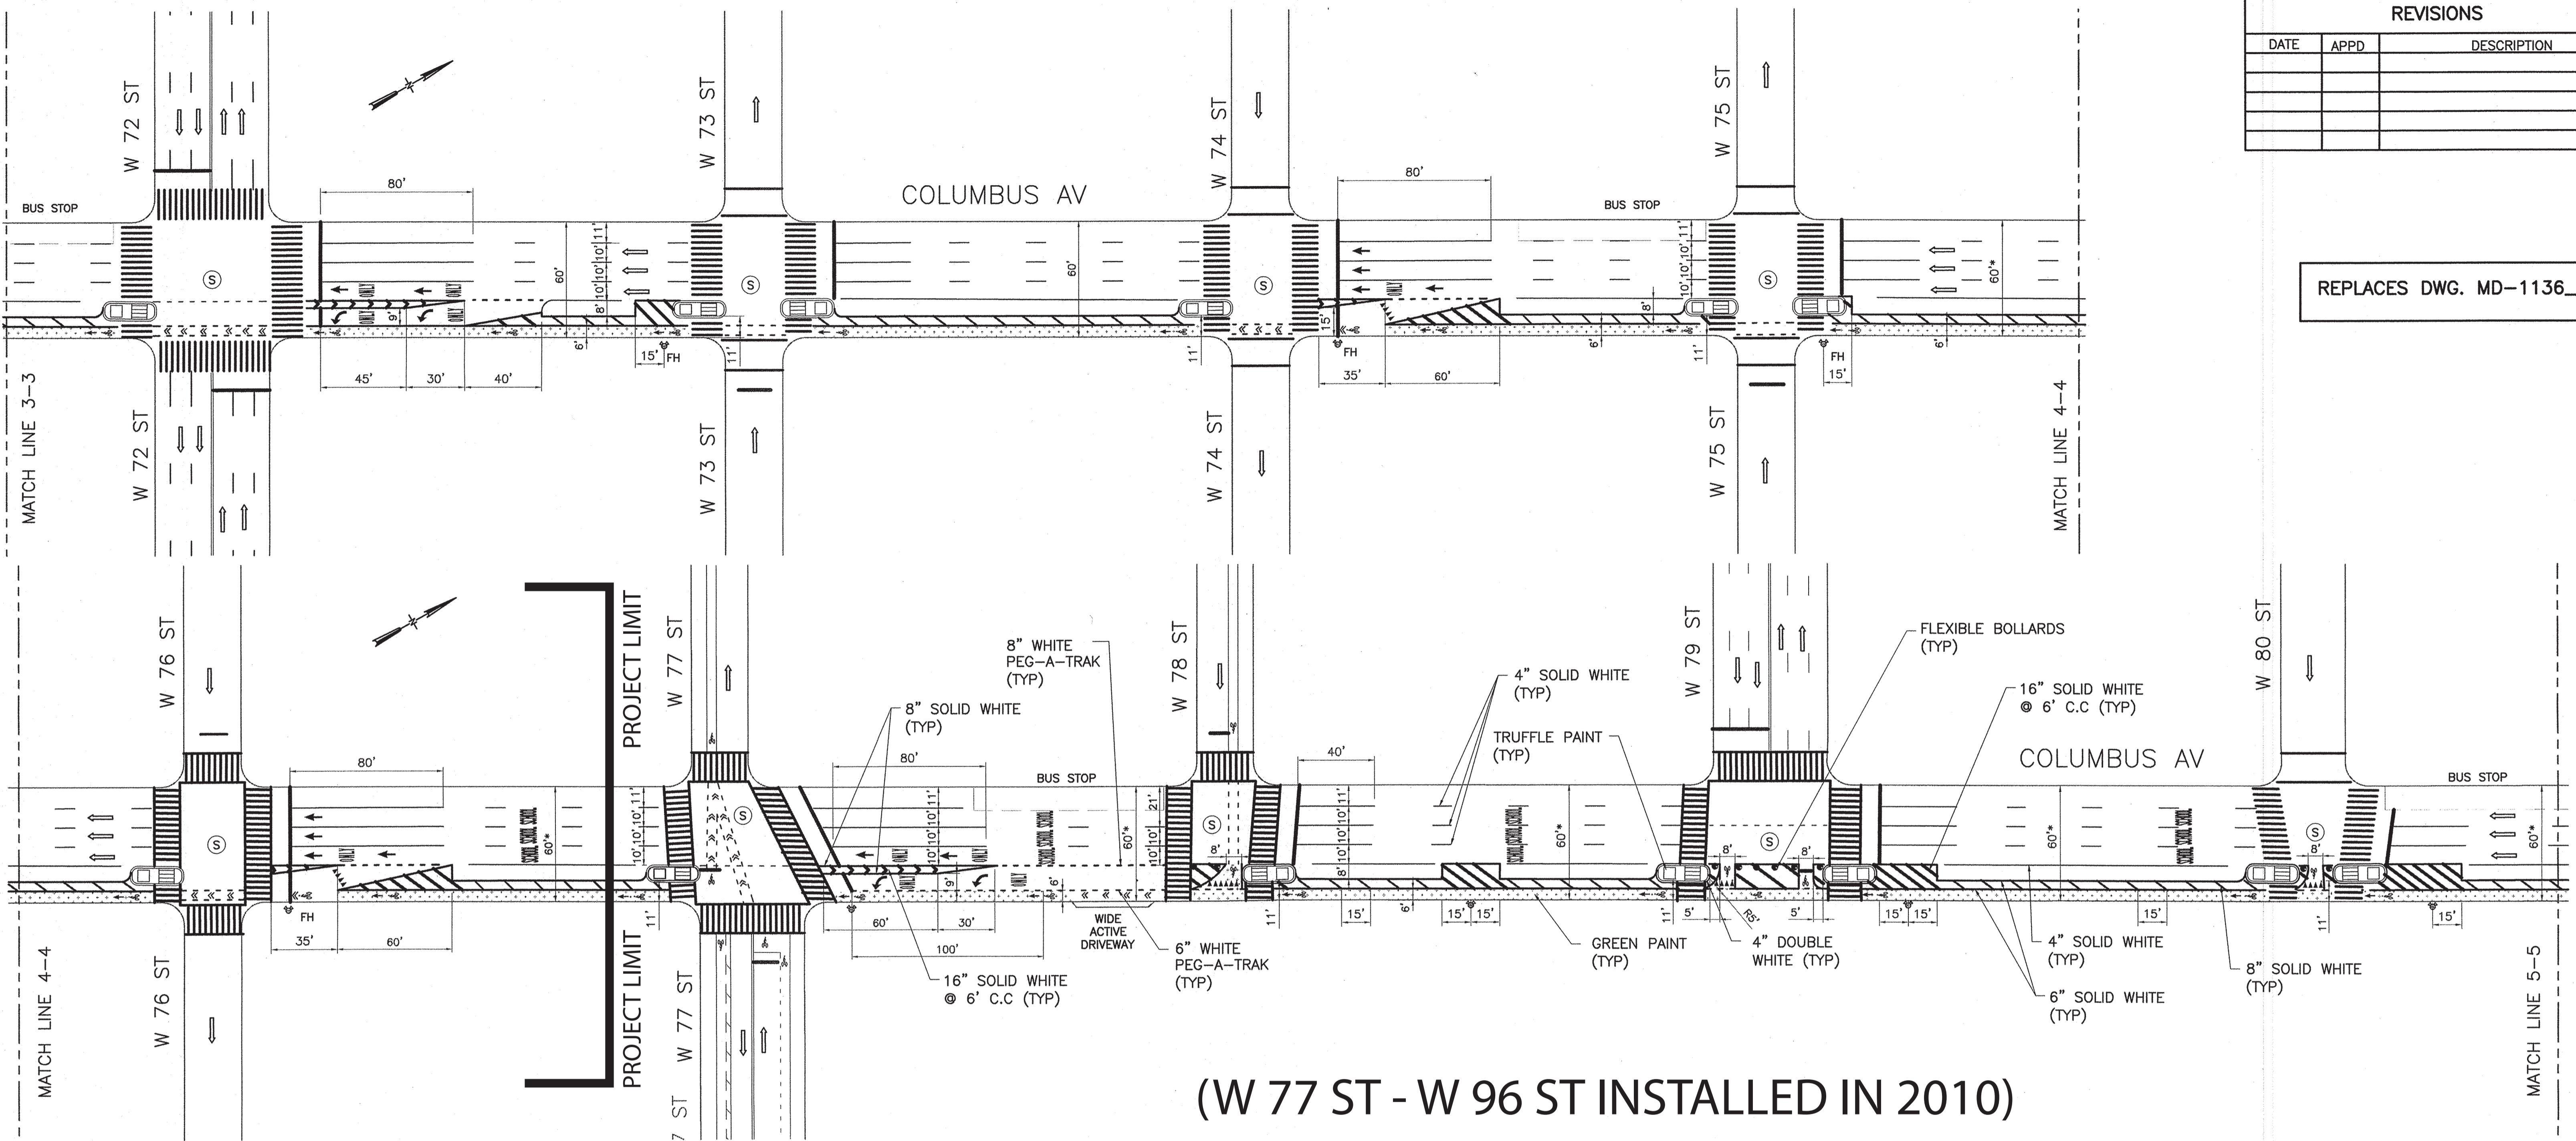

(W 77 ST - W 96 ST INSTALLED IN 2010)

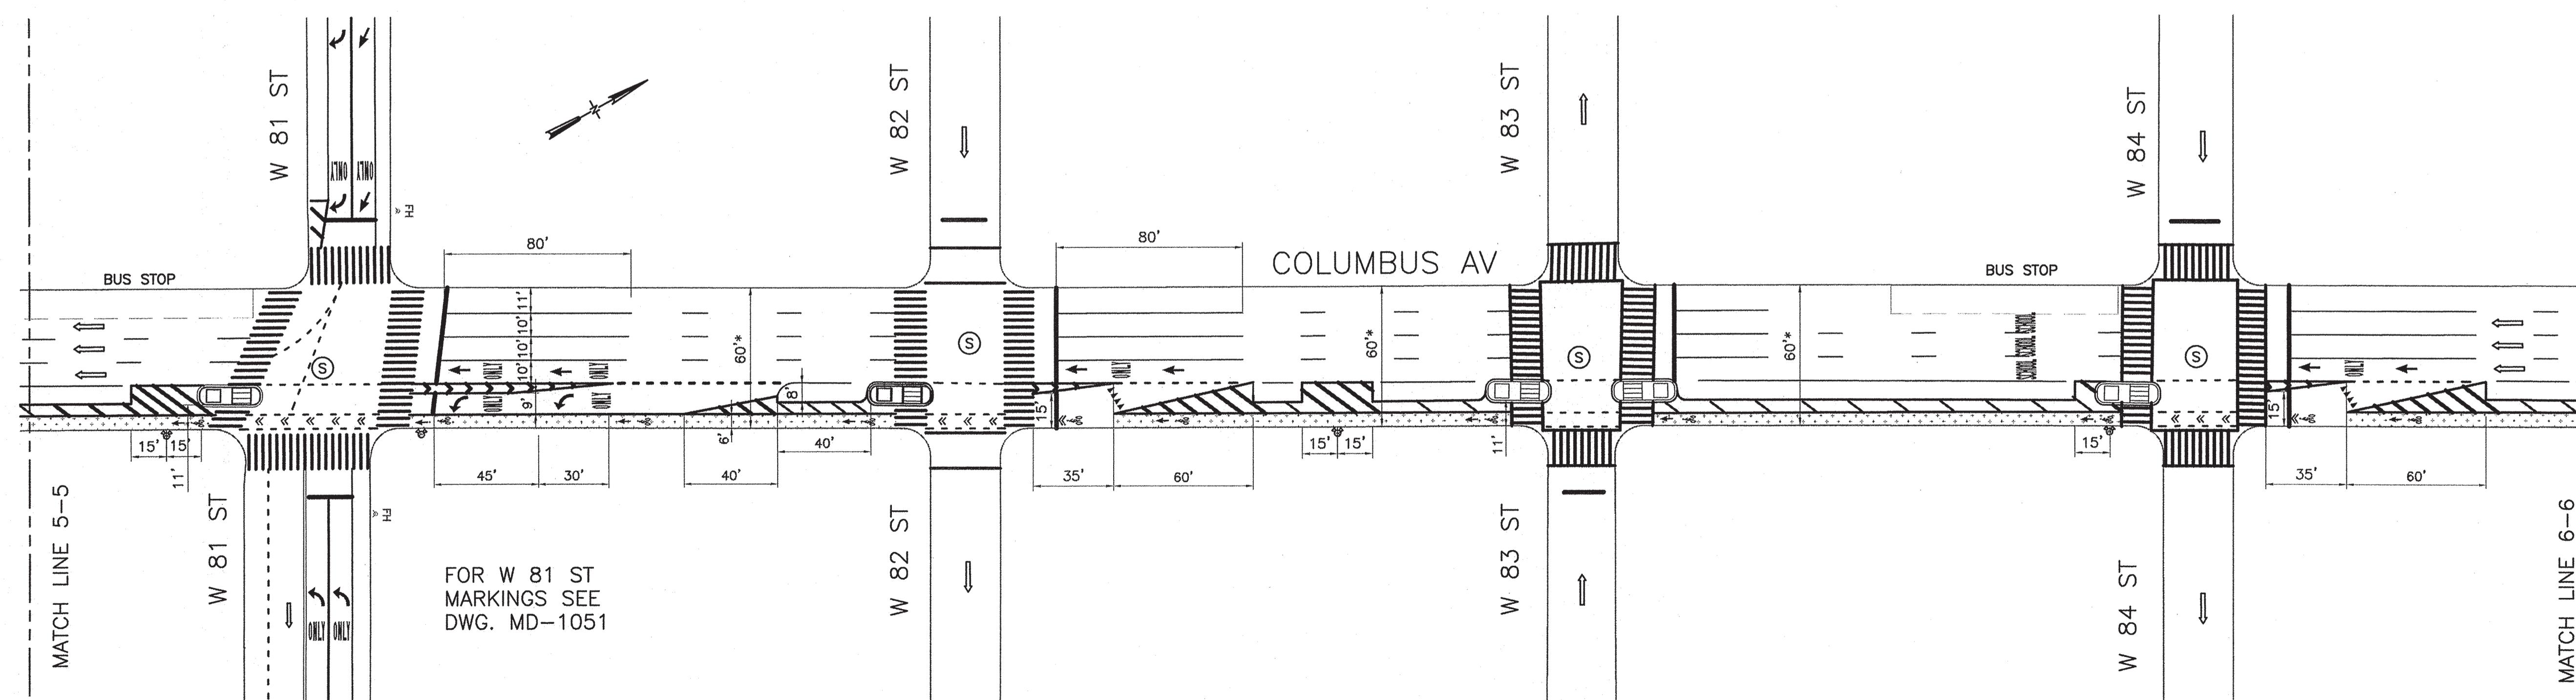

REFERENCES:

1. ALL WORD MESSAGES SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TWM-1.
2. ALL ARROWS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TAR-1.
3. ALL CROSSWALKS, STOP BARS AND LINEAR MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TCW-1.
4. ALL SPECIAL SYMBOL MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TSS-1.
5. ALL BIKE LANE MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TBB-1.
6. ALL BIKE INTERSECTIONS MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TBI-1.


SHEET 2 OF 4

CITY OF NEW YORK		DEPARTMENT OF TRANSPORTATION
BUREAU OF TRAFFIC OPERATIONS		
28-11 Queens Plaza North		L.I.C., N.Y. 11101
COLUMBUS AVENUE		
FROM W 71 ST TO W 84 ST		
 APPROVED BY <i>M. Fridman</i>		Drawn by <i>M. FRIDMAN</i> Checked by <i>J. AHsan</i> Borough <i>MANHATTAN</i> Scale <i>1"=40'</i> Date <i>05/01/2013</i>
DRAWING NO. <i>MD-1136_2R</i>		

REVISIONS

DATE	APPD	DESCRIPTION
05/01/13	MF	MIXING ZONES UPDATED TO NEW

(W 77 ST - W 96 ST INSTALLED IN 2010)

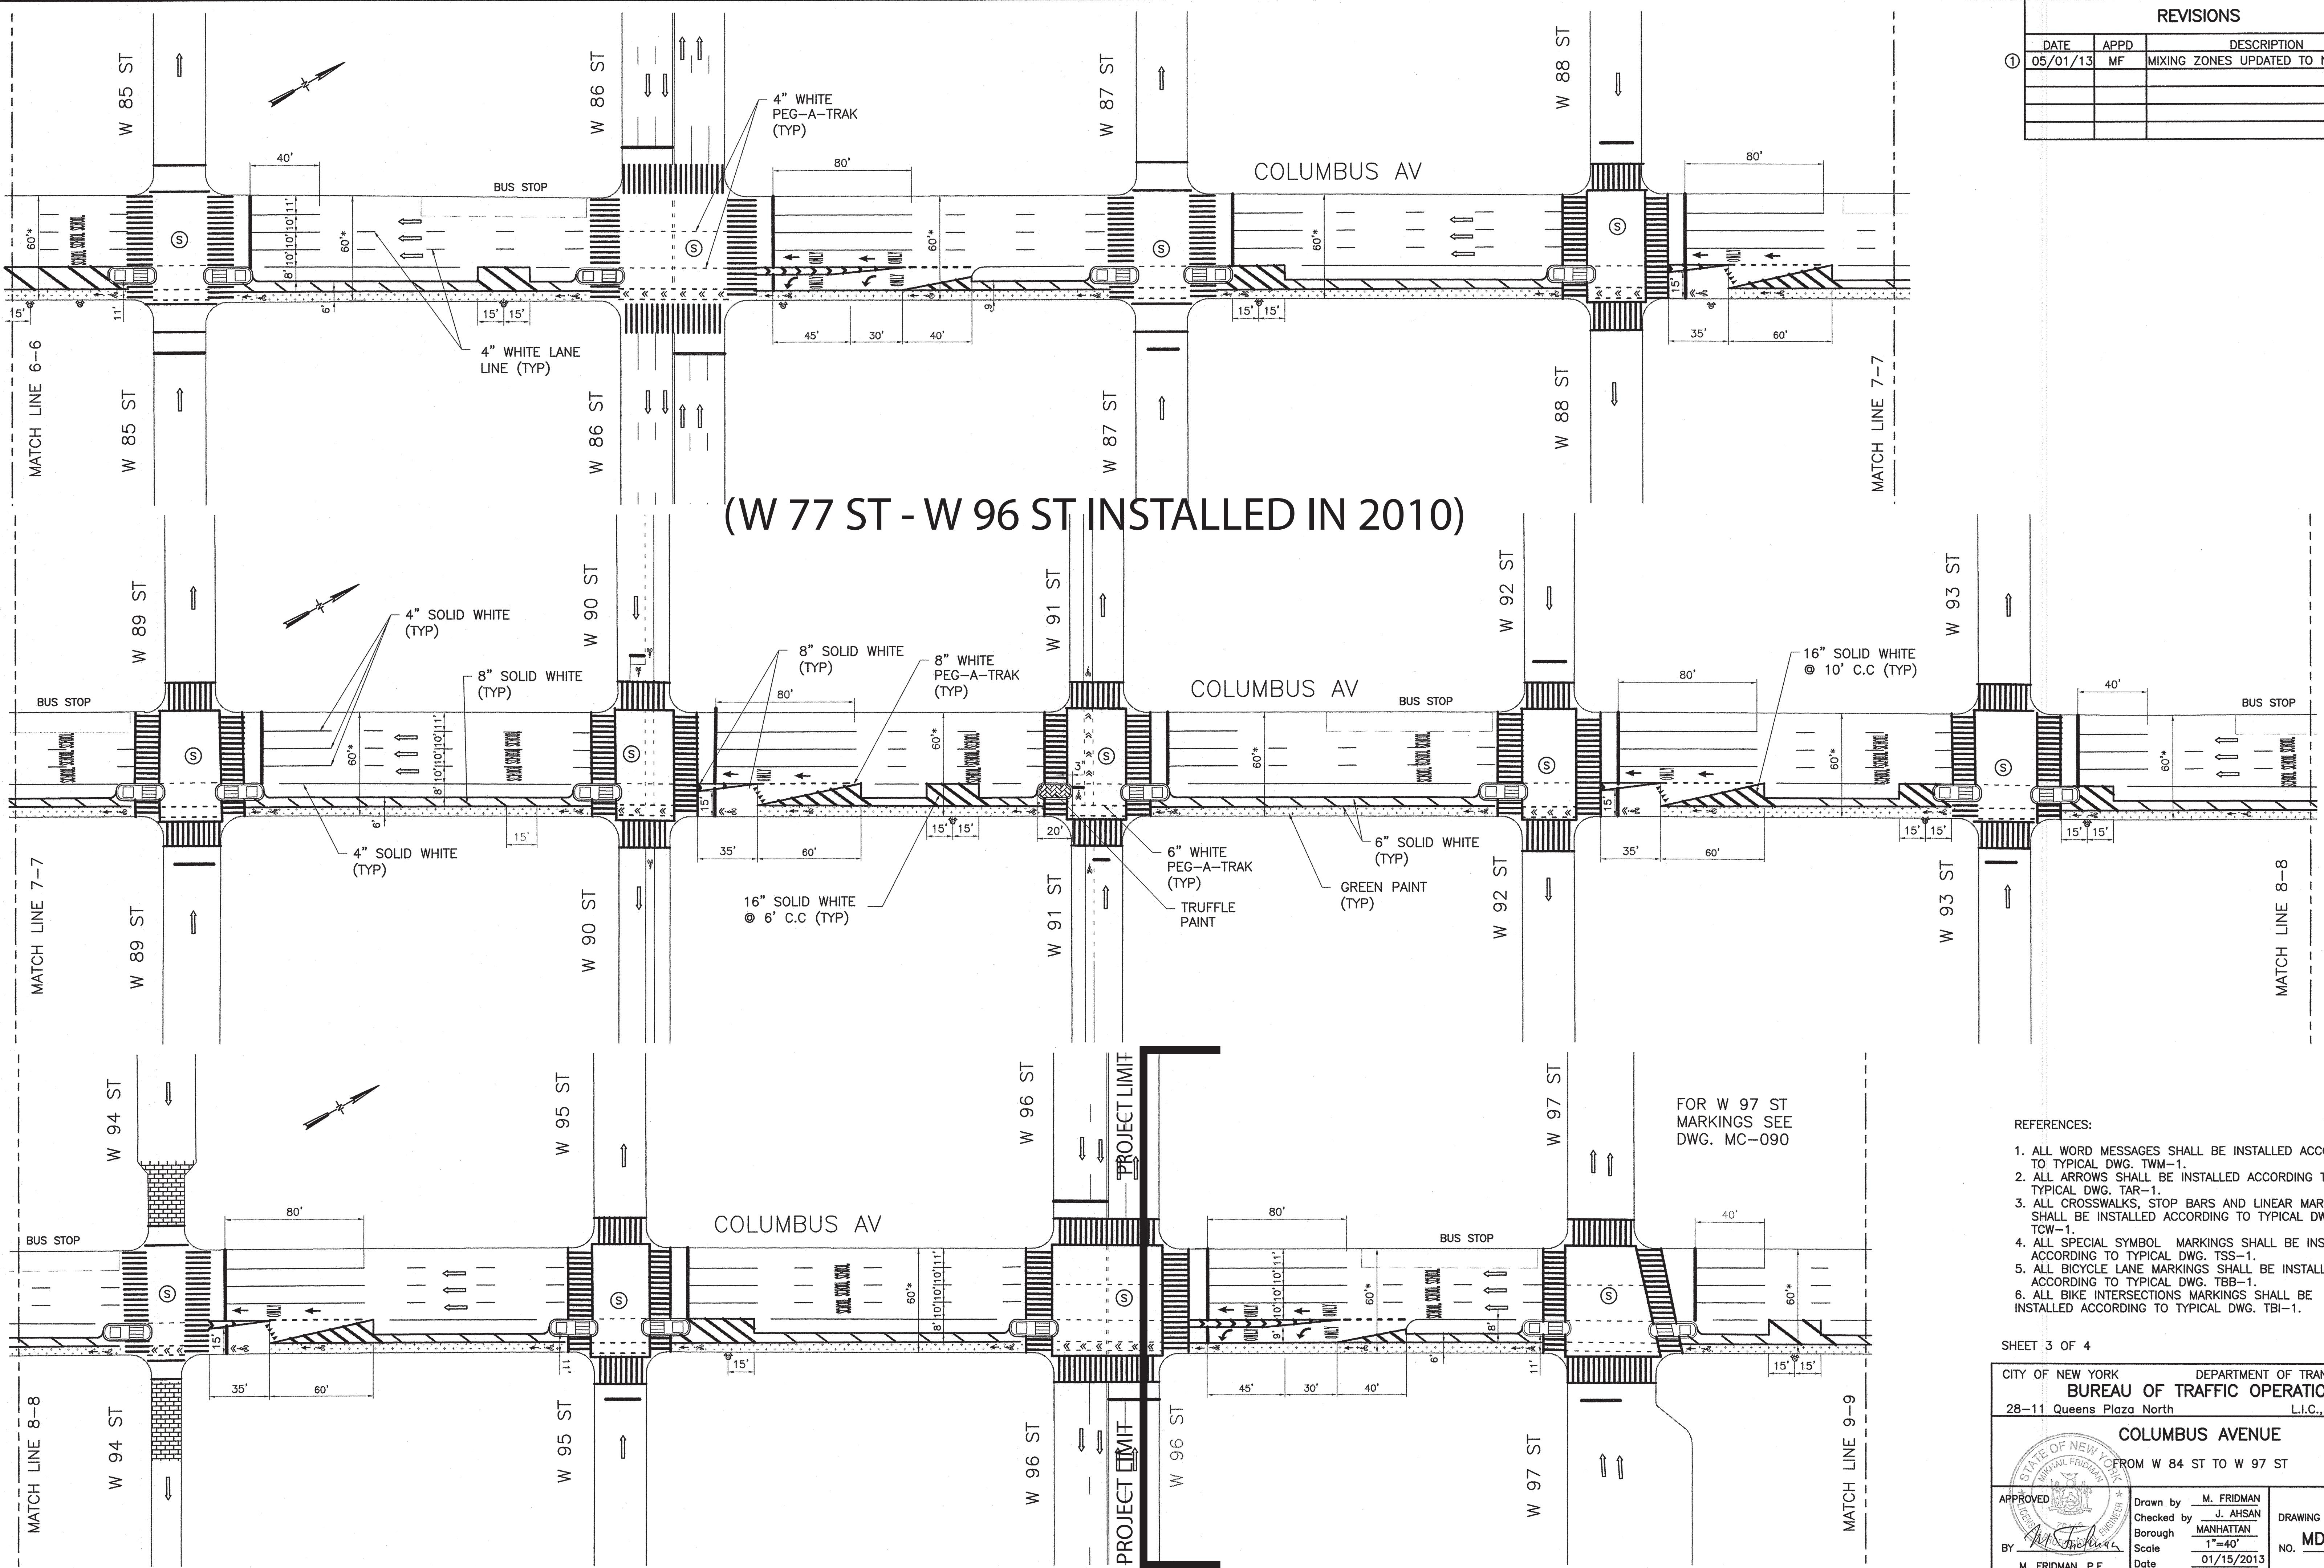

REFERENCES:

1. ALL WORD MESSAGES SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TWM-1.
2. ALL ARROWS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TAR-1.
3. ALL CROSSWALKS, STOP BARS AND LINEAR MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TCW-1.
4. ALL SPECIAL SYMBOL MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TSS-1.
5. ALL BIKE LANE MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TBB-1.
6. ALL BIKE INTERSECTIONS MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TBI-1.

SHEET 3 OF 4

CITY OF NEW YORK DEPARTMENT OF TRANSPORTATION
BUREAU OF TRAFFIC OPERATIONS
28-11 Queens Plaza North L.I.C., N.Y. 11101

COLUMBUS AVENUE

FROM W 84 ST TO W 97 ST




APPROVED BY 	Drawn by M. FRIDMAN
Checked by J. AHsan	Borough MANHATTAN
Scale 1"=40'	Date 01/15/2013
DRAWING NO. MD-1136_3	

AREA WITHIN THE FLOATING PARKING IN FRONT OF EACH FIRE HYDRANT SHALL BE HATCHED 15' TO BOTH SIDES

REVISIONS

DATE	APPD	DESCRIPTION

REPLACES DWG. MD-1136_4

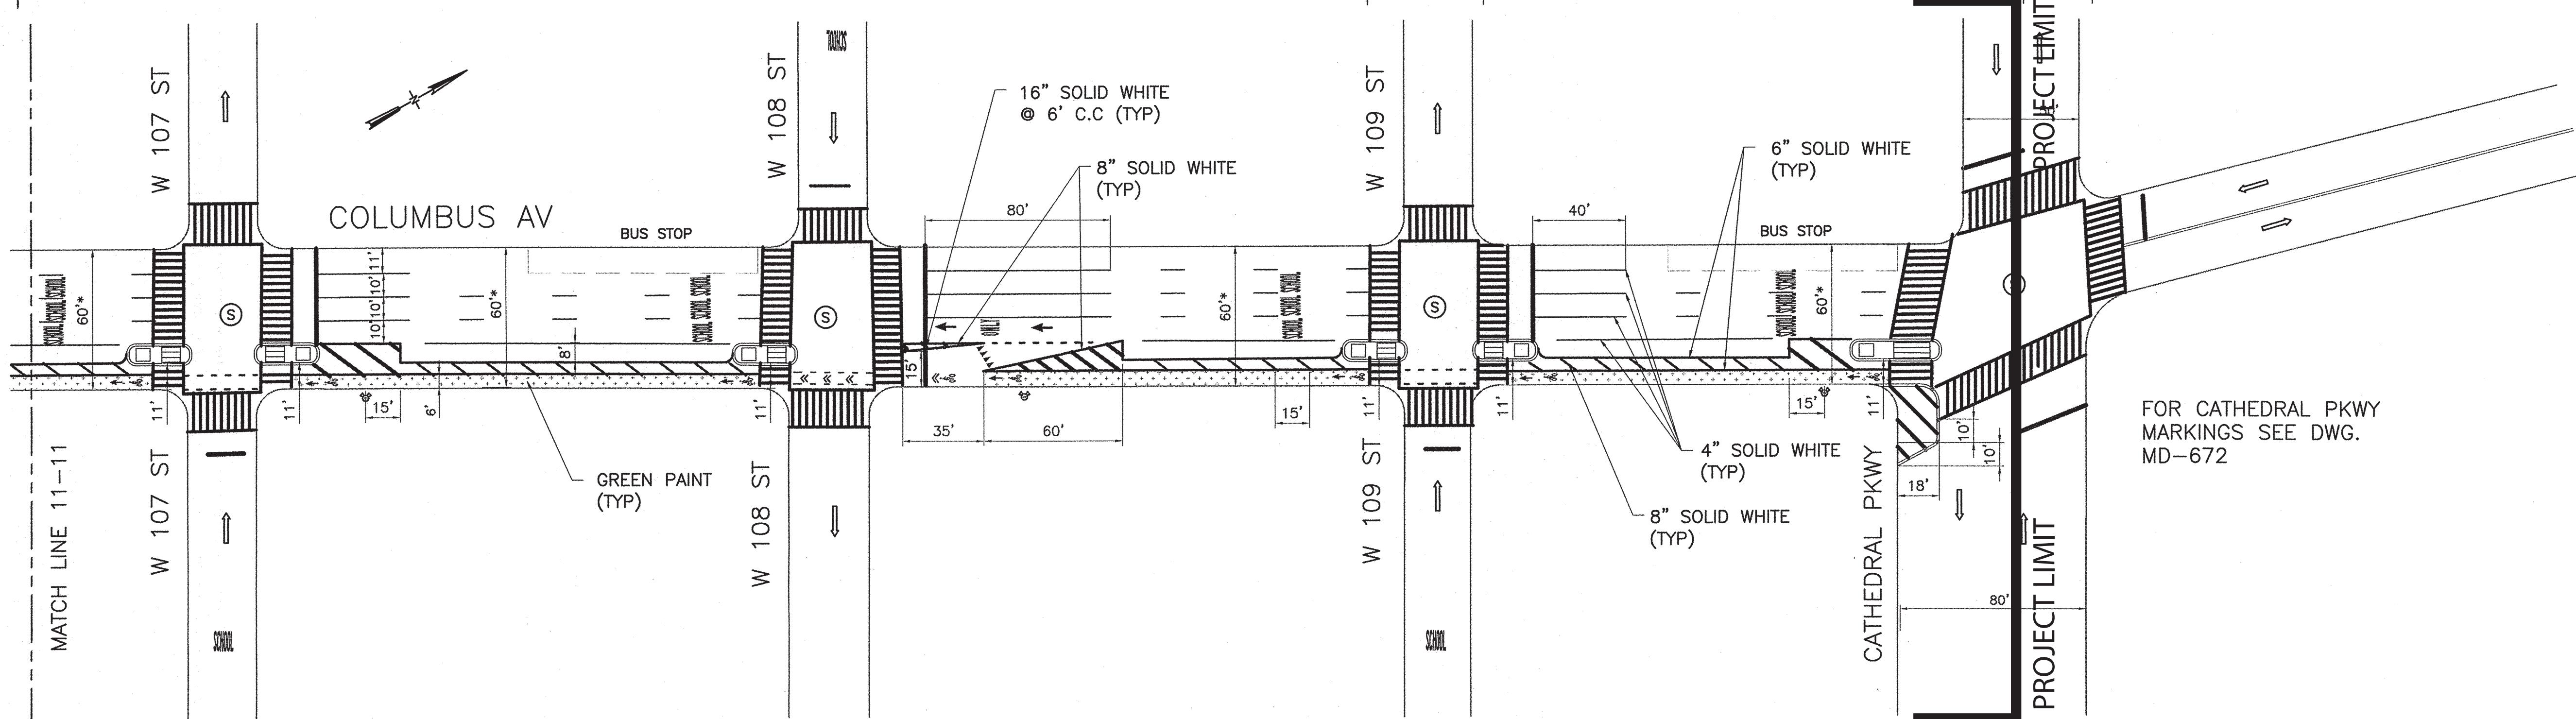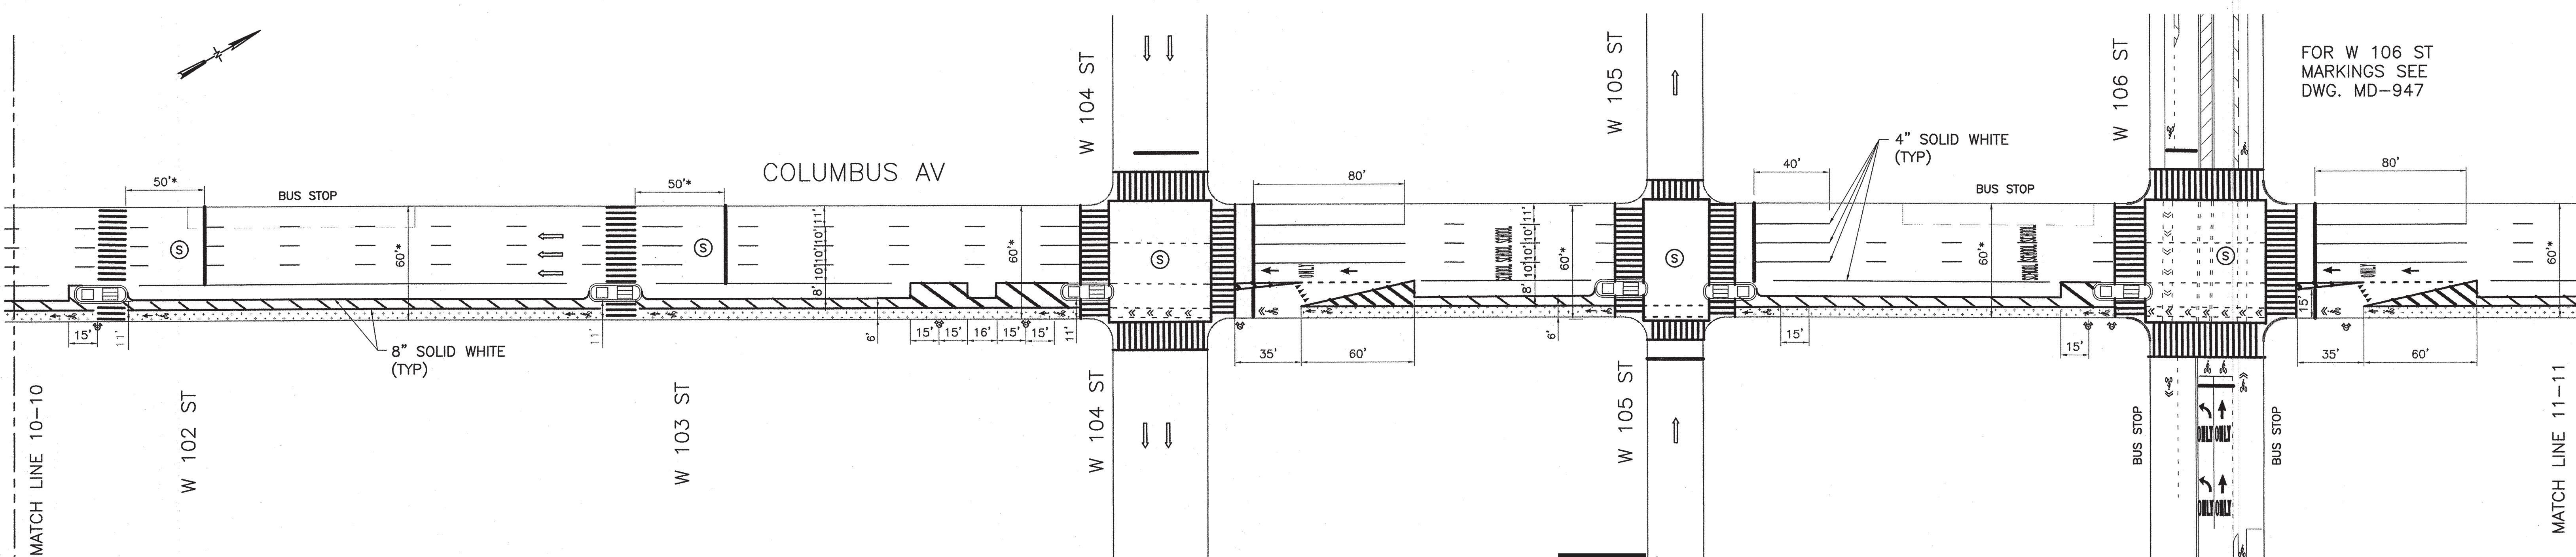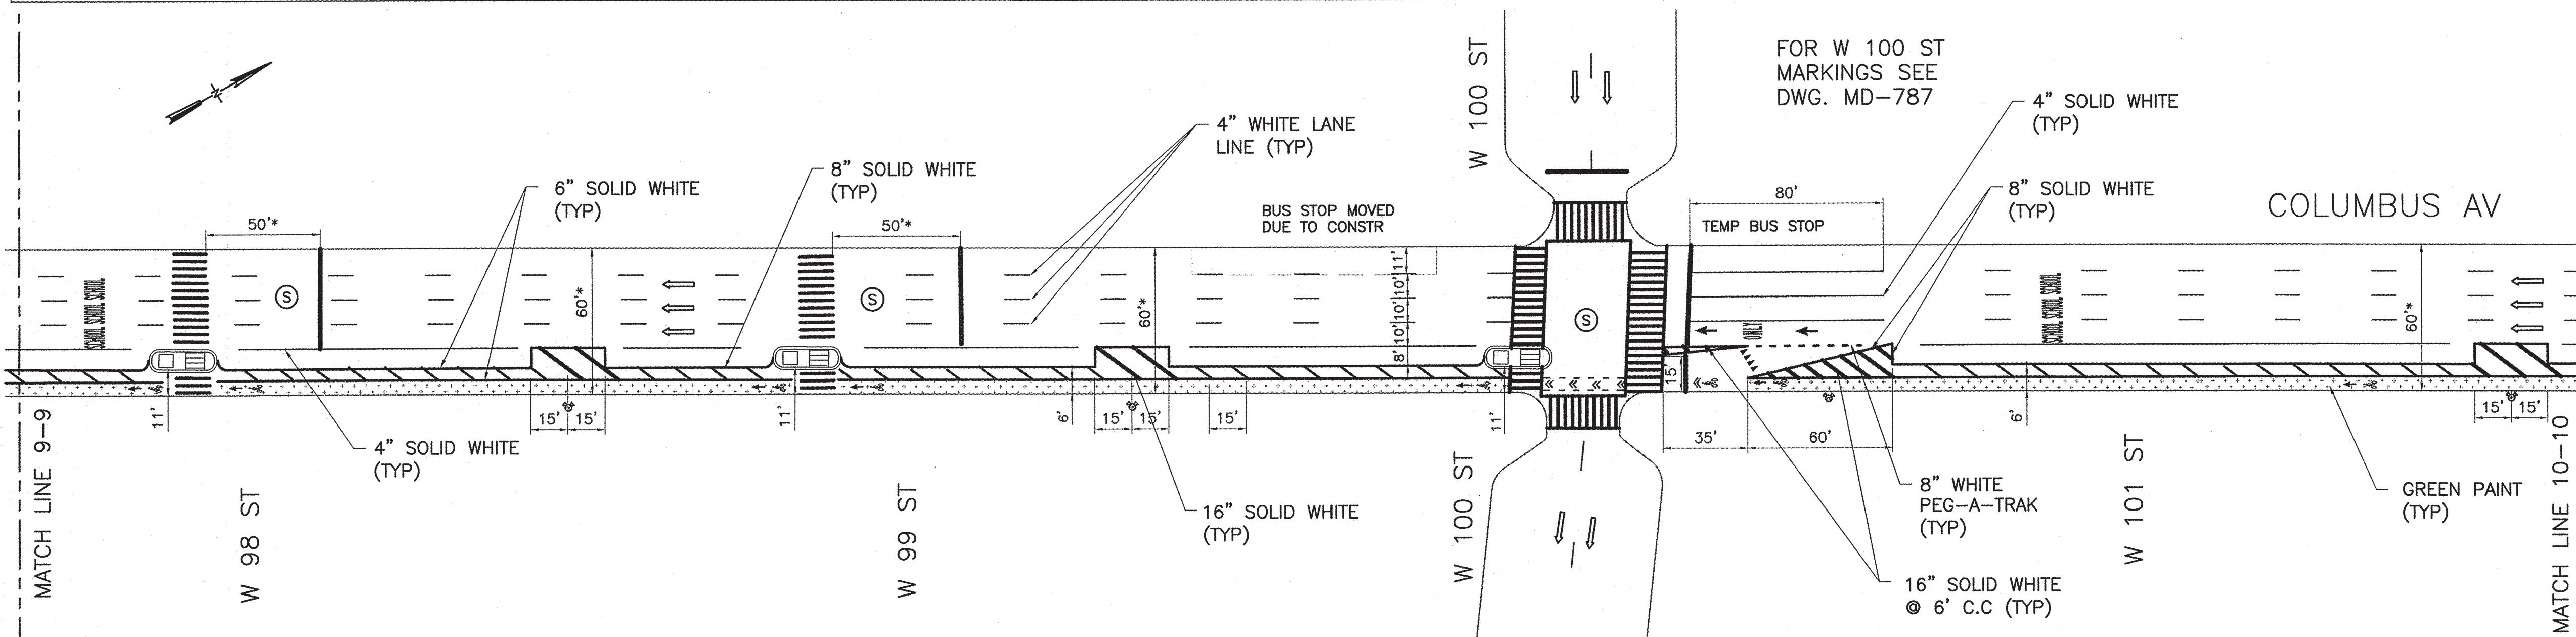

REFERENCES:

1. ALL WORD MESSAGES SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TWM-1.
2. ALL ARROWS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TAR-1.
3. ALL CROSSWALKS, STOP BARS AND LINEAR MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TCW-1.
4. ALL SPECIAL SYMBOL MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TSS-1.
5. ALL BIKE LANE MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TBB-1.
6. ALL BIKE INTERSECTIONS MARKINGS SHALL BE INSTALLED ACCORDING TO TYPICAL DWG. TBI-1.


SHEET 4 OF 4

CITY OF NEW YORK DEPARTMENT OF TRANSPORTATION
BUREAU OF TRAFFIC OPERATIONS
28-11 Queens Plaza North L.I.C., N.Y. 11101

COLUMBUS AVENUE


FROM W 97 ST TO CATHEDRAL PKWY

APPROVED BY M. FRIDMAN, P.E.	Drawn by J. AHsan Borough Scale Date	Checked by M. FRIDMAN MANHATTAN 1"=40' 05/01/2013	DRAWING NO. MD-1136_4R
--	--	---	---------------------------

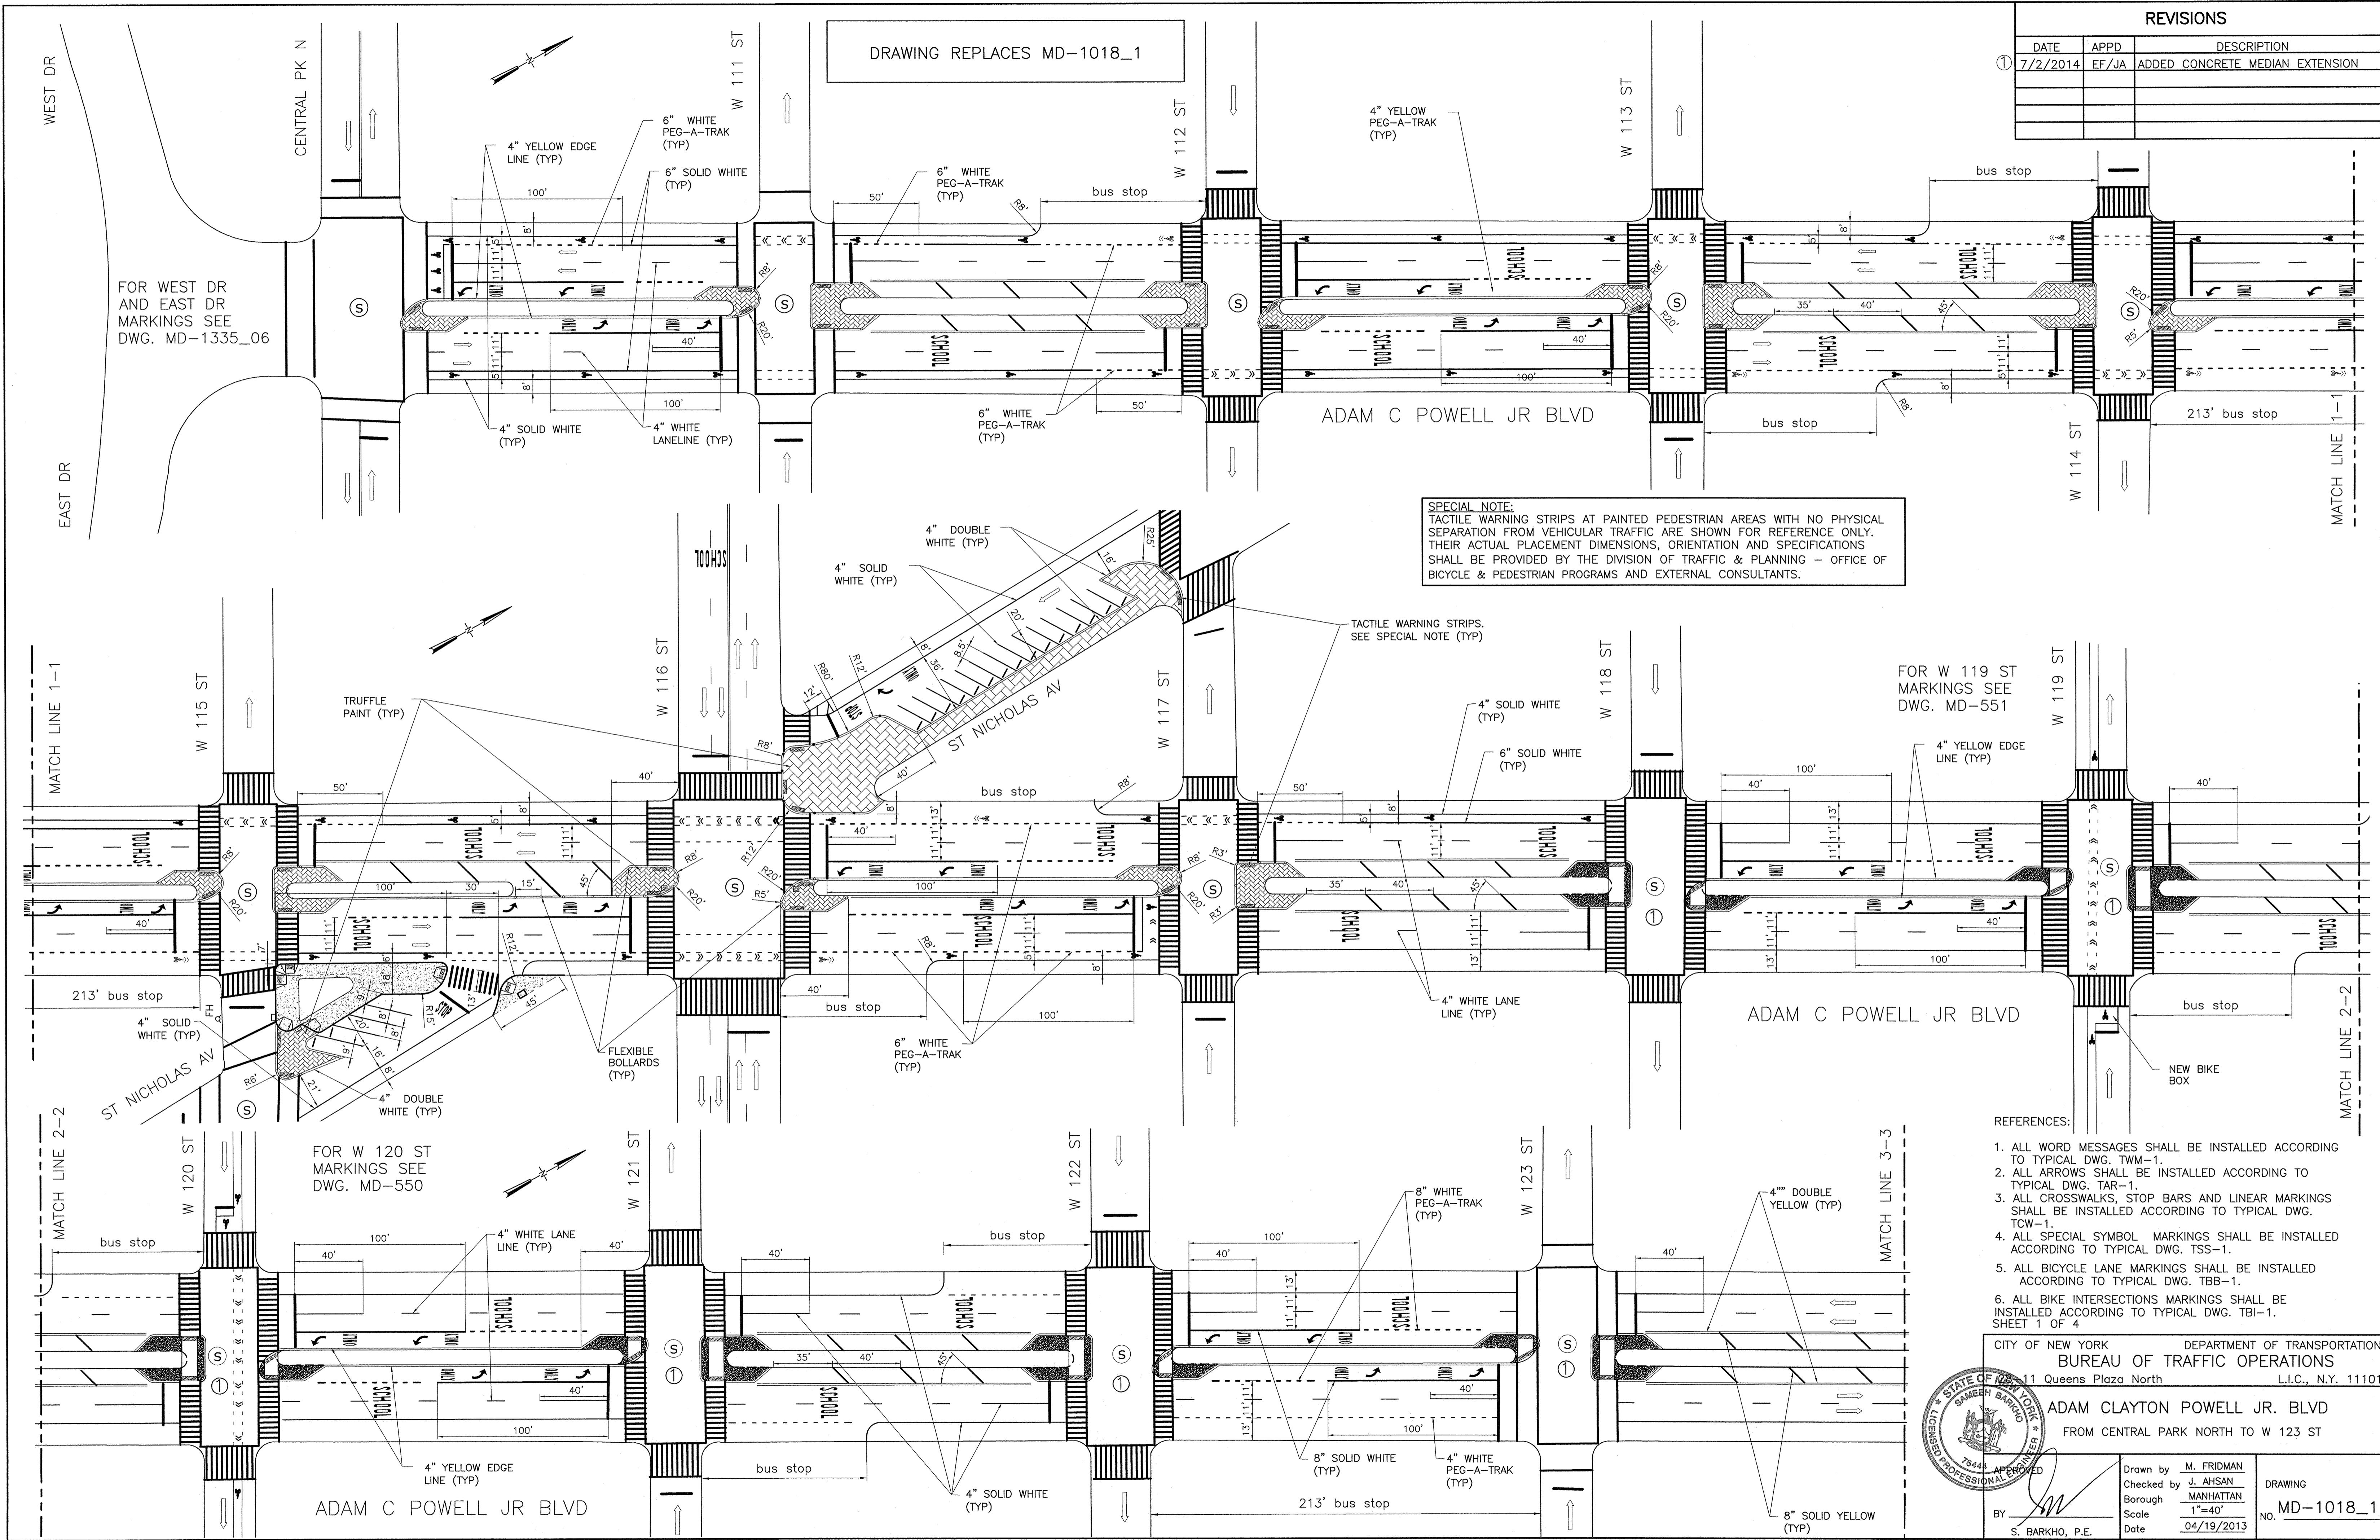

Columbus Avenue Parking-Protected Bicycle Path




West 96th to West 77th Streets

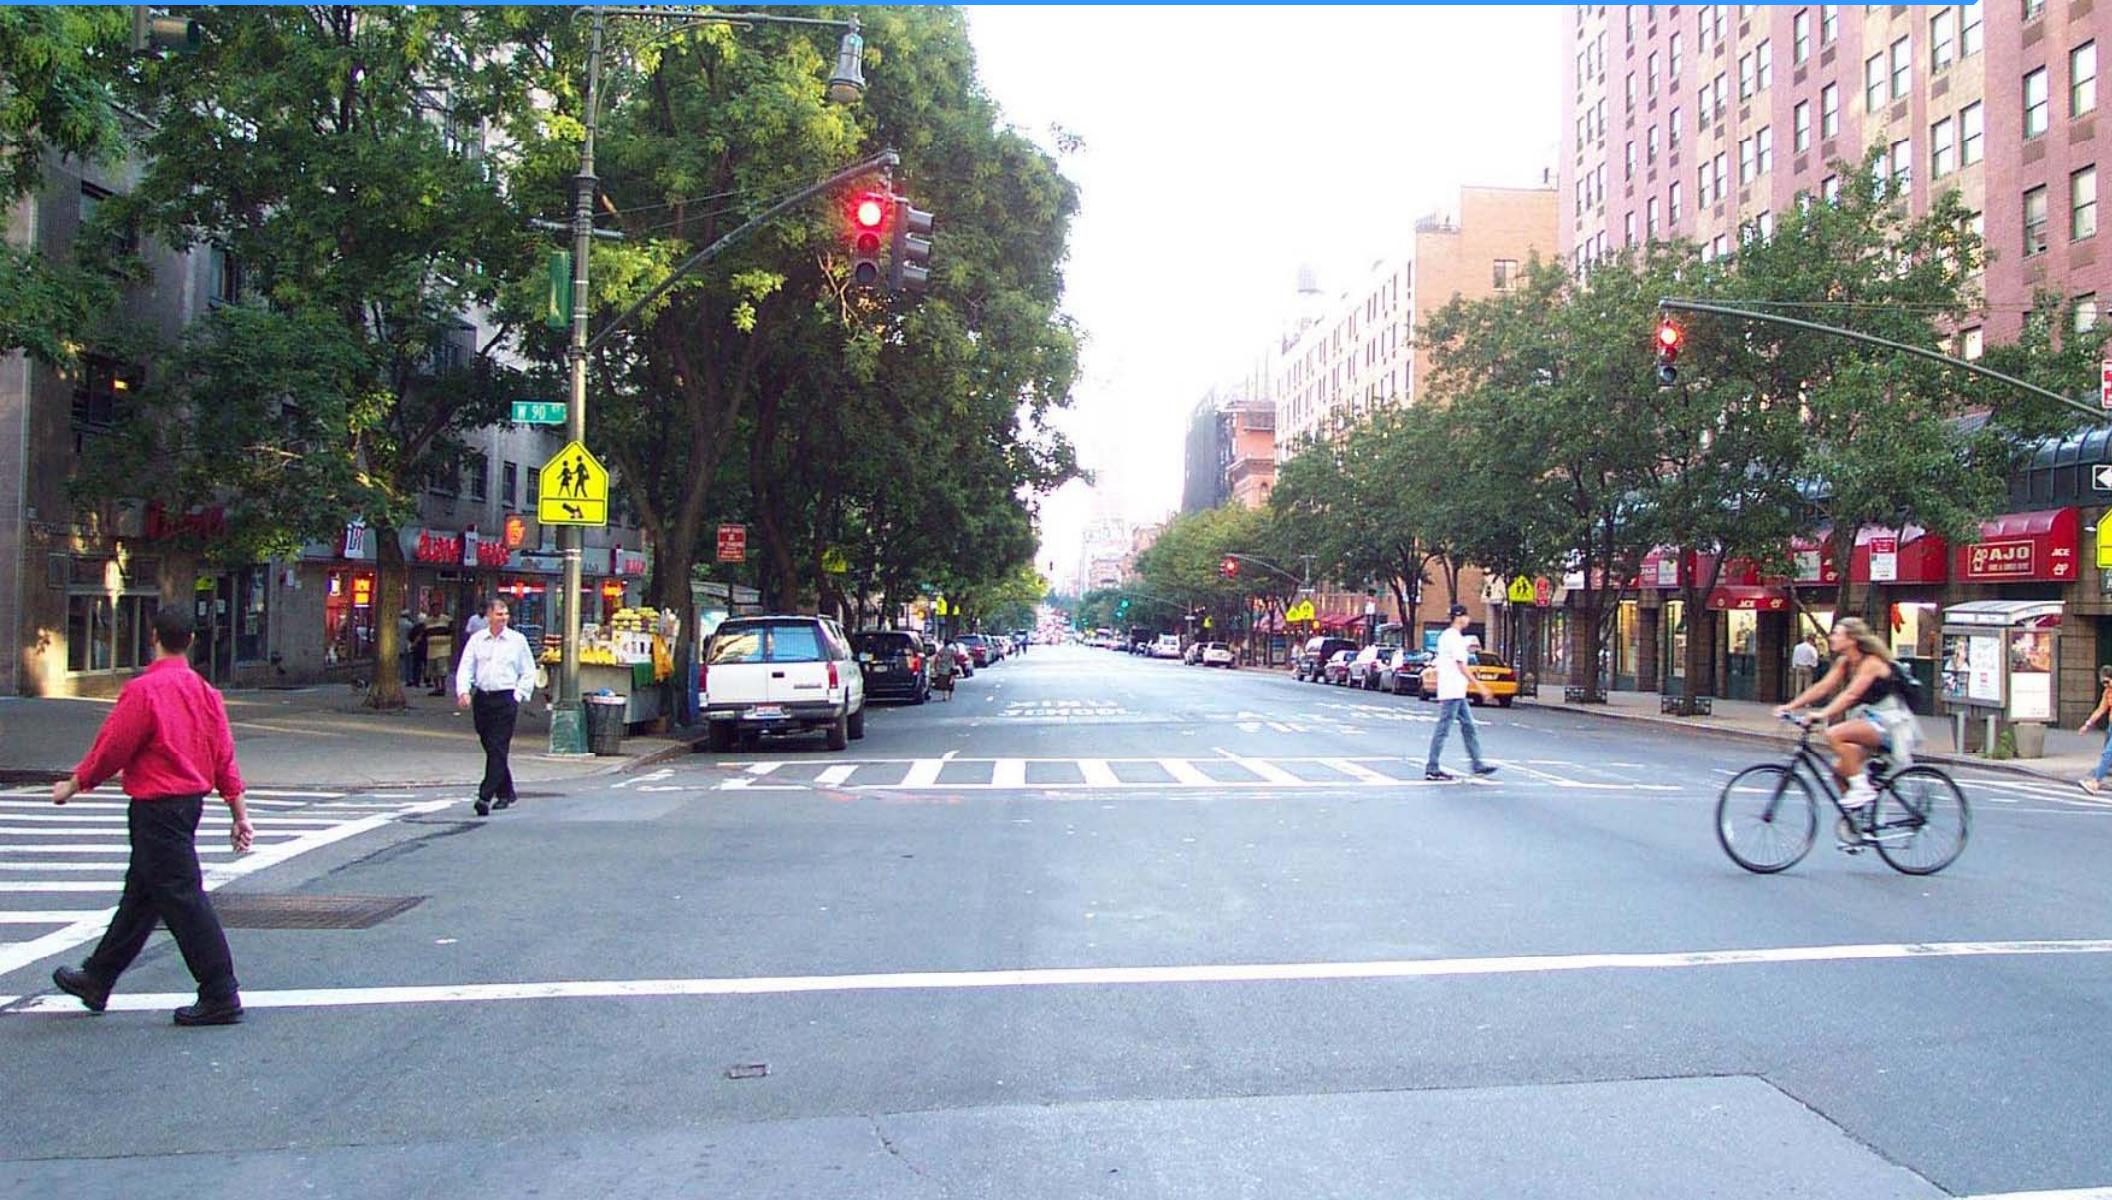

Commissioner Janette Sadik-Khan New York City Department of Transportation
Presented May 11, 2010 to Community Board 7




NYC Cycling Background

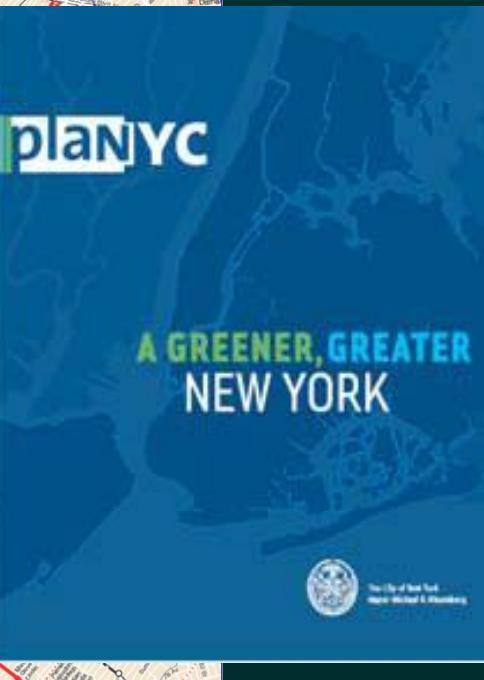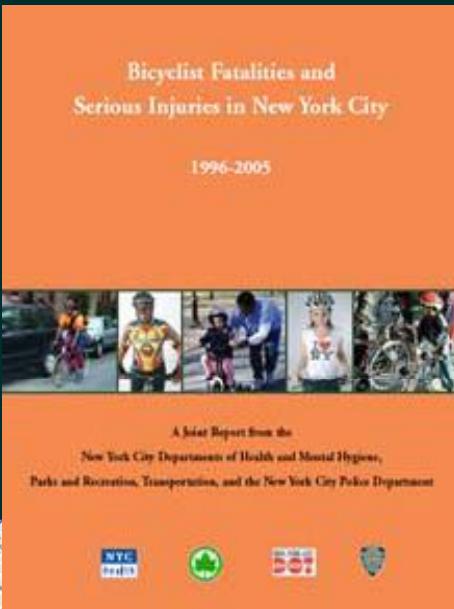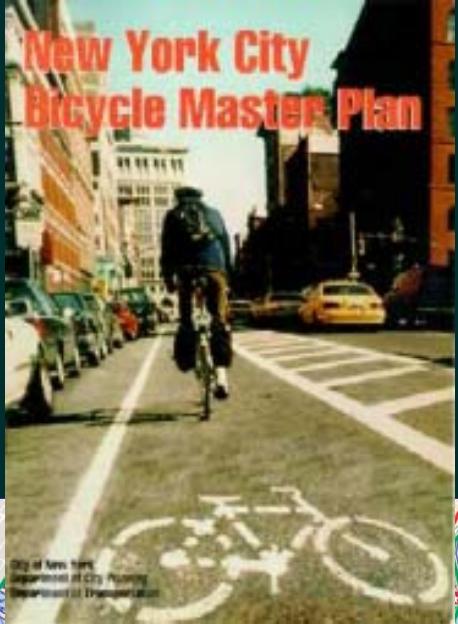

- 200 miles of bike routes installed in last 3 years
- 79% increase in commuter cycling (2006-2009)
- 5 lane miles of on-street protected bicycle paths

Ridership Rates

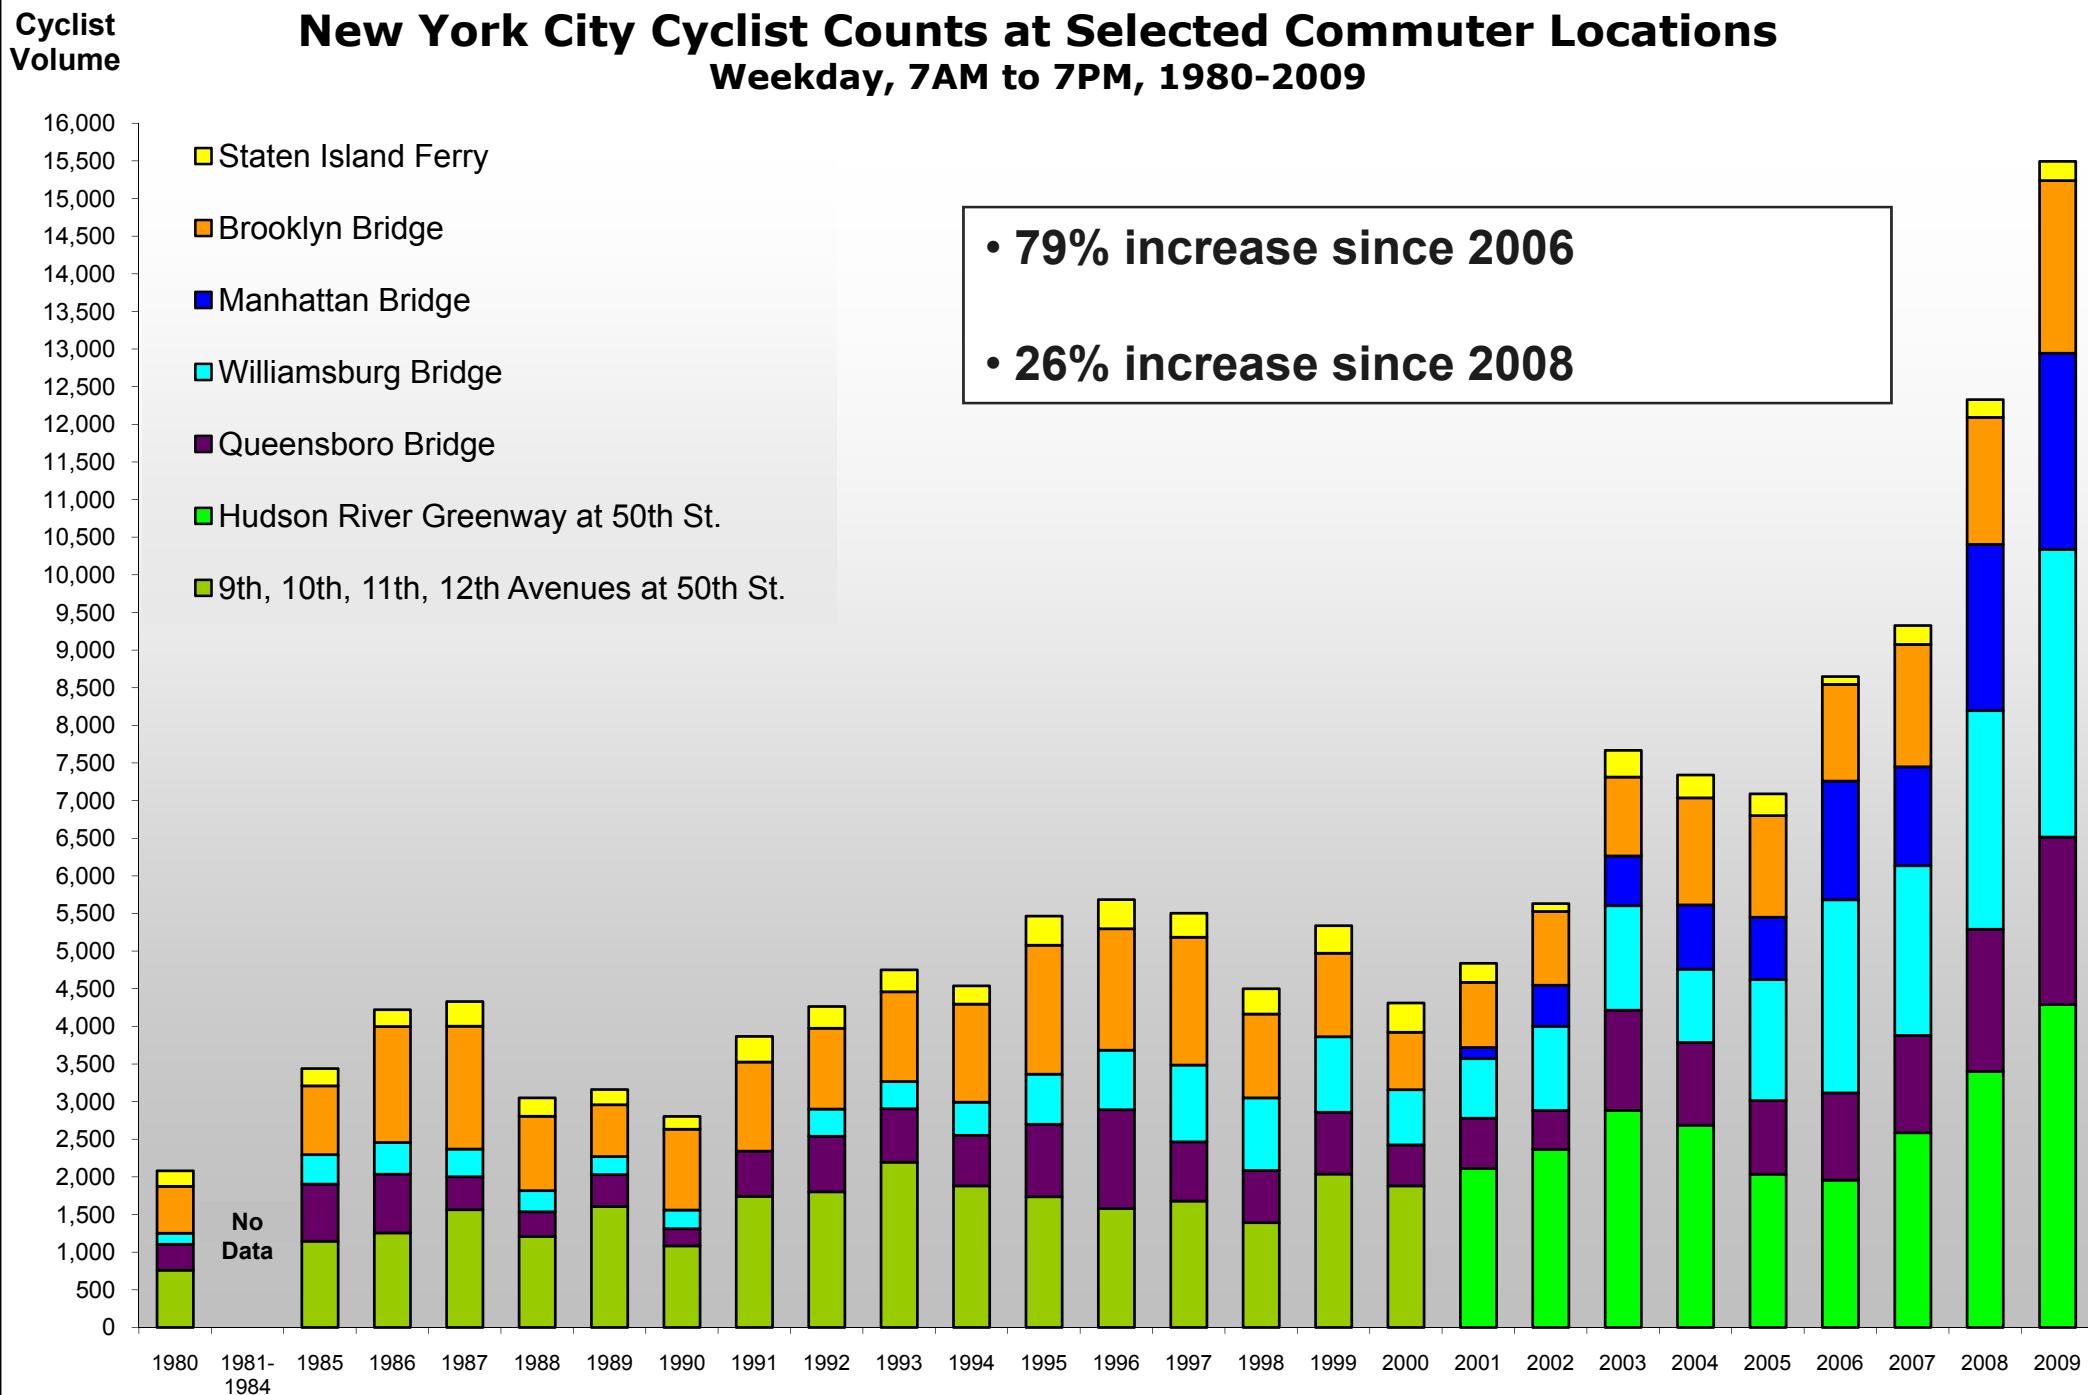

Project Background



Bicycles	12-hour period	
	579	
Motor Vehicles	AM Peak Hour	PM Peak Hour
	1,409	1,390

Source: ATI Data, Vehicles btw. West 78th and 77th Streets, January 2010; Bicycles @ 60th St, September 2008

- CB 7 requested DOT proposal for protected bicycle paths
- No existing on-street southbound bicycle facilities on Upper West Side
- 60-foot wide street with three travel lanes and curbside parking
- Opportunities for speeding and reckless driving

Crash Data

Columbus Avenue Crash History

West 77th-West 96th Sts (2004-2008)

Type of Injury	Total Injuries	Average Injury/Year	Average Injury/Mile/Year
Pedestrian	97	19.4	20.2
Bicyclist	24	4.8	5.0
Motor Vehicle Occupant	130	26	27.1
Total Injuries	251	50.2	52.2

Source: NYSDMV 2004-2008


1 Pedestrian Fatality at Columbus Ave and 86th Street (2006)





Existing
Conditions -
Columbus Ave

Proposed Configuration

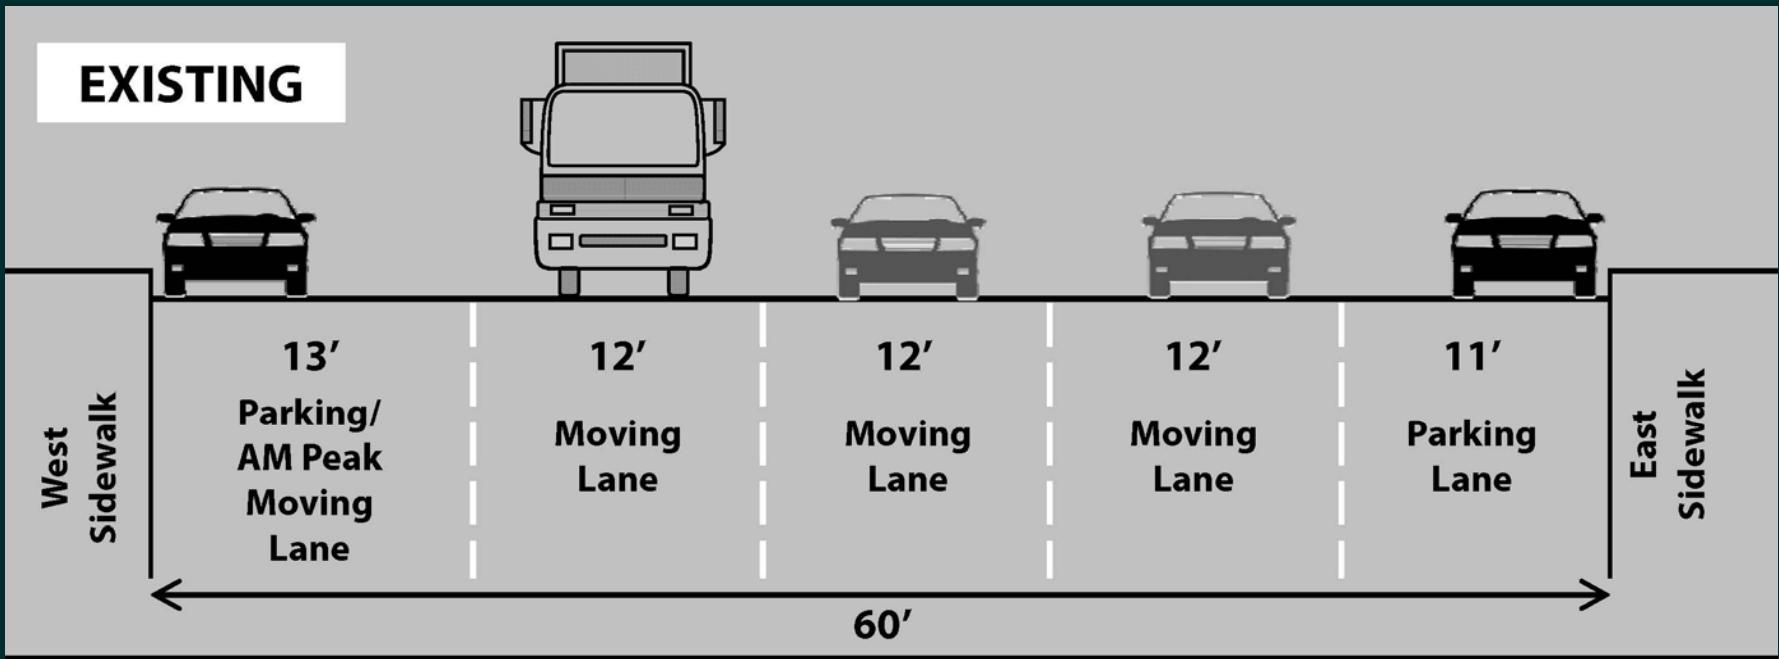

PROPOSED

"Floating" Parking Lane

Parking-Protected
Bicycle Path

Retains Existing Travel Lanes

Striped Buffer Allows for
Safe Vehicle Access Space


Safe Intersections

At Wide, Two-way Cross Streets

1. Separate Bike Signal
2. Pedestrian Refuge Islands
3. Dedicated Left-turn Lane




Safe Intersections – Mixing Zones


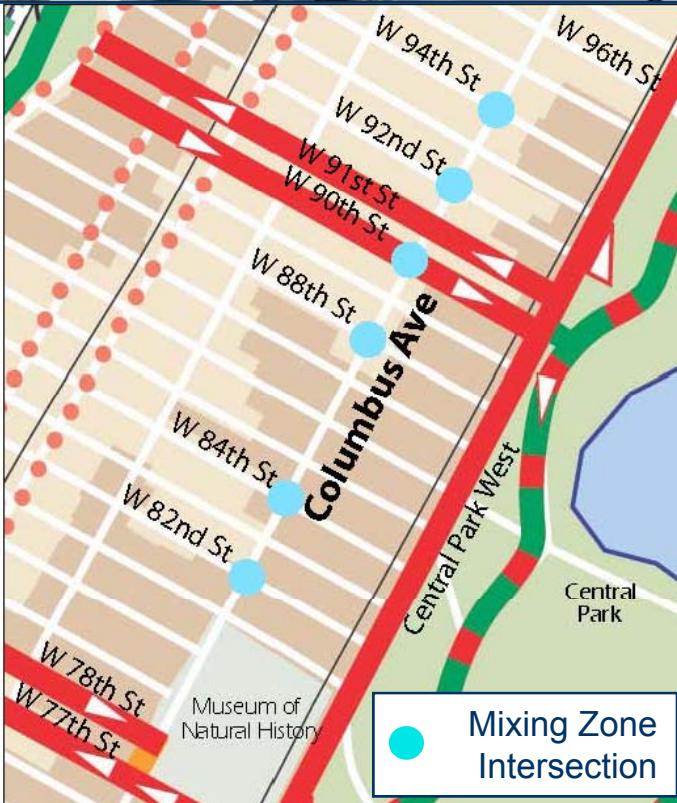


At Narrow, One-way Cross Streets

1. Sight Line Visibility
2. Mixing Zone Markings
3. Drop Green Paint

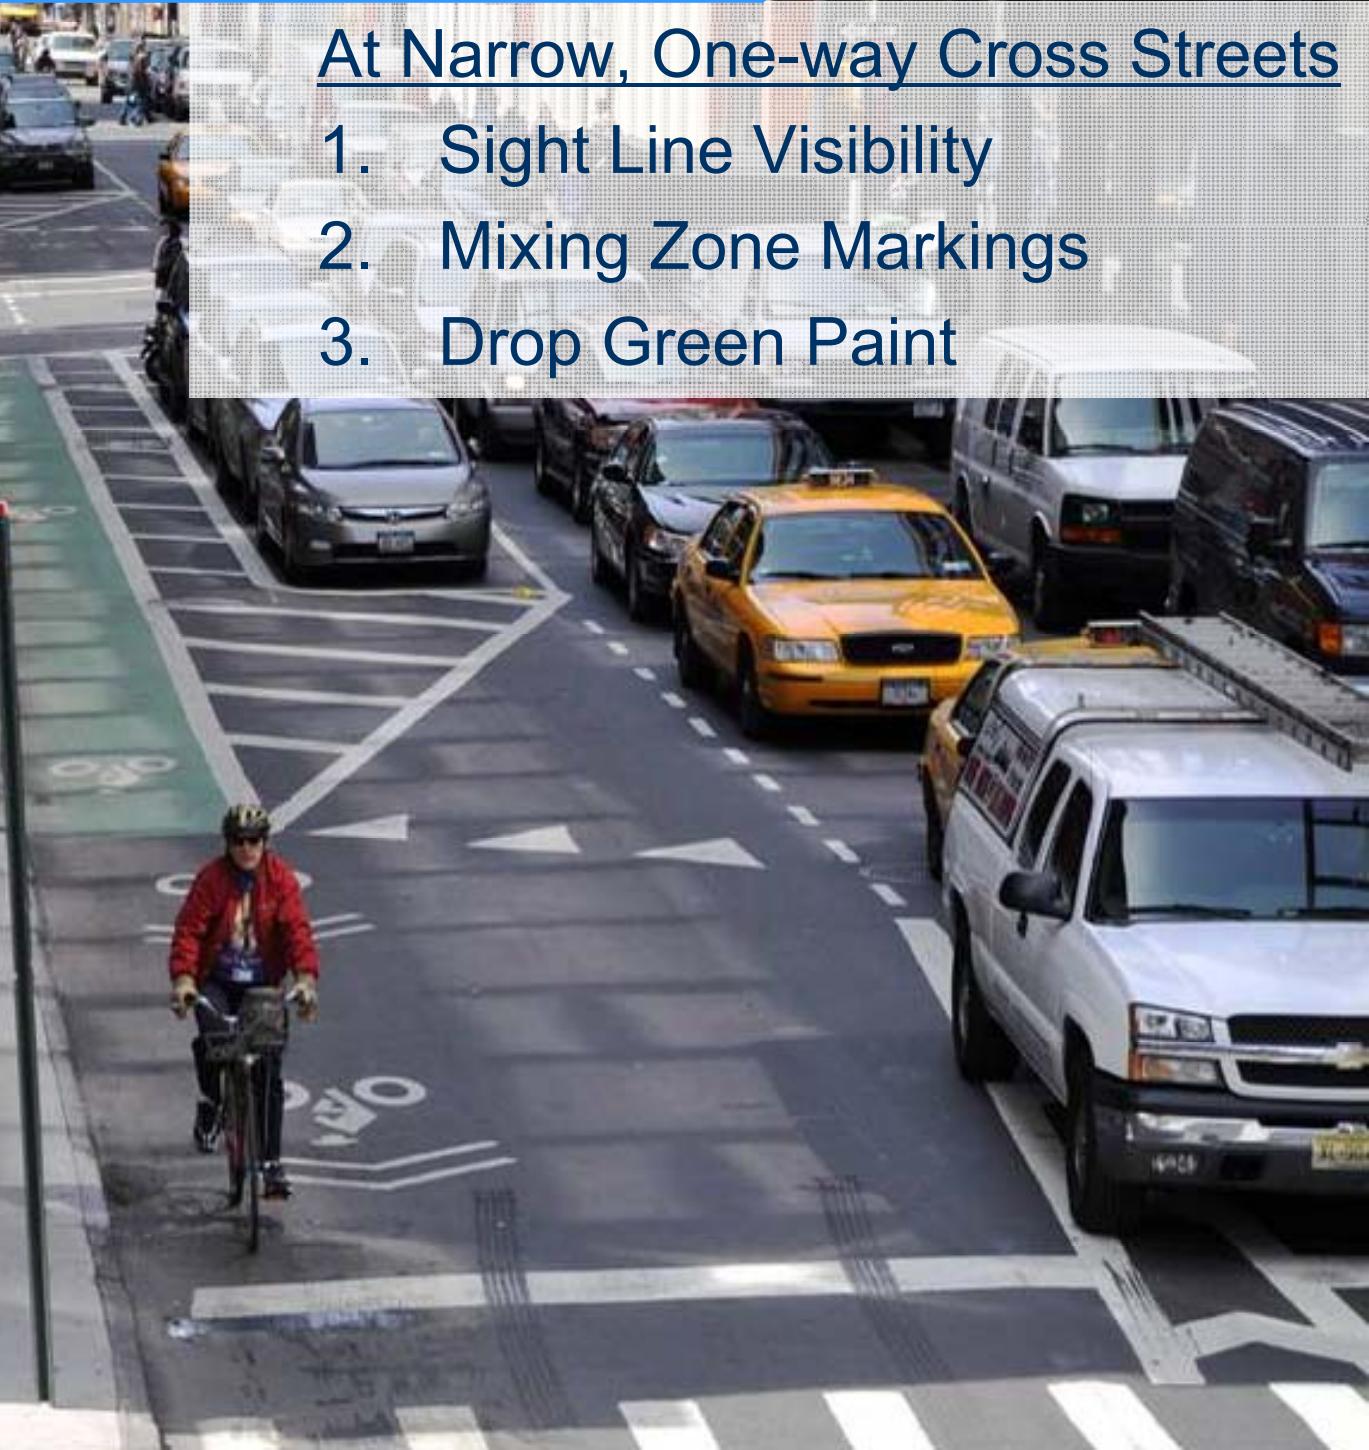

Project Transitions

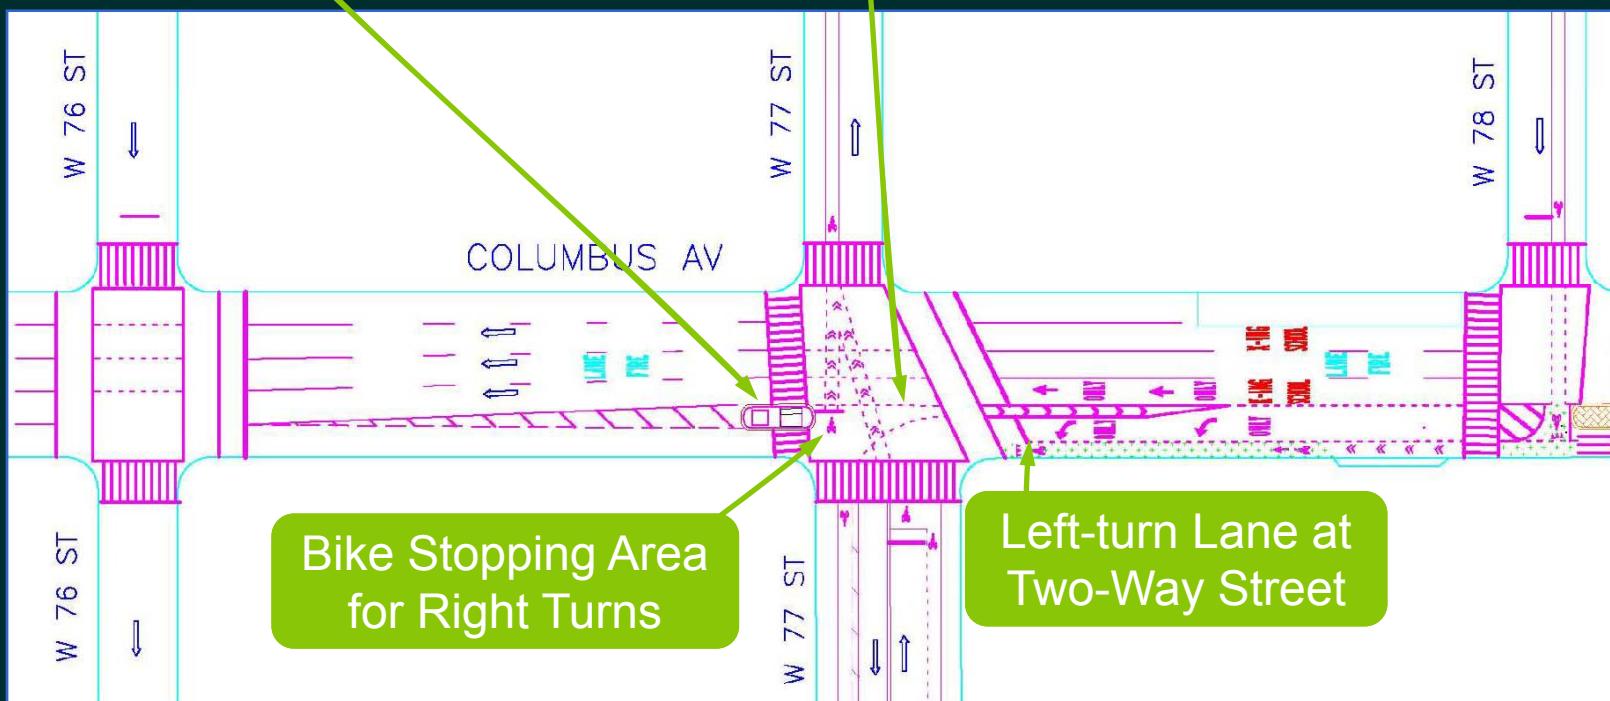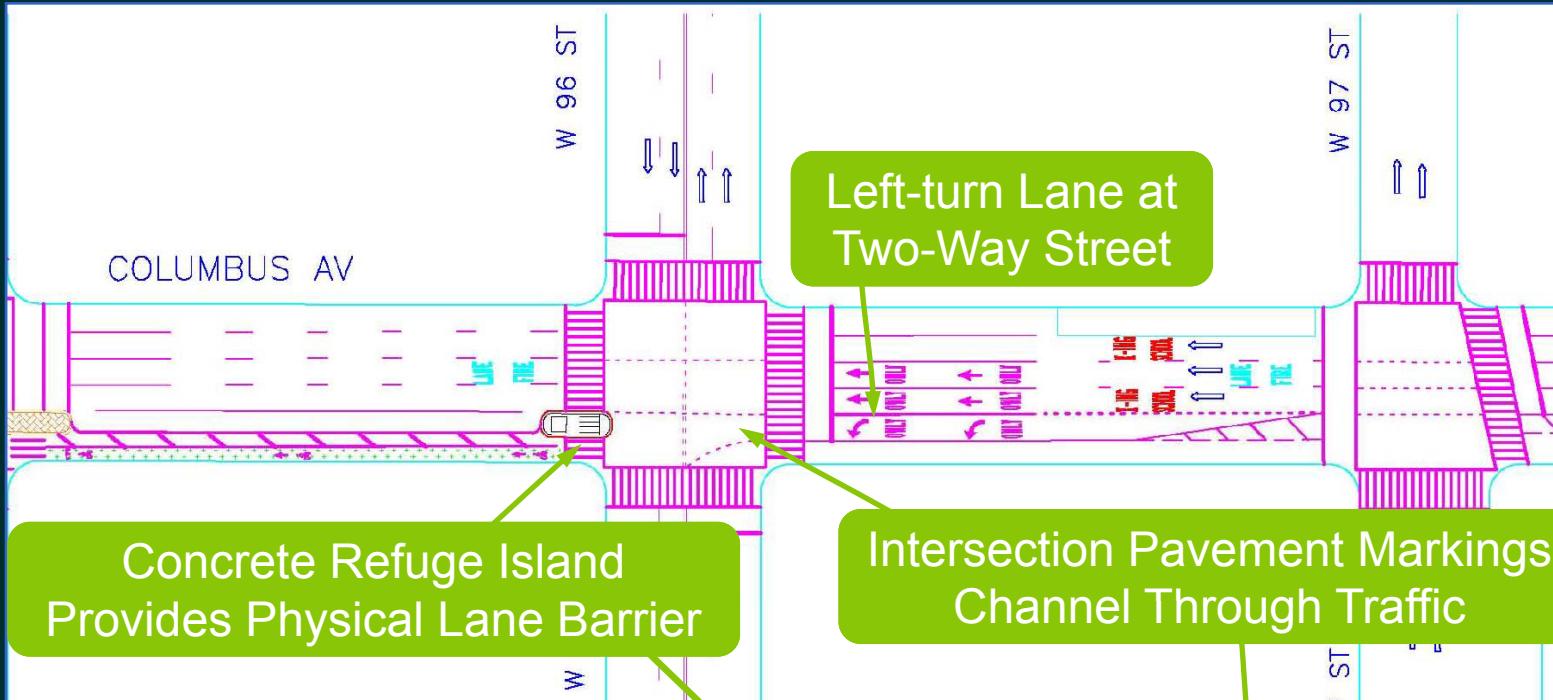

Safety Results




9th Avenue Bicycle Path:

- Injuries to all street users down 56%
- Injuries to pedestrians down 29%
- Injuries to cyclists down 57%
- Sidewalk riding down 84%

Grand Street Bicycle Path:

- Injuries to all street users down 31%
- Reportable crashes down 25%
- Injuries to pedestrians down 21%
- Sidewalk riding down 84%


Project Summary

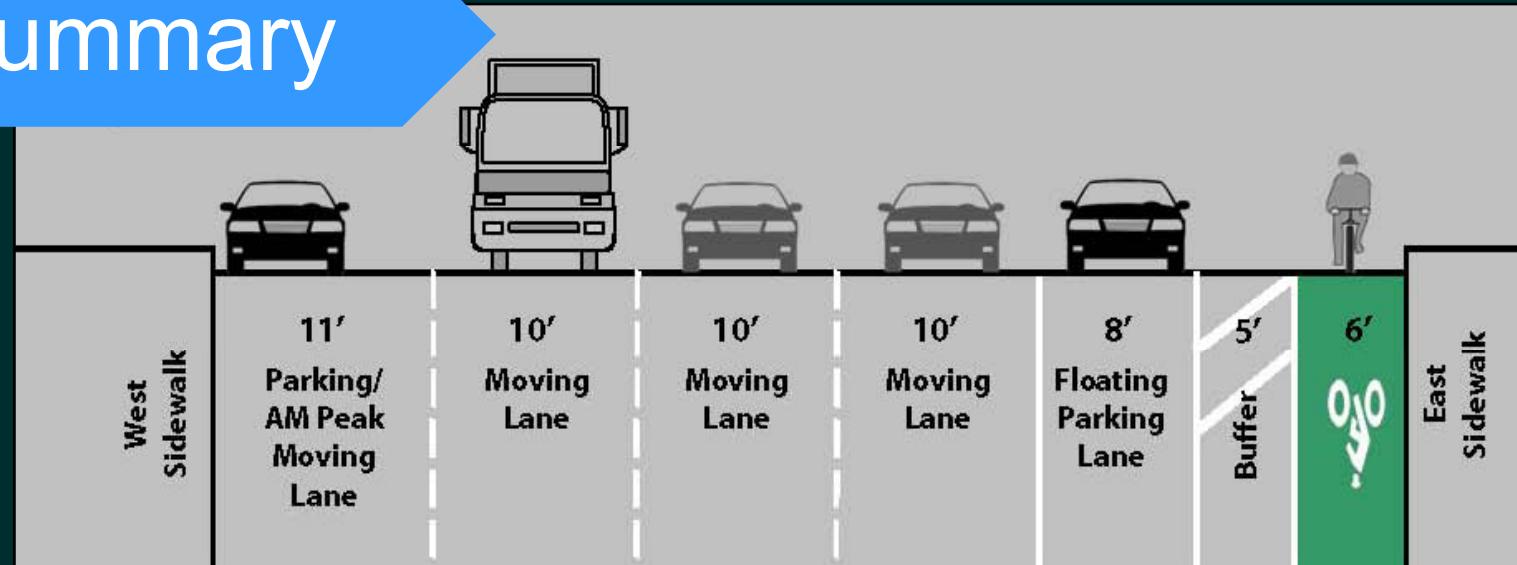

- Enhances Safety for All Street Users
- Improves Bicycle Network Connectivity
- Provides Safety Treatments at Left-turn Intersections in Place of about 55 Metered Parking Spaces
- Decreases Pedestrian Intersection Crossing Distance
- Maintains Vehicle Traffic Capacity

Questions?

Thank
You

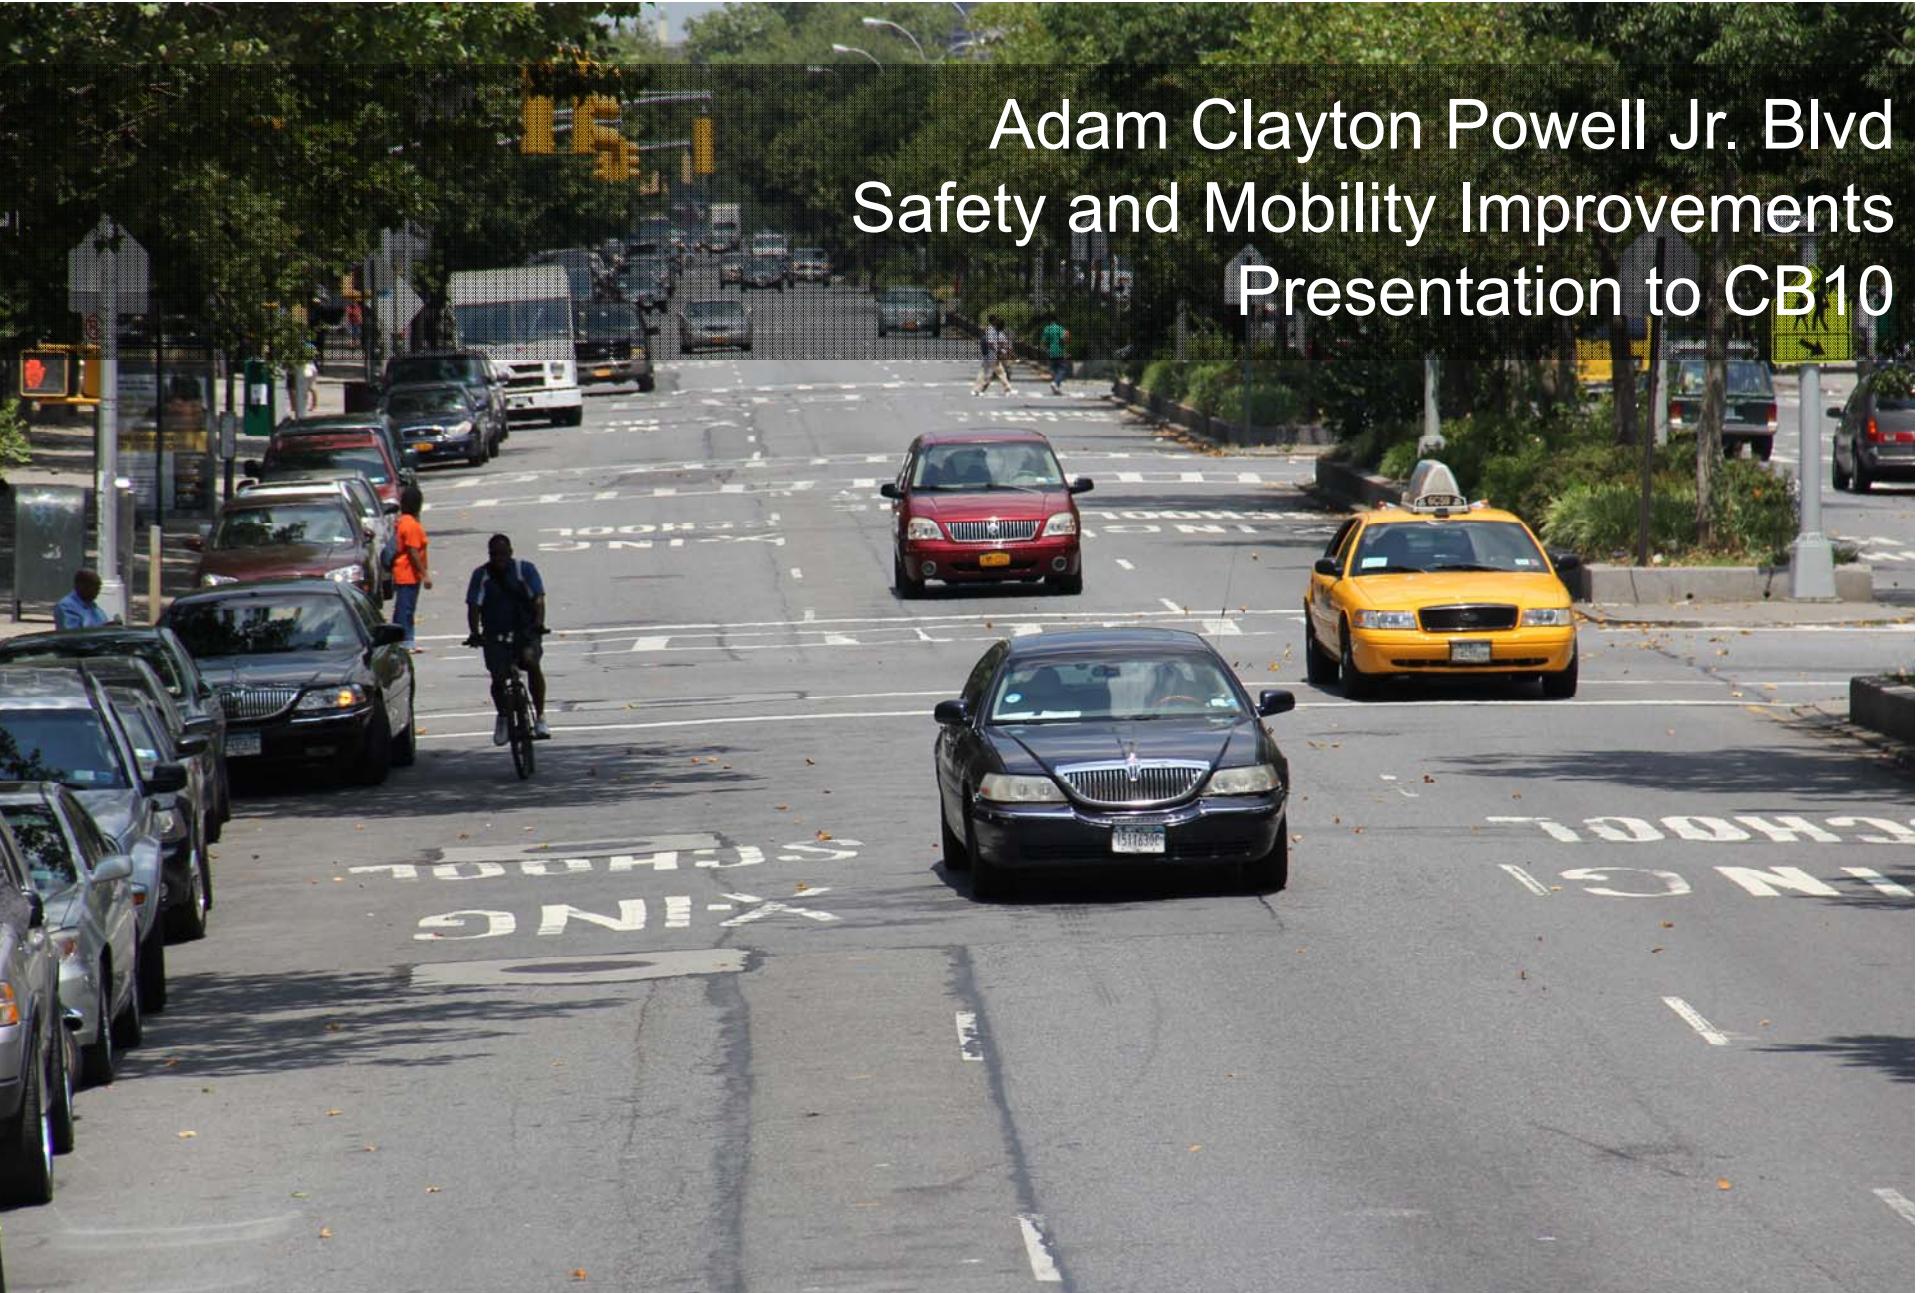


Adam Clayton Powell Jr. Blvd Safety and Mobility Improvements Presentation to CB10

Commissioner Janette Sadik-Khan, New York City Department of Transportation
February 13, 2013



Background

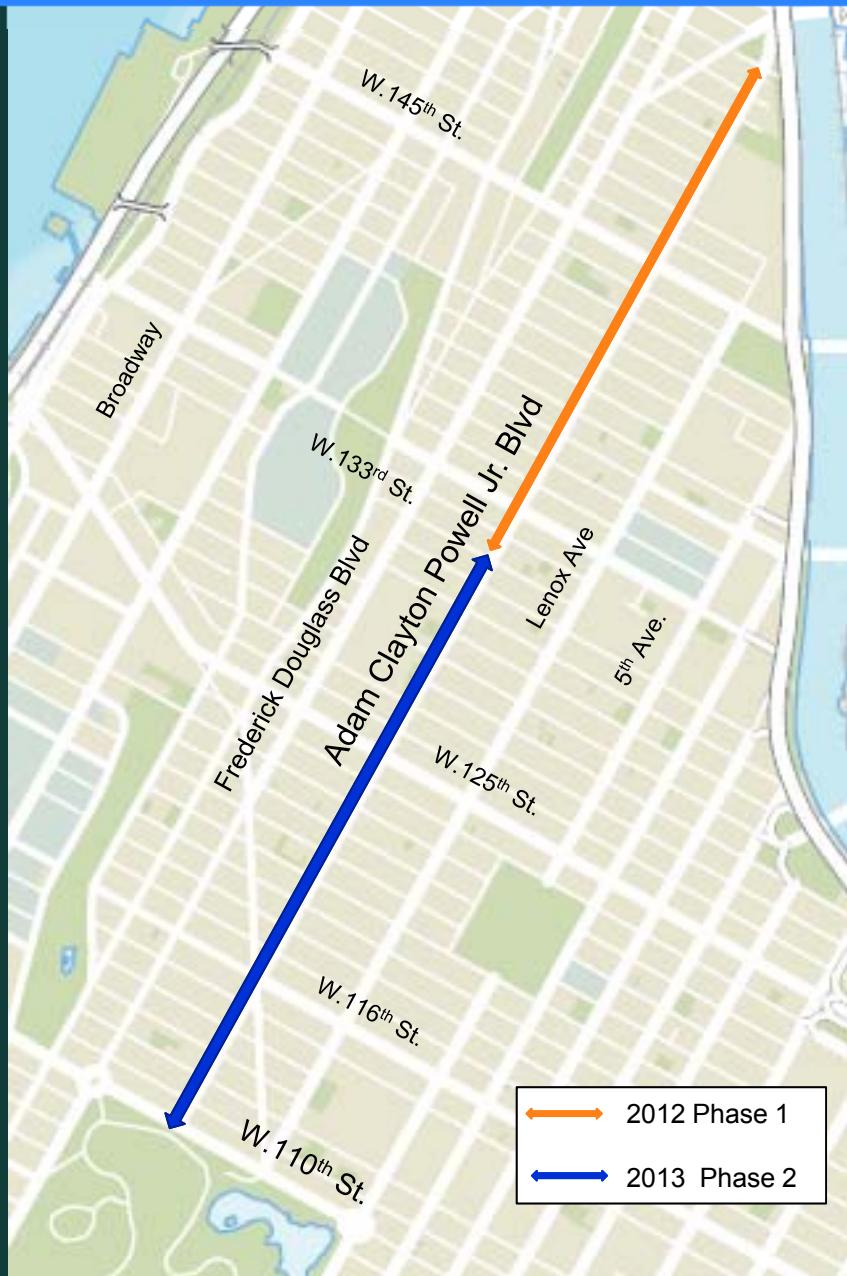

- **2012: Phase 1 Safety Improvements**


- W 133rd St to W 153rd St
- Crashes down **32%**

- **2013: Phase 2 Safety Improvements**

- W 133rd to W 110th Streets
- High Crash Corridor: Ranking in Top **10%** for Manhattan

- Analysis compares the average of the three prior years (2009-2011) between September 1 and October 31 only and September 1 to October 31, 2012

Injuries

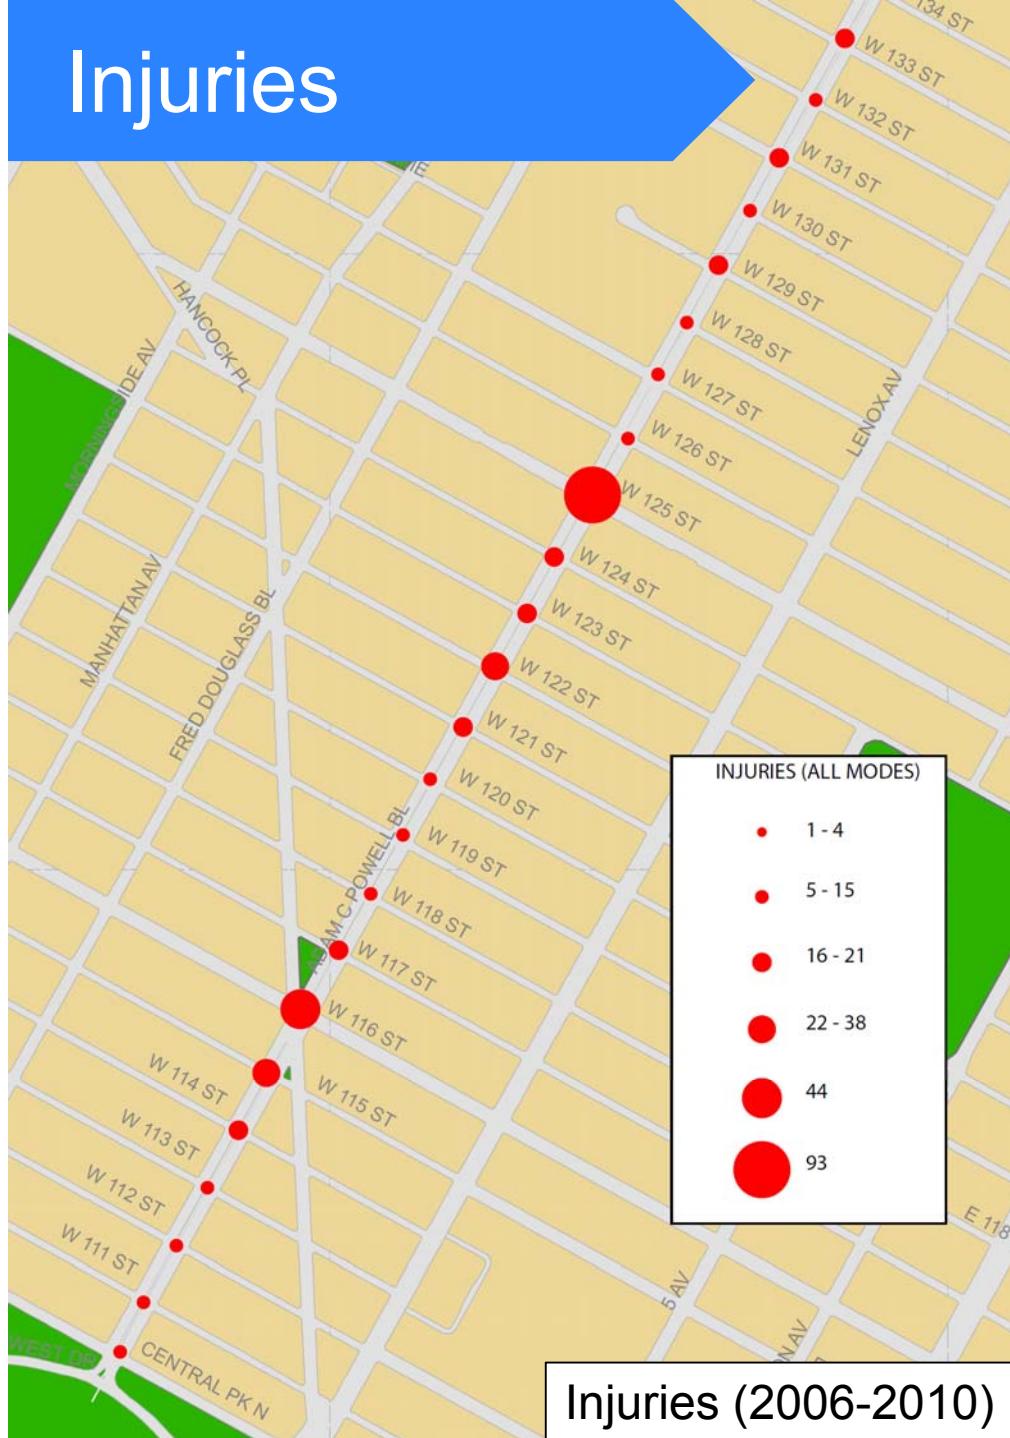

- **464 Total injuries**
- Over **76%** of injuries are motor vehicle occupants
- **31%** of motor vehicles crashes are rear-end collisions

• Motor vehicle crash data per NYPD, between W 133rd Street and W 110th Street

Existing Conditions




- **3 Pedestrian fatalities since 2009**


Existing Conditions



Existing Conditions: W 110 St to W 133 St

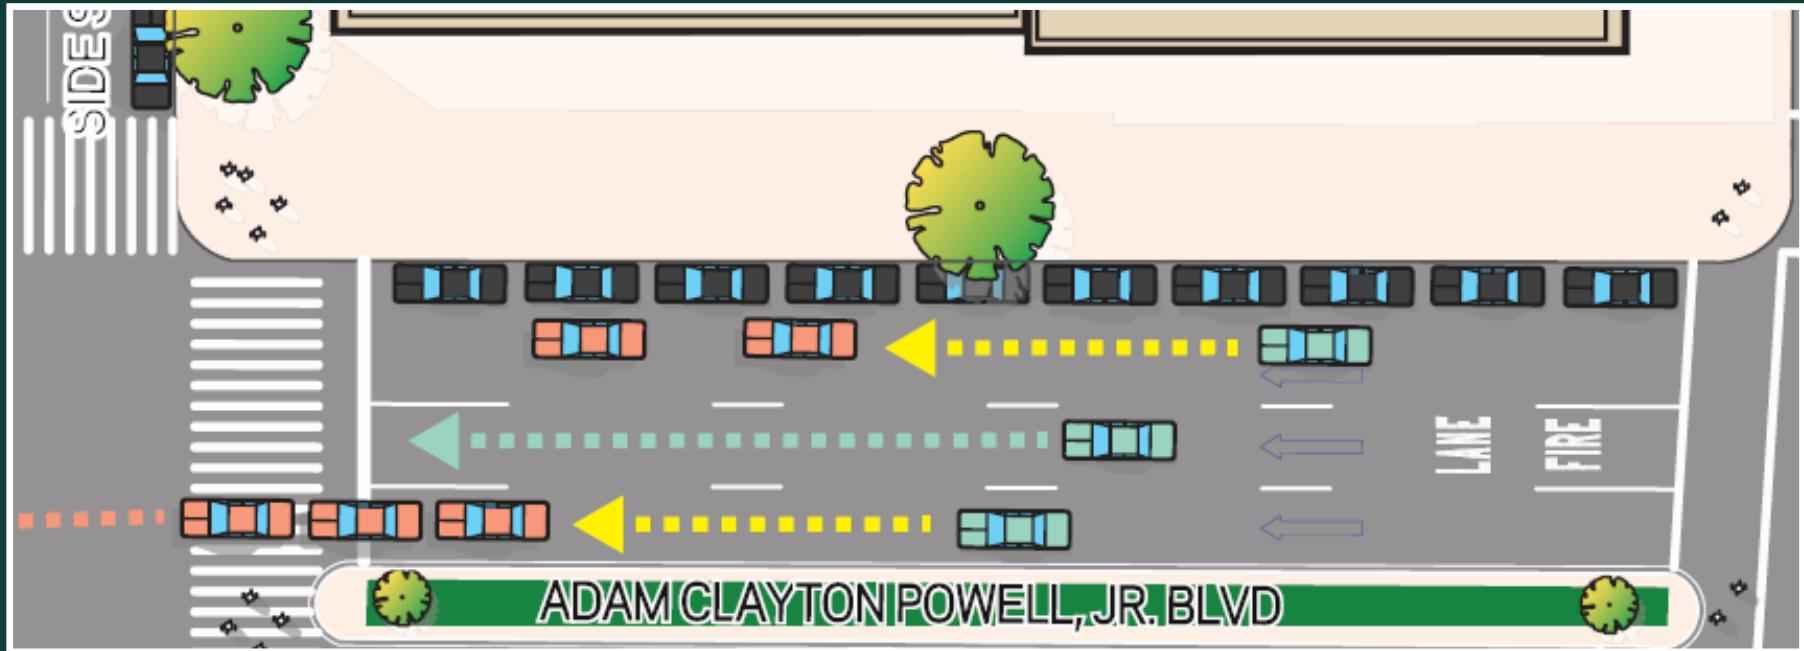

- Unorganized roadway
- Left turning vehicles block through movement
- Many lane changes



Difficult Crossings



Waiting to cross close to speeding vehicles

Safety Treatments




- Painted pedestrian islands
- Left-turn lanes
- Wide parking lanes


Design

Existing

Adam Clayton Powell Jr. Blvd:
W 110th St to W.133rd St

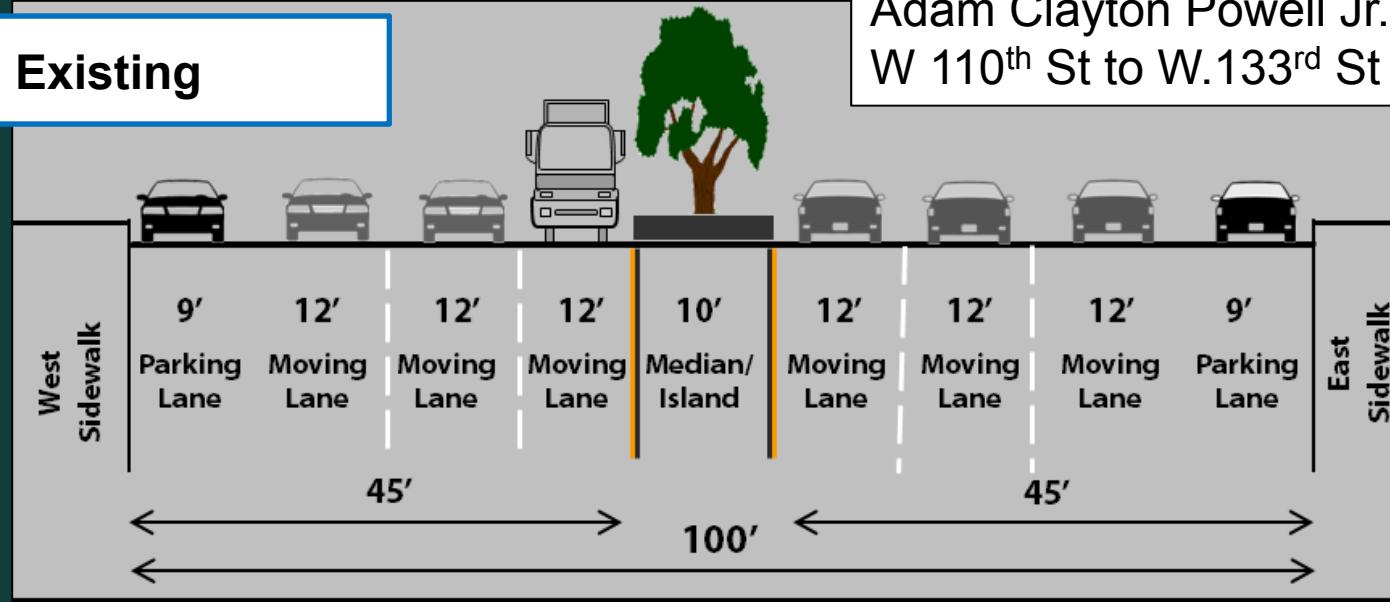


Safety Improvements

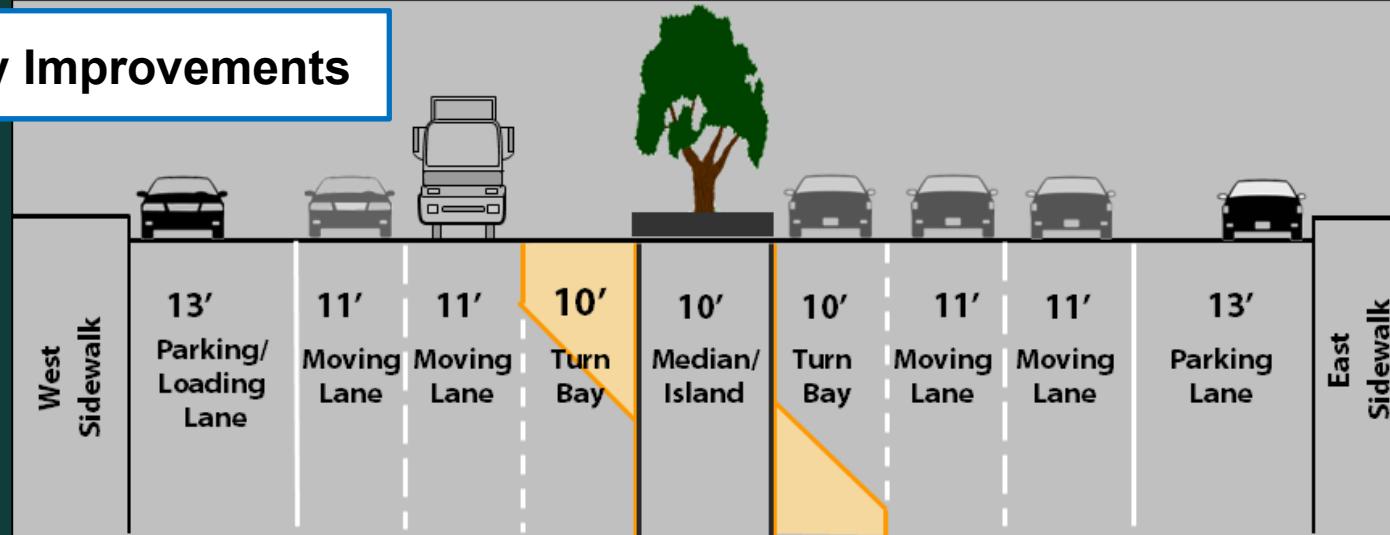

- Existing bike lane between W 110th St and W 118th St to remain

Design


Existing

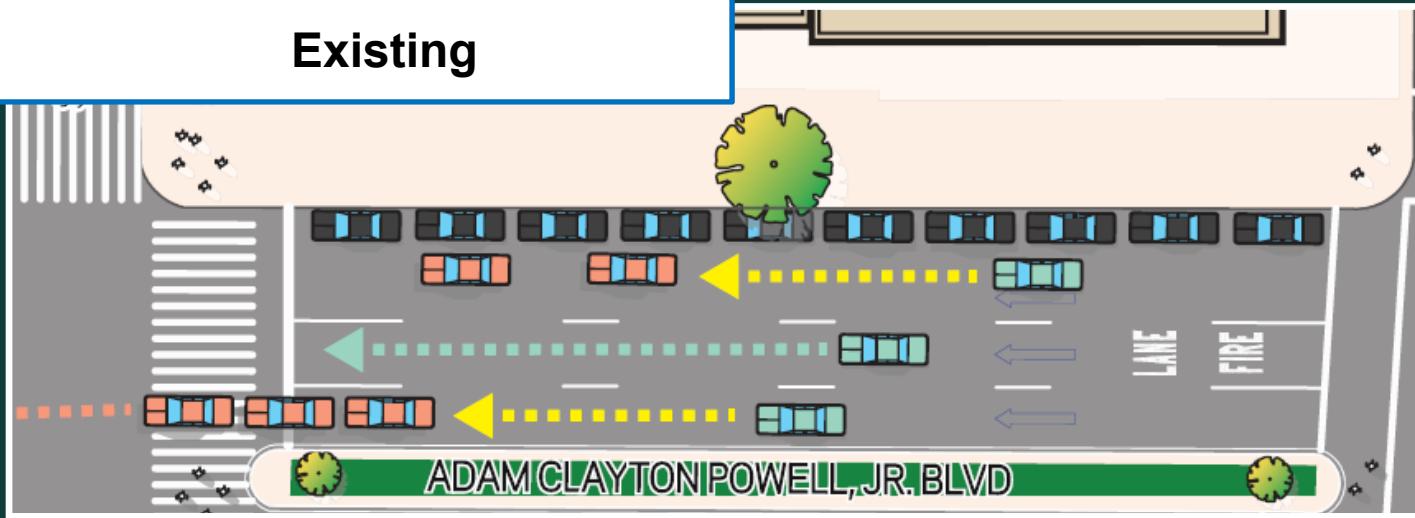

LEGEND


- Through-moving Car
- Double-Parked or Left-turning Car
- Clear Driving Path
- Blocked Driving Path
- Left-turning Path

Safety Improvements

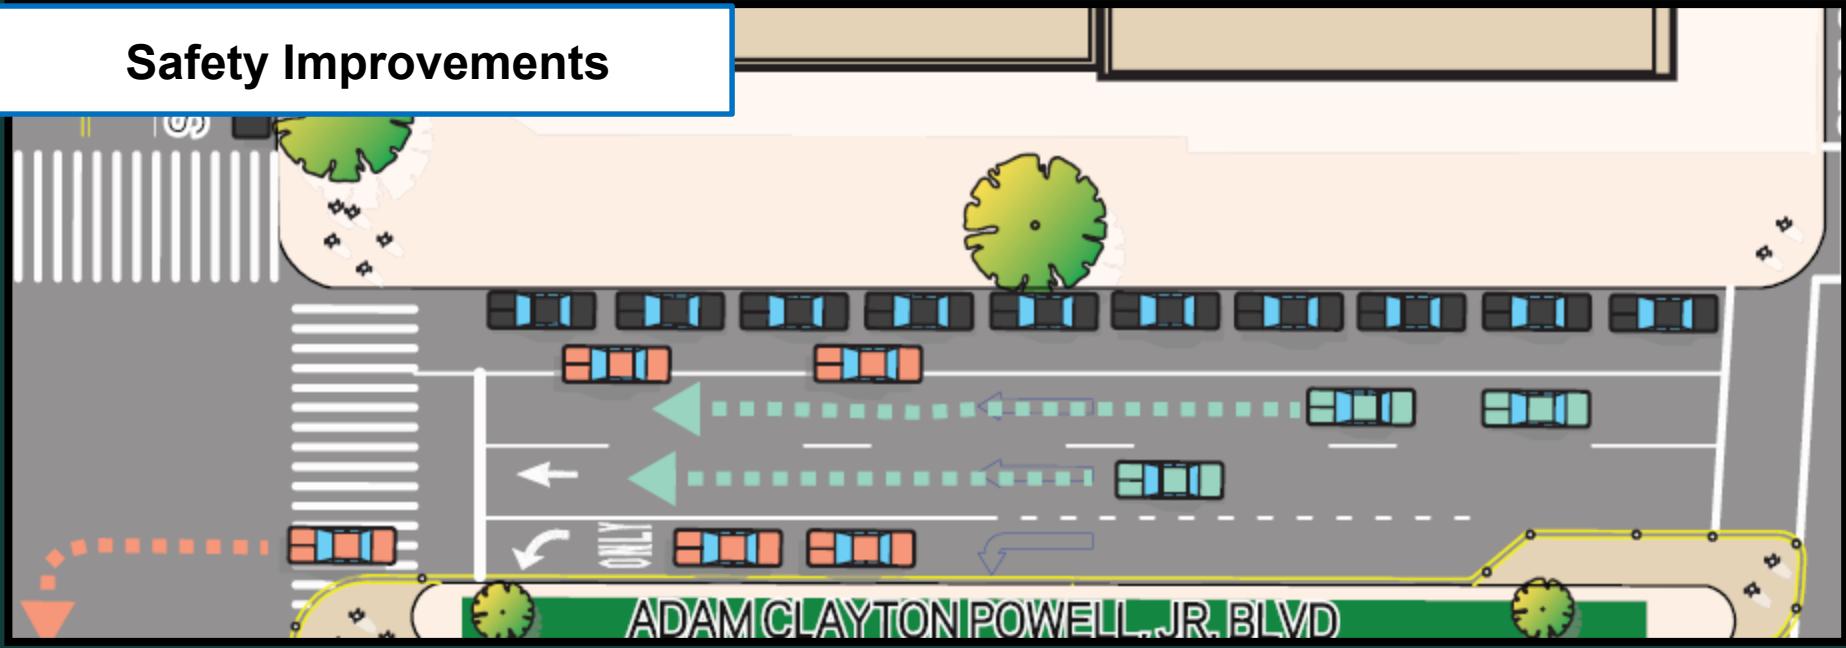


W 116th St Intersection Background

Safety concerns raised in the past

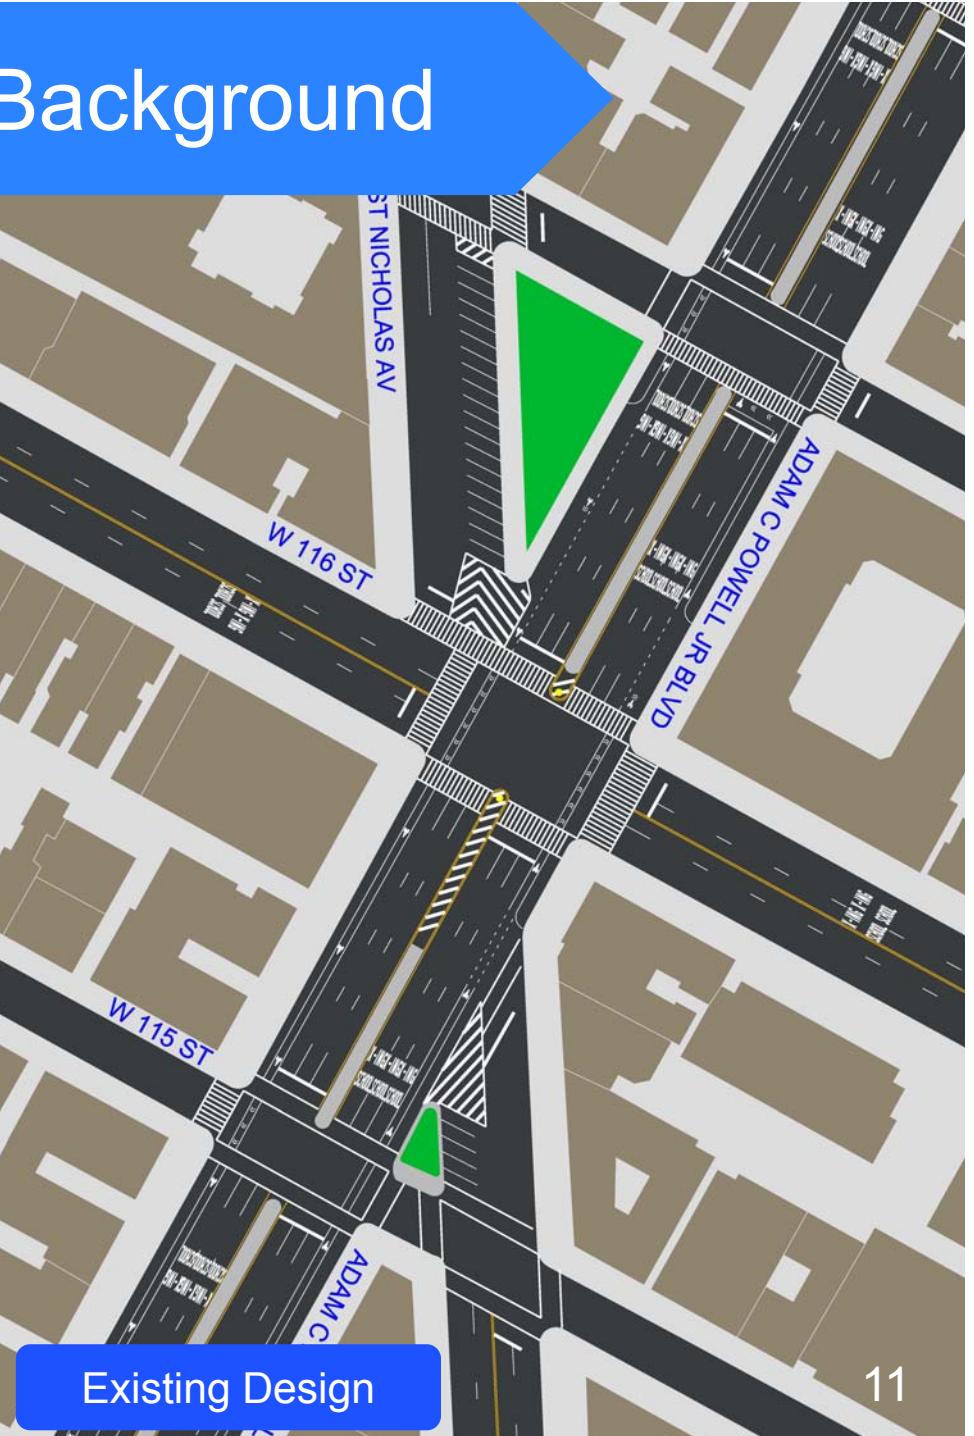

Existing Design

W 116th St Intersection Existing Conditions

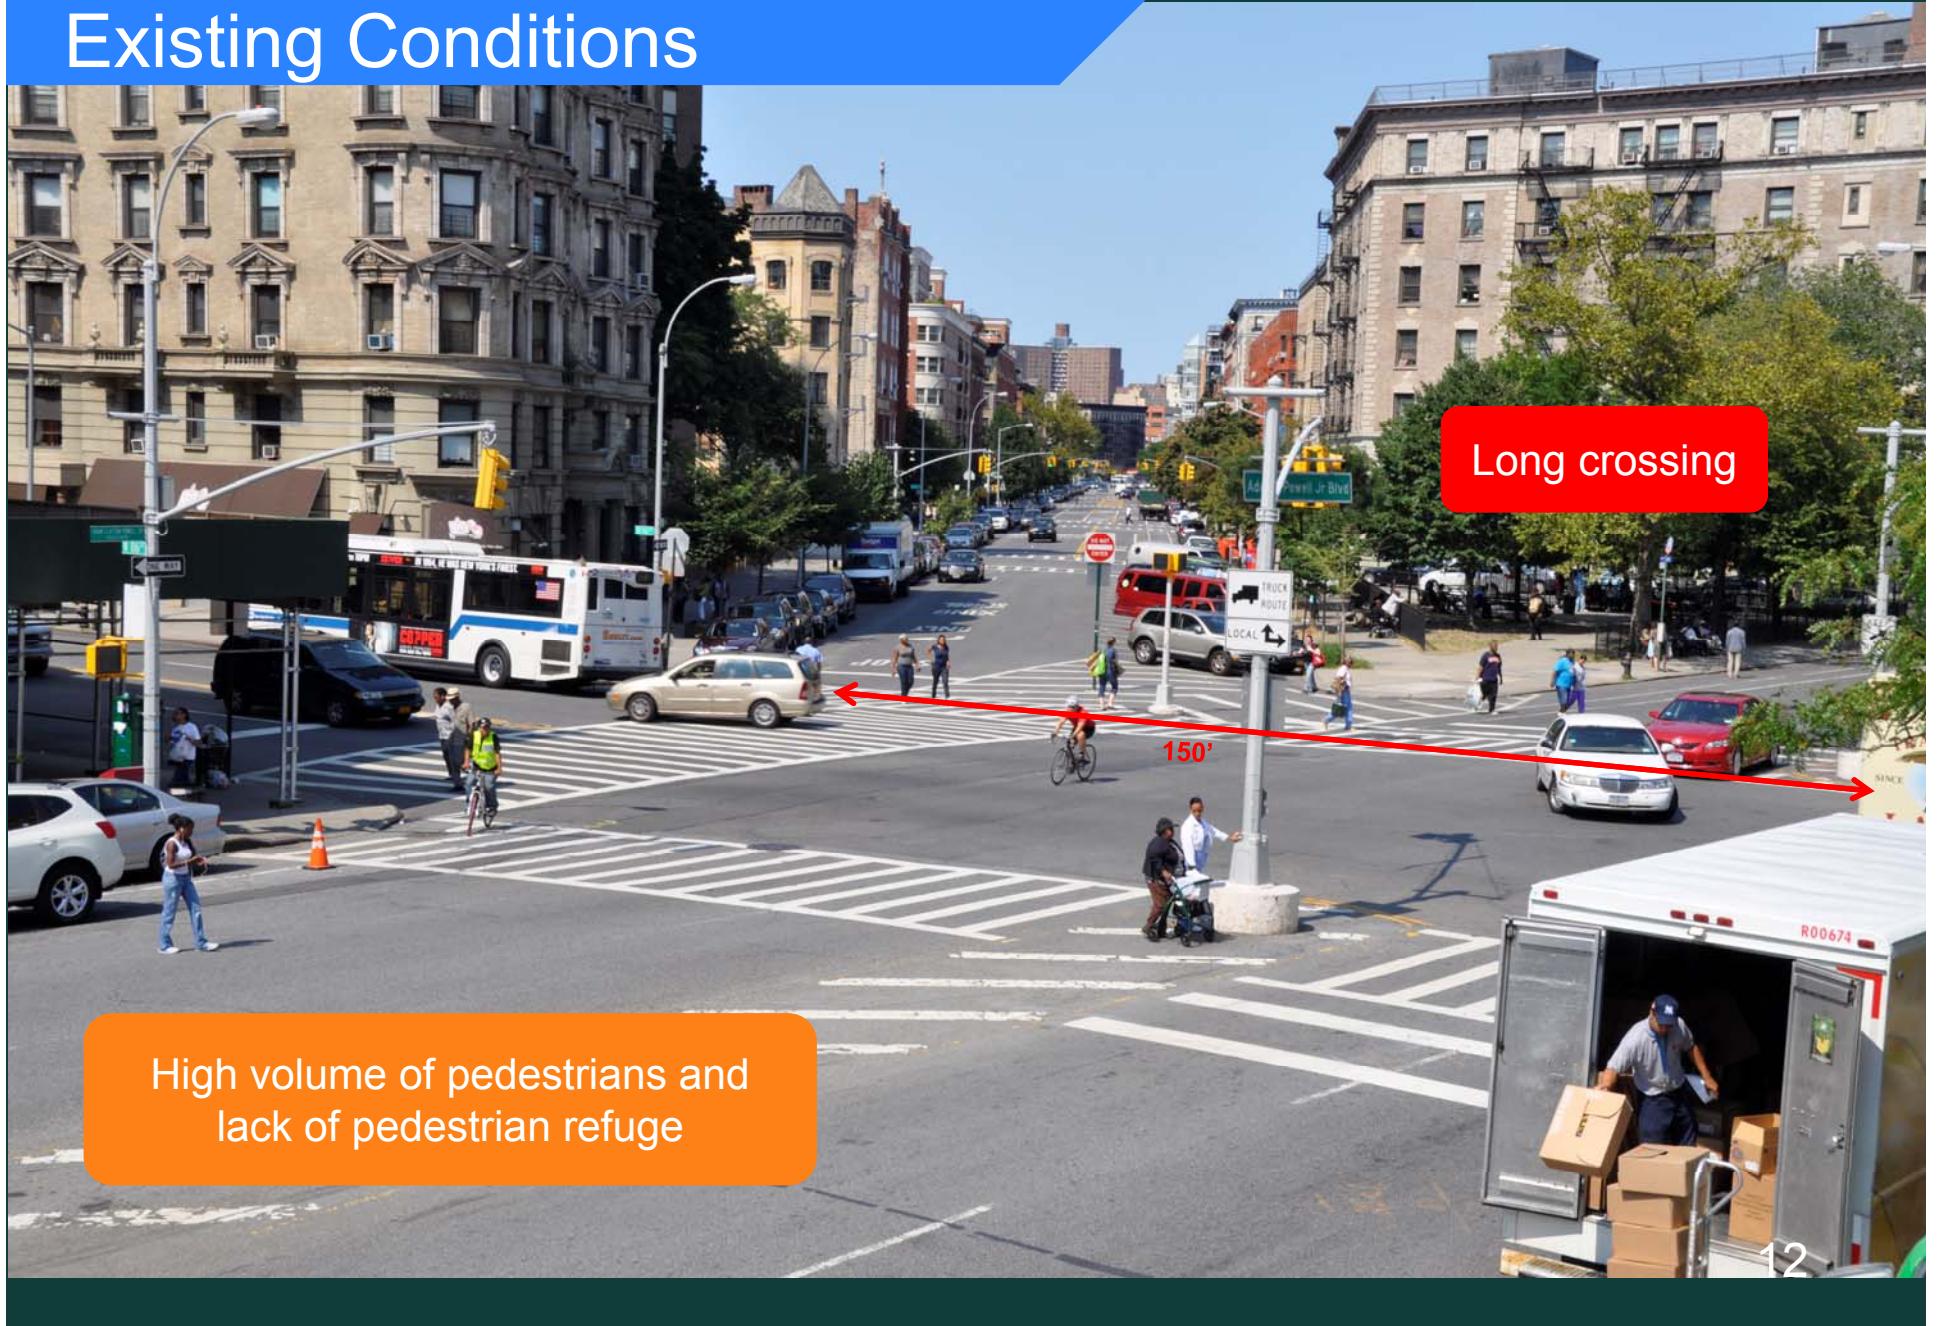

St. Nicholas Ave Existing Conditions



W 116th & St Nicholas Proposal

Paint extension prevents cars from accessing ACP from slip lane


Crossing reduced by 58 feet

Extend concrete tips with paint to provide pedestrian refuge at crossings

Expand triangle with paint to improve pedestrian circulation



Similar proposed design treatment:

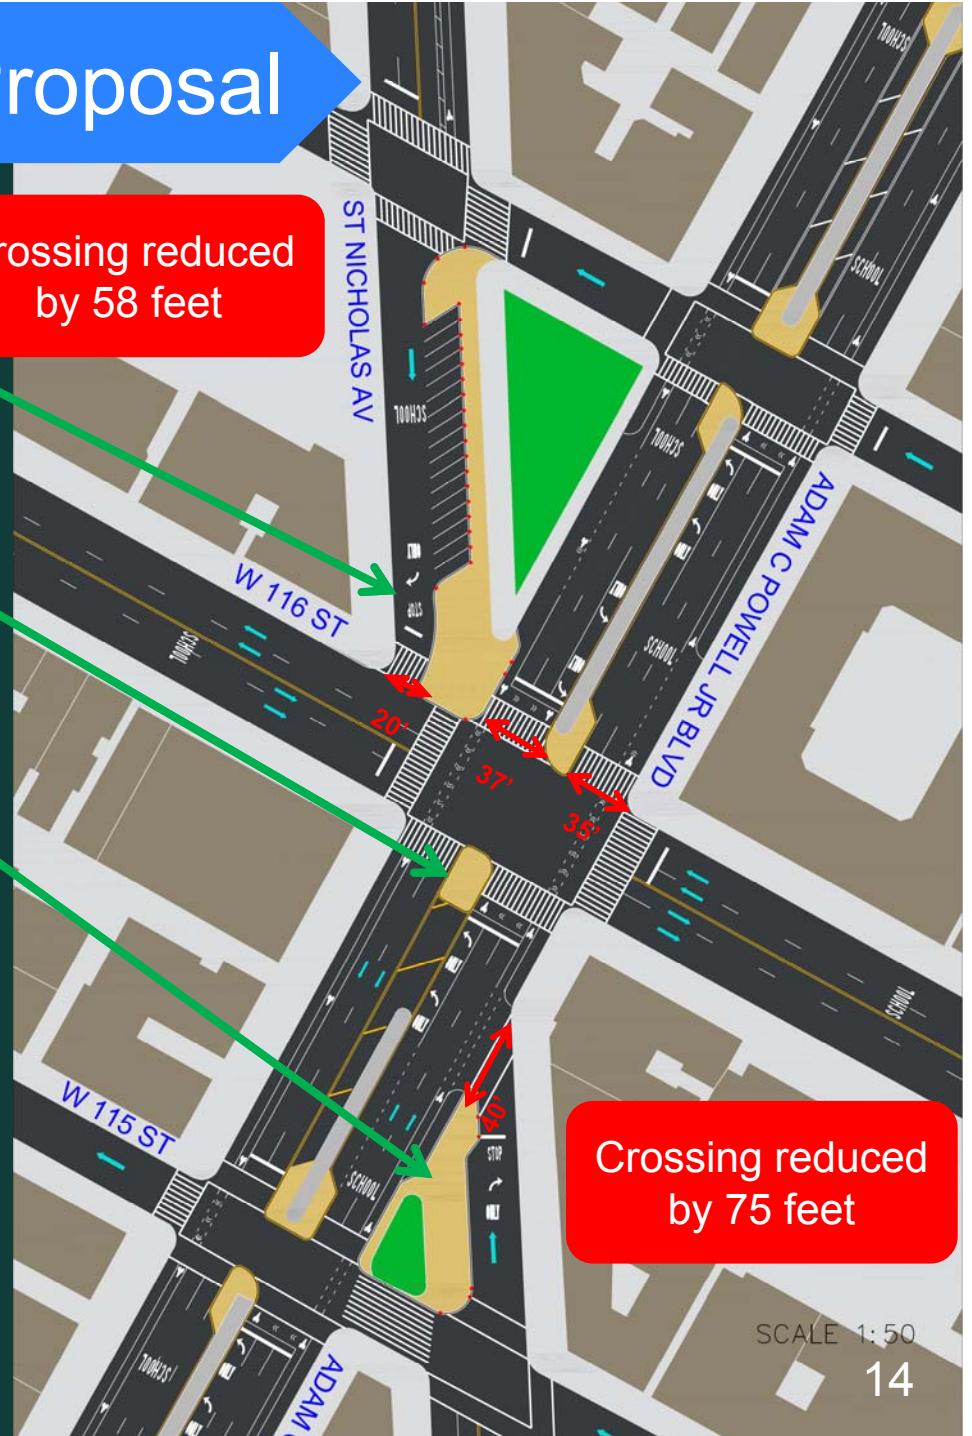

Community Requests / Feedback



- Remove extra delineators along median
 - Completed
- Install left turn signals where feasible
 - Currently being investigated
- Install speed limit signs at all major thoroughfares
 - Speed limit signs will be installed
- Install red light cameras
 - Under study for future contract
- Increase crosswalk countdown to 30 seconds
 - Signals to increase to 28 secs at most intersections
- Install electronic speed boards
 - Speed boards will be placed in the spring
- Extend the median concrete to resemble Lenox Ave.
 - One location planned for 2013 pending feasibility review

Project Summary

- Shortened Pedestrian Crossings
 - Better pedestrian circulation
- Better Organized Roadway
 - Reduces the need for lane changing
- Traffic Calming
 - Organizes through-traffic in multiple school zones
- Enhances Safety for All Road Users

nyc.gov/dot

Thank
You

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Brooklyn

Day Monday

Date 7/8/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	14:30	8	1		
Gadiel Salas	ACHR	5:00	14:30	8	1	H. Foster	
Julio Ochoa	ACHA	5:00	14:30	8	3	Julio Ochoa	
Sammy							

ON STREET

Adam Clinton Power Jr.

CROSS STREET

115 St

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	10	Caulking	Lin. Ft.
Backfill	Cu. Yds.	Sealant Spray	Tube
Asphalt Patch	Tons	Sand	Gal.
STEP STREETS		Cu. Yds.	
Landing	Cu. Yds.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Sq. Ft.	Other:	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #: 0004	Large Dump Truck Truck #: 7367 7377	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Townmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:			5008	

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

DOT Fax:718-353-6381
 DOT/SIM/CITYWIDE CONCRETE
 DAILY GANG REPORT

Borough Queens

Day monday

Date 7-8-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	06:00	16:30	8	3		
Fevrin Agenzord	ACHR	06:00	16:30	8	2		
Frank Messina	ACHR	06:00	16:30	8	2		
Edward Cotton	ACHR						A/L

ON STREET

115 3rd Avenue & Powell	CROSS STREET

WORK PERFORMED

SIDEWALK & CURB	MATERIAL USED
Sidewalk Prep	Ready Mix Concrete Cu. Yds.
Sidewalk Pour	Sq. Ft. Lumber Lin. Ft.
Curb Prep	Sq. Ft. Steel Curb Straight Lin. Ft.
Curb Form	Lin. Ft. Steel Curb Bull Nose Pieces
Curb Pour	Lin. Ft. Detectable Warning Sq. Ft.
	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	
Debris Removal	Caulking Lin. Pt.
Backfill	Cu. Yds. Sealant Spray Tube
Asphalt Patch	Tons Sand Gal.
STEP STREETS	
Landing	Cu. Yds. Stone Cu. Yds.
Pointing/Caulking/Patching	Sq. Ft. Other:
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

Crew Cab Mason Truck Truck #: <u>02-99</u>	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: <u>02-67</u>
Other:				

COMMENTS:

Went to 44 Drive Picket up materials needed. Then went to location set up safety. Help break out snow shovel debris. Set up for dumping for pour, cleaned up location and results safety. Went back to yard. Give winter shoes.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough BK

Day MONDAY

Date July-8-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0500	1530	8	2	<i>Milagros Lopez</i>	
Sean Thomas	ACHR	0600	1530	8		<i>Sean Thomas</i>	
Rohan Wilkinson	ACHR	0600	1430	8	0	<i>Rohan Wilkinson</i>	
Nicholas Depaola	ACHR	0600	1530	8	0	<i>Nicholas Depaola</i>	

ON STREET	CROSS STREET
<u>RICHMOND TERR</u>	<u>STANLYER ST</u>
<u>115TH ST</u>	<u>A.C.D.</u>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep <u>Pep Ramps</u> (2)	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	PICK UP	Light Duty Truck
Truck #:	Truck #:	#:	Truck #: <u>7087</u>	Truck #: <u>0244</u>
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>0014</u>

Other:

COMMENTS:

M. LOPEZ AND N. DEPAOLA HELPED WITH MARK
DT SAW CUT CANNED, R. WILKINSON AND SHAWN,
I SHOT CUT SECOND LOCATION MADE SURE
LOCATION WAS CLEAN AND SAFE

I CERTIFY THAT THE TIME AND THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Milagros Lopez

Title

Crew Leader

Approved By

J. H. H.

Title

Supervisor

DOT Fax: 718-353-6381
 DOT/SIM/CITYWIDE CONCRETE
 DAILY GANG REPORT

Jul 10 2013 05:56am P008/011

Borough Bronx

Day Tuesday

Date 7-9-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3	<i>W.M.</i>	
Fevrin Agenord	ACHR	06:00	16:30	8	2	<i>F.A.</i>	
Frank Messina	ACHR	06:00	16:30	8	2	<i>F.M.</i>	
Edward Colon	ACHR	06:00	16:30	8	2	<i>E.C.</i>	

ON STREET	CROSS STREET
115th Street	115 Adam C. Powell

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete 3 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable, warning 4 (2x4) mats Sq. Ft.
Curb Pour	Lin. Ft. Expansion joints 60 Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0289	Truck #: 0003	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: 0267

Other:

COMMENTS: Poured 3cy yard cement, finished Pad ramp on S/E corner Adam C. Powell, and Pad ramp and S/W corner of 8th Ave and 115 completed 4 pad ramp in total - helps w/ the saw cut, set up. Set by, and cleaned up.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature Frank Messina

Title Crew Leader

Approved By

Title Supervisor

DOT
Fax: 718-353-6381
DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Jul 10 2013 05:55am P001/011

Borough Queens

Day TUESDAY

Date 7-9-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Salvatore Russell	CM	600	1630	7	3	<u>Salvatore M. Russo</u>	

ON STREET

CROSS STREET

ADAM CLAYTON Powell, JR W 115 St
F AV E 109 St
I AV E 114 St

SOY, SSS

WORK PERFORMED

MATERIALS USED

SIDWALK & CURB	Ready Mix Concrete	3	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Strength	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bu. Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>3854</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

OUR 3 cuyd OF CONCRETE FOR NORMAL PREW ALSO WENT TO INSPECT BOR AT I AV 109 St

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader
Salvatore M. Russo
Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Staten Island Day Wed.

Date 7/10/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Comballeri	HR	500	1630	8	3	<i>Franca Comballeri</i>	
Jason James	HR	600	1630	8		<i>Jason James</i>	Worked with Miguel crew.

FROM	ON STREET	CROSS STREET
<i>FRANG</i>	<i>Boy Ave</i>	<i>Richmond Terrace</i>
<i>Jpy</i> ->	<i>Adam C Powell Jr</i>	<i>15th St</i>

WORK PERFORMED		MATERIALS USED	
SIDWALK & CURB		Ready Mix Concrete	
Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
HOLE & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: 754T	Light Duty Truck Truck #: 6836
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Arrived to location received delivery in good

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Jason Comballeri
Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Wednesday

Date 7-10-13

SIGN IN						
Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3	<i>W.M.</i>
Fevrin Agenord	ACHR	06:00	16:30	8	2	<i>F.A.</i>
Frank Messina	ACHR	06:00	16:30	8	2	<i>F.M.</i>
Edward Cotton	ACHR	06:00	16:30	8	2	<i>E.C.</i>

ON STREET	CROSS STREET
<i>Adam C Powell</i>	<i>115th Street</i>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete <u>2 cu. yds.</u> 15 Cu. Yds.
Sidewalk Prep	sq. Ft. Lumber
Sidewalk Pour	sq. Ft. Steel Curb, Straight
Curb Prep	lin. Ft. Steel Curb, Bull Nose
Curb Form	lin. Ft. Detectable Warning
Curb Pour	lin. ft. Expansion Joints
PREP & CAVE-IN	Snap Caps
Debris Removal	Cu. Yds. Caulking 6 Tube
Backfill	Cu. Yds. Sealant Spray
Asphalt Patch	Tons Sand
STEP STREETS	Cu. Yds. Stone
Landing	sq. Ft. Other:
Pointing/Caulking/Patching	lin. Ft.
Step Replacement	lin. Ft.

VEHICLES & EQUIPMENT				
CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #: <u>0003</u>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Truck #:	Tag-Long Trailer	Utility Service Truck
Truck #:	#:	#:	#:	Truck #: <u>0267</u>

Other:

Comments: Poured 1.5 curbs and finished 2 ped ramp. Used 2x4 mats. Laid tile other 4 ped ramp finished yesterday. Set up safety for break and group cleaned up section reported sick, went to Home Depot.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature John J. Miron
Title Crew Leader
Approved By _____
Title Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough S.I.

Day Thur

Date 7/11/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Douglas Olson	CM	6:00	16:30	7	3	<i>SAC</i>	

ON STREET	CROSS STREET
<i>Richmond Terrace</i> <i>Adam Clayton Powell Jr Blvd</i>	<i>Schuyler St</i> <i>w 115 St</i> <i>Chris Snyg</i> <i>Miguel Gary</i>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete 1st 3 2nd 2 5" tall Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>991-835</i>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck

Other:

COMMENTS:

*1st pour Poured 3 yds of curb with Chris Snyg
5" Slump on mix 2nd pour Poured yds 2 of concrete
with Miguel Gary, 5" Slump on mix 2nd pour*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

SAC

Title

Crew Leader

Approved By

Title

Supervisor




**DOT/SI/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Thursday

Date 7-11-13

SIGN IN

Name	Title	In	Out	R.	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30		11	3		
Fevrin Agenord	ACHR	06:00	16:30		10	2		
Frank Messina	ACHR	06:00	16:30		10	2		
Edward Cotton	ACHR	06:00	16:30		10	2		

ON STREET

115 ft <i>Adam C. Powell</i>

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete 2 inches	1.5 Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning (2) 2x4 mats	Sq. Ft.
PREP & CAVE-IN		Expansion Joints	20 Lin. Ft.
Debris Removal	cu. Yds.	Susp Caps	Lin. Ft.
Backfill	cu. Yds.	Caulking	(2) Tube
Asphalt Patch	Tons	Sealant Spray	Gal.
STEP STREETS	cu. Yds.	Sand	Cu. Yds.
Landing	Sq. Ft.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	Other:	
Step Replacement	Lin. Ft.		


VEHICLES **EQUIPMENT**

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Track
Truck #: 0287	Truck #: 0203	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #	#	Truck #: #	#:	Truck #: 0267
Other:				

COMMENTS:

*finished working on the two pedestrian ramps from Yorkway. Poured 1.5 cu.yards.
on 2 pedestrian ramp S/B corner of Adam C. Powell. Set up safety for break at
Gra. cleared up debris and painted 2 safety. sent Eddie Cotton to 149th*

I CERTIFY THAT THE TIME OF THIS EMPLOYEE'S RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature 

Title Crew Leader

Approved By

Title Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Thurs.

Date 7/11/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
J. Buzzelli	M60	05:00	16:00	8	3	_____	
L. Soto	M60	5:00	16:00	7	3	Z. L.	

ON STREET	CROSS STREET
Adam C. Powell Jr.	W. 115 Street (Manhattan)
[REDACTED]	

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	20 Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS: Excavated Put down stone

Grand left safe.

F. Calle.

**DOT/SIM/CITYWIDE CONCRETE
DAIL GANG REPORT**

Borough Queens

Day Fri

Date 7-12-13

SIGN IN

Name	Title	In	Out	Reg. H.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3	<i>Miguel Morel</i>	
Fevrin Agenord	ACHR	06:00	16:30	8	2	<i>Fevrin Agenord</i>	
Frank Messina	ACHR					<i>Frank Messina</i>	A/L
Edward Cotton	ACHR	06:00	16:30	8	2	<i>Edward Cotton</i>	
Gadiel Sales	ACHR	5:00	16:30	8	3	<i>Gadiel Sales</i>	

ON STREET	CROSS STREET
115 th Adam C Powell	S/W CORNER

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	S. Ft. Lumber 4x2x6 4x2x4 Lin. Ft.
Sidewalk Pour	S. Ft. Steel Curb, Straight 20' Lin. Ft.
Curb Prep	L. Ft. Steel Curb, Bull Nose Pieces
Curb Form	60' L. Ft. Detectable Warning Sq. Ft.
Curb Pour	L. Ft. Expansion Joints 10 Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking 3 Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	H. Ft. Other: 1 sheet Ply wood
Pointing/Caulking/Patching	L. Ft.
Step Replacement	L. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Excavator	Large Dump Truck	Light Duty Truck
Truck #: 6289	Truck #: 003	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Frontmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: 0267

Other:

Comments: Caulked Sidewalk on the corner of Adam C Powell and 115th S/W corner. Performed front part of curb 20' back to 115th. Sidewalk extension cut out bedding into 20' int. Side curb cleared up location and resocketed. Safety.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Miguel Morel

Crew Leader

Miguel Morel

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Friday

Date 7.12.13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alen Shinnarshy	T.O.	—	—	—	—	Out	
Quality Sales	ACM	On Miguel gang sheet		→ Queens			

ON STREET	CROSS STREET
115th St & Adam C Powell	

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

On Miguel gang sheet - See Miguel Sheet

**DOT/SIN/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Monday

Date 7-15-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:50	16:30	10	3	<i>Min</i>	
Fevrin Agenord	ACHR						S/L
Frank Messina	ACHR	06:50	16:30	10	2	<i>FC</i>	
Edward Cotton	ACHR	06:00	16:30	10	2	<i>ECC</i>	

ON STREET	CROSS STREET
115 St Adam C Maxwell	

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	
Sidewalk Prep	Sq. Ft.	Lumber 2x4 (10)	2x6 (4) Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	60 Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	20 Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	cu. Yds.	Caulking	Tube
Backfill	cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other: Plywood (2) Sheets	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0289	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck

Other:

Comments: Turned out back of curb, Shoveled out trench, turned 60 linear ft. of back form, cleared up location and recycled soffy. Work back to yard and made shovels, Back filled form work.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Wednesday

Date 7-17-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Horace Johnson	HR	5:00	18:30	8	5		
Tyrone Thomas	HR	6:00	18:30	8	4	J. Thomas	
Thakadial Jamainram	ACHR	5:00	16:30	8	3	J. Jamainram	
Willie Smith	SST	8:00	16:30	7	12	Willie Smith	

ON STREET 58th St Yd.

2nd Ave and 58th St

5th Ave and 124th St

Colin C Powell Blvd 116th St

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	<u>Out-Cali-Soto-Buzzell</u>	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #: 1169117 9875
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS: Willie came out of College Pt Yd. Tyrone did community service with the FEM A people. Robbie paved at two location with the Zim-Mixer. I checked on the crews in Manhattan and worked in yard at 28th St.

DOT
Fax: 718-353-6381
DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Jul 18 2013 06:12am P001/003

Borough Queens

Day Wednesday

Date 7-17-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	S. Name	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	

ON STREET	CROSS STREET
115th Avenue	C Powell

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep 200' Sq. Ft.	Lumber 4x4 Lin. Ft.
Sidewalk Pour Sq. Ft.	Steel Curb, 3" height 20' Lin. Ft.
Curb Prep 30' Lin. Ft.	Steel Curb, Bull Nose Pieces
Curb Form Lin. Ft.	Detachable Wheeling Sq. Ft.
Curb Pour Lin. Ft.	Expansion Joints 20' Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal Cu. Yds.	Caulking Tube
Backfill Cu. Yds.	Sealant Spray Gal.
Asphalt Patch Tons	Sand Cu. Yds.
STEP STREETS Cu. Yds.	Stone Cu. Yds.
Landing Sq. Ft.	Other:
Pointing/Caulking/Patching Lin. Ft.	
Step Replacement Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>0267</u>	Mason Dump Truck Truck #: <u>55503</u>	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: <u>0267</u>

Others:

Comments: Sent Eddie to 29th yard b.l. bid up 20' width steel curb. formed out 200' sq ft sidewalk 3 30' ft curb. spray 2" and 3" ground stripes yesterday. pour of curb. cleaned up location w/ vacuums salt.

I CERTIFY THAT THE TIME OF THE EMPLOYEE'S WORKED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Supervisor _____

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Thur day

Date 7-18-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	6	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30		2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30		2	<i>[Signature]</i>	

ON STREET

115th Adam C. Ponelli

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	sq. Ft.	Ready Mix Concrete	5 Cu. Yds.
Sidewalk Pour	cu. ft.	Lumber	Lin. Ft.
Curb Prep	lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	lin. Ft.	Detachable Warning	Sq. Ft.
	30'	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snaps Caps	
Debris Removal	c. Yds.	Caulking	Tube
Backfill	c. Yds.	Sealant Spray	2 Gal
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	in. Ft.		
Step Replacement	in. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Excavator	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #: <u>5003</u>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Dozer	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u></u>	#:	Truck #:	#:	Truck #: <u>0267</u>
Other:				

COMMENTS:

Powered by conveyor. 20' x 8' sidewalk & 30' x 12' curb, approx 10' tempers. for tomorrow's bmr, went to the Fisher's yard. No parking sign, went inside to yard factory, had to go see. Damaged gate.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

[Signature]

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Brooklyn

Day Friday

Date 7/19/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	14:30	8	1		
Gadiel Salas	ACHR	5:00	14:30	8	1	<i>Gadiel Salas</i>	

ON STREET	CROSS STREET
<i>1153+</i>	<i>Adams & Power St.</i>

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor





**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Bronx

Day Friday

Date 7/19/13

SIGN IN

Name	Title	In	Out	Registers	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	06:15P	14:30	8	1		
Fevrin Agenord	ACHR	06:15P	14:30	8	1		
Frank Messina	ACHR	06:15P	14:30	8	1		
Edward Coton	ACHR	06:15P	14:30	8	1		

ON STREET	CROSS STREET
115 st Avenue C	Powell

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	in. Ft. Steel Curb, Bull Nose Pieces
Curb Form	in. Ft. Detectable Warning Sq. Ft.
Curb Pour	in. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	C. Yds. Caulking Tube
Backfill	C. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	C. Yds. Stone Cu. Yds.
Landing	sq. Ft. Other:
Pointing/Caulking/Patching	in. Ft.
Step Replacement	in. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Dozer	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u>0267</u>	Truck #:	Truck #:	Truck #:	Truck #:

Other:

COMMENTS:

*work to location specified yesterday. Part of
Curbless, Street work to Basin Felt, Curbless
work with backhoe.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Miguel Morel

Title

Crew Leader

Approved By

Title

Supervisor

**DOT/SIM/ CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens:

Day FRIDAY

Date 7-19-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Salvatore Russello	CM	600	1530	7	2	Salvatore Russello	

ON STREET	CROSS STREET
AC Powell	JR 1/5 S

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	S. Ft. Lumber Lin. Ft.
Sidewalk Pour	S. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Ls. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Ls. Ft. Detectable Warning Sq. Ft.
Curb Pour	Ls. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	S. Ft. Other:
Pointing/Caulking/Patching	Ls. Ft.
Step Replacement	Ls. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>3859</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

COMMENTS: work to inspect framing work

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Salvatore Russello

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BK

Day Friday

Date July - 19 - 13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0500	1430	8	1	Milagros Lopez	
Sean Thomas	ACHR	0600	1430	8	3	Sean Thomas	
Rohan Wilkinson	ACHR	0600	1430	8	3	Rohan Wilkinson	
Nicholas Depaola	ACHR	Worked with Calis Gang					

ON STREET	CROSS STREET
ADAM Clayton Powell Blvd	115TH STREET

WORK PERFORMED	MATERIALS USED		
SIDEWALK & CURB	Ready Mix Concrete		
Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Pt.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps		
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other: SAW CUT 140 LIN FT.	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #: 0244
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: 0014

Other:

COMMENTS:

Gang met up at location, we saw cut required area also we posted for Monday's excavation. Made sure location was clean & safe. Due to hot weather condition, returned to the yard early... M. Lopez drove with S. Thomas

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Milagros Lopez

Title

Crew Leader

Approved By

Title

Supervisor

JH

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day TUESDAY

Date 7-23-13

SIGN IN

Name	Title	In	Out	Rel.	OT Hrs.	Signature	Supervisor's Remarks
Frederick Robbins	HR	5:00	16:30	8	3	<i>JH</i>	

ON STREET

*W 115th st
W 5th st*

CROSS STREET

*ADAM Clayton Ave
Bk F 8th & 9th Ave*

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
PREP & CAVE-IN		Expansion Joints	Lin. Ft.
Debris Removal	Cu. Yds.	Snap Caps	Lin. Ft.
Backfill	Cu. Yds.	Caulking	Tube
Asphalt Patch	Tons	Sealant Spray	Gal.
STEP STREETS		Sand	Cu. Yds.
Landing	Sq. Ft.	Stone	
Pointing/Caulking/Patching	Lin. Ft.	Other:	Cu. Yds.
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

*Went to various locations assisted
Queens on various tasks.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAIL / GANG REPORT**

Borough Queens

Day Tuesday

Date 7-23-13

SIGN IN							Supervisor's Remarks
Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	
Miguel Morel	ACHR	05:00	14:30	8	1	<i>[Signature]</i>	
Fevrin Agnord	ACHR	06:00	14:30	8	0	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	14:30	8	0	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	14:30	8	0	<i>[Signature]</i>	

ON STREET	CROSS STREET
115 Adam C. Powell.	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	
Sidewalk Prep	Ready Mix Concrete Cu. Yds.
Sidewalk Pour	Lumber Lin. Ft.
Curb Prep	Steel Curb, Straight Lin. Ft.
Curb Form	Steel Curb, Bull Nose Pieces
Curb Pour	Detectable Warning Sq. Ft.
	Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Sealant Spray Gal.
Asphalt Patch	Sand Cu. Yds.
STEP STREETS	Stone Cu. Yds.
Landing	Other: Lin. Ft.
Pointing/Caulking/Patching	I. n. Ft.
Step Replacement	I. n. Ft.

VEHICLES & EQUIPMENT				
CrewCab Mason Truck Truck #: 0289	Mason Dump Truck Truck #: F M 0003	Fronthoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Excavator Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: 2067 0267
Other:				

COMMENTS:

Went to loc in, spread and tampered stone.
Left a Btr in hole to be used later
Cleaned up loose and reset safety posts on site
for no parking vehicles sign

I CERTIFY THAT THE TIME OF THIS EMPLOYEE'S RECORDS ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Title

Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough QUEENS

Day 7-26-2013

Date WEDNESDAY

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castronovo	CM	1:00	16:70	7	3	M. Castronovo	

ON STREET

ADAM C. POWELL JR. BLVD

CROSS STREET

W 115 ST

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	L. Ft.	Lumber	Ch. Yds.
Sidewalk Pour	L. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	L. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	L. Ft.	Detachable Warning	Sq. Ft.
Curb Pour	L. Ft.	Expansion Joints	Lin. Ft.

PREP & CAVE-IN

Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	S. Pt.	Other:	
Pointing/Caulking/Patching	L. Ft.		
Step Replacement	L. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>703B</u>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Trimmer Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

ON LOCATION POUR 5 CU. YD. OF READY MIX
FOR MIGUEL MORELES CREW

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader Richard Casas

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Wednesday

Date 7/24/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	16:30	11:30	5		
Gadiel Salas	ACHR	5:00	16:30	11:30	5	<i>G. Salas</i>	

ON STREET	CROSS STREET
<u>175 St</u>	<u>Adam Clayton Powell Jr</u>

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	b0	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Cu. Yds.
Landing	Sq. Ft.	Stone	
Pointing/Caulking/Patching	Lin. Ft.	Other:	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#: <i>0004</i>	Truck #: <i>751</i> <i>737</i>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#: <i>5009</i>	Truck #:

Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Thursday

Date 7/25/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	16:30	8	1		
Gadiel Salas	ACHR	6:00	16:30	8		J. Salas	

ON STREET	CROSS STREET
11551	Adams C Power Sv

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone 20 Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#: <i>0004</i>	Truck #: <i>751-754</i> <i>737</i>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#: <i>3009</i>	Truck #:

Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

[Signature]

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day THURSDAY

Date 7-25-2013

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castronovo	CM	6:30	16:30	7	3	<u>M. Castronovo</u>	

ON STREET

ADAM Z. POWELL JR. BLVD

CROSS STREET

W 115 ST

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.

PREP & CAVE-IN

Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck # <u>7038</u>	Mason Dump Truck Truck #:	Boat Shoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Teamster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

ON LOCATION POUR 6 CU.YD. OF READY MIX
FOR MICHELE MORTLES CREW.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Leader

Ronald Est

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Chester

Day Tuesday

Date 7-25-13

SIGN IN

ON STREET

Broadway

CROSS STREET

W 117-6

四〇八

C Clayton Powell

WORK PERFORMANCE

PERFORMED		MATERIALS USED	
SIDEWALK & CURB			
Sidewalk Prep		Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sc. Ft.	Lumber	Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Cu. Yds.
Landing	Sq. Ft.	Stone	
Pointing/Caulking/Patching	Lin. Ft.	Other:	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

VEHICLES & EQUIPMENT				
Crew Cab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <i>1672</i>
Other:				
COMMENTS:	<i>went to various locations</i>			

Other
Books

COMMENTS:

went to various location assisted
Clerk in various tasks.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC
Signature _____
Title _____

Signature

True

Approved By

Tide

Crew Leader

Symmetries

**DOT/SIM/ CITYWIDE CONCRETE
DADY GANG REPORT**

Borough Green

Day Thursday

Date 7-25-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	3	3	<u>MM</u>	
Fevrin Agenord	ACHR	06:00	16:30		2	<u>FA</u>	
Frank Messina	ACHR	06:00	16:30		2	<u>FM</u>	
Edward Cotton	ACHR	06:00	16:30		2	<u>EC</u>	

ON STREET

W. 115 th Street
W. 134 th Street

CROSS STREET

Adam C Powell
Lenox Avenue

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	9. Ft.	Ready Mix Concrete	5 Cu. Yds.
Sidewalk Pour	300	Lumber 3) 2x5	Lin. Ft.
Curb Prep	1. in. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	1. in. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	1. in. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	40 Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	C. Yds.	Caulking	Tube
Backfill	C. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	lin. Ft.		
Step Replacement	in. Ft.		

VEHICLES / EQUIPMENT

CrewCab Mason Truck Truck #: <u>0289</u>	Mason Dump Truck Truck #: <u>0003</u>	Jackhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: <u>0267</u>

Other:

Comments: Poured 5 cubic yard cement 300 sq ft sidewalk. Grade and trowel and form for tomorrow pour. Saw cut 3 more places. Set up probe team and to get correct concrete grade. Leave up location as needed softy.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

John A. Ryan

Title

Crew Leader

Approved By

J. Ryan

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day FRIDAY

Date 7-26-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Frederick Robbins	HR	5:00	16:32	8	3	ZPR	

ON STREET

CROSS STREET

<u>W 115th</u>	<u>A 1st Avenue</u>
<u>W 74th</u>	<u>Bkly 1st Avenue</u>

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sc. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sc. Ft.	Lumber	Lin. Ft.
Curb Prep	Sc. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Lin. Ft.
Backfill	Cu. Yds.	Sealant Spray	Tube
Asphalt Patch	Tons	Sand	Gal.
STEP STREETS		Cu. Yds. Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

Crew Cab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Tow Master Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <u>1672</u>
Other:				

COMMENTS:

went to location assigned
Crews in pouring concrete -

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title Crew Leader

Approved By

Title Supervisor

**DOT/SIM/C TYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day FRIDAY

Date 7-26-2013

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castranova	CM	6:00	16:30	7	3	R. Castranova	

ON STREET

ADAM C. POWELL JR BLVD

CROSS STREET

6115 ST

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB	Ready Mix Concrete	5 Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight
Curb Prep	Lir. Ft.	Steel Curb, Bull Nose
Curb Form	Lir. Ft.	Detectable Warning
Curb Pour	Lir. Ft.	Expansion Joints
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking
Backfill	Cu. Yds.	Sealant Spray
Asphalt Patch	Tons	Sand
STEP STREETS	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Track Truck #: <u>7038</u>	Mason Dump Truck Truck #: _____	Bob khoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Terexmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other: _____

COMMENTS:

ON LOCATION FOUND 5 CU. YD. OF READY MIX
FOR MICHAEL'S CREW

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Fri Aug Date 7-26-13

SIGN IN

Name	Title	In	Out	Reg. H.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:50	16:30	8	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	

ON STREET	CROSS STREET
115 St	<i>Adam Powell</i>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete 5 Cu. Yds.
Sidewalk Prep	1 Ft. Lumber 4 2x4 Lin. Ft.
Sidewalk Pour	300 Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	1 Ft. Steel Curb, Bull Nose Pieces
Curb Form	1 Ft. Detectable Warning Sq. Ft.
Curb Pour	1 Ft. Expansion Joints 60 Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking 3 Tube
Backfill	Cu. Yds. Sealant Spray 2 Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	1 Ft. Other:
Pointing/Caulking/Patching	1 Ft.
Step Replacement	1 Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Herrick	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
0289	6203			
Medium Dump Truck	Hydraulic Excavator	Driver	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
				0267

Other:

Comments: *Poured 50' sidewalk and finished, sprayed 2 gal. Sealant, Caulked yesterday's pour, cleaned up trench and reset curb, went to back and my truck and posted for tomorrow.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By _____

Title Supervisor

**DOT/SIN/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Monday

Date 7-29-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	3	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	2	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	2	2	<i>[Signature]</i>	
Edward Cotton	ACHR						

ON STREET

1/8 ST Adam C. Powell

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep		Ready Mix Concrete	5 Cu. Yds.
Sidewalk Pour	300 sf.	Sq. Ft. Lumber	Lin. Ft.
Curb Prep		Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Form		Sq. Ft. Steel Curb, Bull Nose	Pieces
Curb Pour		Sq. Ft. Detectable Warning	1 1/2 x 2 mat Sq. Ft.
		Sq. Ft. Expansion Joints	50 Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal		Cu. Yds. Caulking	3 Tube
Backfill		Cu. Yds. Sealant Spray	3 Gai.
Asphalt Patch		Tons Sand	Cu. Yds.
STEP STREETS		Cu. Yds. Stone	
Landing		3 Ft. Other:	Cu. Yds.
Pointing/Caulking/Patching		in. Ft.	
Step Replacement		in. Ft.	

VEHICLES		EQUIPMENT		
CrewCab Mason Truck Truck #: <u>0289</u>	Mason Dump Truck Truck #:	Rockhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Crusher	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: <u>0267</u>
Other:				

COMMENTS:

Poured 5 yards concrete, 300 sq ft. Sidewalks with Red reg. and 1(2x5) mat. Sealed with Caulking Expansion Joint. Spray. Sealed. Set up location and tools.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By

Title Supervisor

**DOT/SIM/ CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Crown

Day 7-29-13

Date Monday

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Frederick Robbins	HR	52	162	8	3	<i>27/7/13</i>	

ON STREET

CROSS STREET

(W) 115 Va

No man stay down forever

Glen Gate 9th

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep		Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
	Cu. Yds.	Stone	Cu. Yds.
STEP STREETS		Sq. Ft.	Other:
Landing	Sq. Ft.		
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Tow Master Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				<i>1672</i>

COMMENTS:

*work to location
Assist in pouring concrete*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Supervisor

Title

Boro

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BKlyn

Day Mon.

Date 7-29-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Lawrence Johnson	MGO	5:00	16:30	8	3	L. Johnson	
Julio Samayoa	ACHR	5:00	16:30	8	3	Julio Samayoa	
T. Thomas	IT-R	6:00	16:30	8	2		

ON STREET	CROSS STREET	
GONZALEZ PL & RODNEY		
GIENDALE YR		
ADAM CILATOV POWELL & 115 ST		—SOY.SSS

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	(22) Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	(18) Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS: EXCAVATION & SPREADER STONE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Tuesday

Date 7-30-13

SIGN IN

Name	Title	In	Out	Reg.	S.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	06:00	18:30	5		5	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	18:30	8		4	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	18:30	1		4	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	18:30	2		4	<i>[Signature]</i>	

ON STREET

*(15 * Area Cleaned.
Spring field yard.)*

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	: Ft.	Ready Mix Concrete	3 Cu. Yds.
Sidewalk Pour	: Ft.	Lumber <i>(3x4 2x6)</i>	Lin. Ft.
Curb Prep	: Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	: Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	: Ft.	Detectable Warning <i>1 2x4</i>	Sq. Ft.

PREP & CAVE-IN

Debris Removal	C Yds.	Caulking	6 Tube
Backfill	C Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	C Yds.	Stone	Cu. Yds.
Landing	: Ft.	Other: 3 sheets Ply wood.	
Pointing/Caulking/Patching	: Ft.		
Step Replacement	: Ft.		

VEHICLES / EQUIPMENT

CrewCab Mason Truck Truck #: 0289	Mason Dump Truck Truck #: 0003	Dickhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: 0267

Other:

Comments: Poured 3 cynd cement, Red ramp. 17' long. was 10' wide, finished
carrying neck down, cleaned up all location as needed etc. Then went to
Spring field yard and Box set up ~~together~~ together with Plymouth 2x4.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By _____

Title Supervisor

**DOT SIDEWALK INSPECTION MANAGEMENT
CITYWIDE CONCRETE PROGRAM - DAILY GANG REPORT**

Borough: Brooklyn Date: 7-30-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
F. DODRINS	HHR	5:22	162	8	3	<u>7/30/13</u>	
Total Hrs.							

Location	From	To
W 175 St	A 7th Avenue	Park
Central Park		

STEP STREETS		PREP & CAVE-IN	
Coping	Lin.	Fill	Cu. Yd.
Sidewalk	Sq. Ft.	Debris	Cu. Yd.
Walls	Cu. Ft.	Opening	Sq. Yd.
Pointing & Patching	Lin.		
MATERIAL USED		CURB WORK	
Ready Mix	Cu. Ft.	Sidewalk Prep	Sq. Ft.
Hand Mix	Cu. Ft.	Sidewalk Pour	Sq. Ft.
Cement	Bags	Curb Prep	Lin. Ft.
Sand/Stone	Cu. Ft.	Curb Pour	Lin. Ft.
Lumber	Lin.	Paving Block	Unit
Expansion Joint	Unit	Forming	Lin. Ft.

VEHICLE & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Excavator #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Lowmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <u>1672</u>
Other:				

Comments: work so far was checked in by Green

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF THE CITY OF NEW YORK

Signature _____

Title Supervisor

Approved By _____

Title Citywide Concrete Program

**DOT/SIM/CITYWIDE CONCRETE
DAIL / GANG REPORT**

Borough QUEENS

Day TUES, 94

Date 7-30-2013

SIGN IN

Name	Title	In	Out	Reg. H.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castrovovo	CM	7:00	16:20	7	3	<i>M. Castrovovo</i>	

ON STREET

ADAM C. POWELL JR. BLVD

CROSS STREET

W 115 ST

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep

MATERIALS USED

Ready Mix Concrete 4 Cu. Yds.

Sidewalk Pour

S Ft.

Lin. Ft.

Curb Prep

S Ft.

Lin. Ft.

Curb Form

L Ft.

Pieces

Curb Pour

L Ft.

Sq. Ft.

PREP & CAVE-IN

Debris Removal

Ready Mix Concrete

Backfill

Cu Yds.

Tube

Asphalt Patch

Cu Yds.

Gal.

STEP STREETS

Cu Yds.

Cu. Yds.

Landing

S Ft.

Other:

Pointing/Caulking/Patching

L Ft.

Step Replacement

L Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>7038</i>	Mason Dump Truck Truck #:	B Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	T Excavator #:	Tag-A-Long Traiter #:	Utility Service Truck Truck #:

Other:

COMMENTS:

ON LOCATION POUR 4 CU. YD. OF READY MIX
AND INSTALLED 10 SQ. FT. OF DETECTABLE WARNING
MATS FOR MILE MOPACES CREW.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT / THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader *Robert C. Cottino*

Title

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day 7-31-13

Date Wednesday

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Frederick Robbins	HR	7:22	7:22	0	3	21M	

ON STREET

W 115 St
Glen Oaks

CROSS STREET

Open play lot
powell

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sc. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
		Stone	Cu. Yds.
STEP STREETS		Other:	
Landing	Sq. Ft.		
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

Crew Cab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Tow Mater Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				1672


COMMENTS:

Client location

Assist in pouring concrete

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC


Signature


Crew Leader

Title

Approved By

Title


Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens,

Day Wednesday,

Date 7-31-13

SIGN IN

Name	Title	In	Out	Reg.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	E	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	E	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	E	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	E	2	<i>[Signature]</i>	

ON STREET	CROSS STREET
115th Avenue (Powell)	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete 3 Cu. Yds.
Sidewalk Prep	sq. Ft. Lumber Lin. Ft.
Sidewalk Pour 275'	sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	in. Ft. Steel Curb, Bull Nose Pieces
Curb Form	in. Ft. Detectable Warning 1 2x4 Sq. Ft.
Curb Pour	in. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	cu. Yds. Caulking Tube
Backfill	cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	cu. Yds. Stone Cu. Yds.
Landing	sq. Ft. Other:
Pointing/Caulking/Patching	in. Ft.
Step Replacement	in. Ft.

VEHICLES		EQUIPMENT		
CrewCab Mason Truck Truck #: 0289	Mason Dump Truck Truck #: 02203	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Cowmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: 0267

Other:

Comments: *Poured 3 curbs - finished back up work 1 2x4
detectable warning not cleaned up together and
wore safety belt & safety for break out group.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

SSS only Alvaro Arias

Fax 17184205208

Aug 1 2013 06:27am P002/009

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Webster
A. Arias

Borough SII Day Wed Date 7/31/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR						A/C
Jason James	HR	600	16:30	8	2	not SSS	not SSS
Alvaro Arias	HR	0600	1530	8	2	A.A.	100% SSS

not SSS →

ON STREET	CROSS STREET
100 CP Blvd	113 [±] St
Cushing Ave	E 193 [±] St

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal <u>3</u>	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: <u>754T</u> <u>752T</u>	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS: removed debris from these locations and picked up stone.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

Orizzi

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Thursday

Date 8/1/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	16:30	8	3		
Gadiel Salas	ACHR	5:00	16:30	8	3	<i>G. Salas</i>	
Isaac James	HP	6:00	16:30	8	2		

ON STREET	CROSS STREET
<i>115 St</i>	<i>Adam C Power Jr.</i>

WORK PERFORMED	MATERIALS USED
SIDWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal <i>60</i>	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch <i>--</i>	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone <i>40</i> Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#: <i>Towmaster 0004</i>	Truck #: <i>737</i>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#: <i>5009</i>	Truck #:

Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Leader



Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough SIDay Thur.Date 8/1/13**SIGN IN**

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR						OUT ALL
Jason James	HR	6:00	16:30	8	2	<i>James</i>	
Alvaro Arias	HR	6:00	14:30	8		<i>Arias</i>	

ON STREET	CROSS STREET
12 Ave	E 114 th St
ACP Blvd	115 th St

SOY. SSS

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	3 Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Cu. Yds.
Landing	Sq. Ft.	Stone	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #: 754 752	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

Al worked with Ron's crew. Jason removed debris and dumped st Evergreen

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader
E.J.H.
Supervisor

**DOT/SI 4/CITYWIDE CONCRETE
D. ILY GANG REPORT**

Borough Queen

Day THURSDAY

Date 8-1-2013

SIGN IN

ON STREET

ADAM C. POWELL JR. BLOWD
101 ST

CROSS STREET

STREET
W 11557
158 AC

WORK PERFORMED

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	lin. Ft.		
Step Replacement	lin. Ft.		

VEHICLES & EQUIPMENT

VEHICLES & EQUIPMENT				
Crew Cab Mason Truck Truck #: 7038	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	CraneMaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

ON THE ABOVE LOCATION AT WORK IS
ON SCHEDULE 101ST LOCATION READY FOR
CURB POIN.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT, & THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC.
Signature _____
Title _____

Signature

118

Approved By

Title

Crew Leader Michael Corr Supervisor _____

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough *Rein.*

Day *TH*

Date *8-1-13*

SIGN IN

Name	Title	In	Out	Reg Hrs	OT Hrs.	Signature	Supervisor's Remarks
Frederick Robbins	HR	<i>00</i>	<i>16 2</i>		<i>?</i>	<i>F.R.</i>	

ON STREET

ON STREET	CROSS STREET
<i>W 115 St</i>	<i>A Drw Clinton</i>
<i>101 75 St</i>	<i>Fire w C</i>

WORK PERFORMED

SIDEWALK & CURB

MATERIALS USED

Sidewalk Prep	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Lumber	Lin. Ft.
Curb Prep	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft. Detectable Warming	Sq. Ft.
	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

Crew Cab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Tow Master Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <i>1672</i>
Other:				

COMMENTS:

work in location on 115th crew in preparing for forming.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Manhattan

Day TUESDAY

Date 08-01-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	—	—	—	—	<i>Miguel</i>	SL
Fevrin Agenord	ACHR	5:00	14:30	8	1	<i>Fevrin</i>	
Frank Messina	ACHR	6:00	14:30	8	1	<i>Frank</i>	
Edward Cotton	ACHR	6:00	14:30	8	1	<i>Edward</i>	

ON STREET <u>ADAM C. Powell</u>	CROSS STREET <u>W-115</u>

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Lin. Ft.
Backfill	Cu. Yds.	Sealant Spray	Tube
Asphalt Patch	Tons	Sand	Gal.
STEP STREETS		Cu. Yds.	
Landing	Cu. Yds.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Sq. Ft.	Other:	
Step Replacement	Lin. Ft.		
	Lin. Pt.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

*Caulking 85 Lin FT, Grade and Tempered 560 SQ FT
Set up Safety*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Age 7/25

Title

Crew Leader

Approved By

J.W.

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BK

Day Thursday

Date Aug - 1 - 13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0500	1630	8	3		
Sean Thomas	ACHR	0600	1630	8	2	<u>Sean Thomas</u>	
Rohan Wilkinson	ACHR	0600	1430	8	0	<u>Rohan Wilkinson</u>	
Nicholas Depaola	ACHR	Worked with Cali				<u>Nicholas Depaola</u>	

ON STREET

115 ST
W 74 ST

CROSS STREET

ADAM CLAYTON POWELL
BROADWAY

WORK PERFORMED		MATERIALS USED		
SIDEWALK & CURB		Ready Mix Concrete		
Sidewalk Prep	Sq. Ft.	Lumber		Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight		Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose		Pieces
Curb Form	Lin. Ft.	Detectable Warning		Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints		Lin. Ft.
PREP & CAVE-IN		Snap Caps		
Debris Removal	Cu. Yds.	Caulking		Tube
Backfill	Cu. Yds.	Sealant Spray		Gal.
Asphalt Patch	2 Y2	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:		
Pointing/Caulking/Patching	Lin. Ft.			
Step Replacement	Lin. Ft.			

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #: <u>PICKUP</u> <u>7087</u>	Truck #: <u>0014</u> <u>4</u> <u>HOT BOX</u>
Medium Dump Truck	Hydraulic Excavator	Townmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>0244</u>

Other:

COMMENTS:

Ruben W. drove to harper yard for asphalt while the rest of gang met up at location we asphalt both location. Made sure they were clean and safe. Michael Graf worked with BKlyn gang....

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Milagros Lopez

Title

Crew Leader

Approved By

JL

Title

Supervisor

**DOT/SI /CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough QUEENS

Day FRI MAY

Date 8-2-2013

SIGN IN

Name	Title	In	Out	Re.	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castronovo	CM	6:00	16:30		7	3	<i>M. Castronovo</i>	

ON STREET	CROSS STREET
<i>ADAM C. POWELL JR. BLVD</i>	<i>W 15 ST</i>

WORK PERFORMED	MATERIALS USED		
SIDEWALK & CURB			
Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	in. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	in. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	in. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN			
Debris Removal	C. Yds.	Caulking	Tube
Backfill	C. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	3 BALS Cu. Yds.
STEP STREETS	C. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	PORTLAND CEMENT 1 BAG
Pointing/Caulking/Patching	in. Ft.	MORTARACEMENT 1 BAG	
Step Replacement	in. Ft.	50 BRICKS	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>703B</i>	Mason Dump Truck Truck #:	Excavator #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Jobmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

ON THE ABOVE LOCATION BASE EACH BASE FOR STORM DRAIN USED 50 BRICK 3 BAG OF SAND 1 BAG OF PORTLAND 1 BAG OF MORTAR FOR MICHAEL MIRALLES CREW

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT / THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader *R. L. Lee Jr.*

Supervisor

**DOT/NYC/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Green

Day Fri July

Date 8-2-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:07	16:30	1	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR					<i>[Signature]</i>	A/L
Frank Messina	ACHR	06:00	16:30	2	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	2	2	<i>[Signature]</i>	

ON STREET

115 Adams C Powell

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber <u>5x2 x 6</u>	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	20' Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	10 Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other: Portland 1 Bag, Mortar 1 Bag,	
Pointing/Caulking/Patching	Lin. Ft.	3 Sawn, 5C Bricks,	
Step Replacement	Lin. Ft.	Bricks	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	#:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
<u>62-89</u>					
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	#:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
					<u>62-67</u>

Other:

Cut out new ramp into 1/2 ft steel curb, and set it up. Raised street. Stroma Driveway with 1/2 ton of rock. Dug out curb trench, cleaned up trench and reset 1/2 ft. back to original point. and took it back to College Point.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT

I CERTIFY THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Supervisor

Approved By

Title

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Friday

Date 8/2/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TQ	5:00	16:30	8	3		
Gadiel Salas	ACHR	5:00	16:30	8	3	<u>G Salas</u>	
Jason James	HS	6:00	16:30	8	2		

ON STREET	CROSS STREET
<u>115 St</u>	<u>Adam C Power St</u>

WORK PERFORMED	MATERIALS USED	
SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #: <u>0004</u>	Large Dump Truck Truck #: <u>7541</u> <u>737 T</u>	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #: <u>5009</u>	Utility Service Truck Truck #:

Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader (Signature)

Title

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Friday.

Date 8-2-13

SIGN IN							Supervisor's Remarks
Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	
Frederick Robbins	HR	5:00	16:00	8	3	FR	

ON STREET	CROSS STREET
W 115th Street	Clinton Avenue
108 1/2 Avenue	Powell Street

WORK PERFORMED	MATERIALS USED	
SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <u>1622</u>

Other:

COMMENTS:

went to location
assisted crew in various tasks

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Crew Leader _____

Supervisor _____

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough

Green;

Day Saturday.

Date 8/3/13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	06:00	14:30		8		
Fevrin Agenord	ACHR						A/L
Frank Messina	ACHR	06:00	14:30		8		
Edward Cotton	ACHR	06:00	14:30		8		
Luis Soto	ACRH	06:00	14:30		8		

ON STREET

115 ft from C Powell

CROSS STREET

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	sq. Ft.	Lumber 15' 2 x 6	Lin. Ft.
Sidewalk Pour	sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	150'	lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	C Yds.	Caulking	Tube
Backfill	C Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		C Yds. Stone	16 Cu. Yds.
Landing	sq. Ft.	Other: Ply wood (1)	
Pointing/Caulking/Patching	sq. Ft.		
Step Replacement	lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>2289</u>	Mason Dump Truck Truck #: #:	Backhoe #:	Large Dump Truck Truck #: #:	Light Duty Truck Truck #: #:
Medium Dump Truck Truck #: #:	Hydraulic Excavator #:	Jobmaster Truck #: #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <u>0267</u>

Other:

COMMENTS:

formed out 150 ft of front curv. crooked and
twisted, cleaves e. leading w/ rest sandy.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC.

Signature

Title

Approved By

Tide

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough

Crew

Day

SAT

Date 8-3-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Frederick Robbins	HR	<u>6:00</u>	<u>14:00</u>		<u>8</u>	<i>JPL</i>	

ON STREET	CROSS STREET
<u>W 115th</u>	<u>Adam Clayton Powell</u>
<u>108th</u>	<u>158th Avenue</u>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #: <i>1672</i>
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

work to location assisted

COMMENTS:

Crews on various tasks

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Leader

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough

SI

Day

Monday

Date

8/5/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR						A/C
Jason James	HR						SICK
Alvaro Arias	HR	0600	1430	8			11/13/2013

ON STREET	CROSS STREET
ACP Blvd	W 115 th St

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #: 0001	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

Helped crew frame curb forms.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Lead

Approved By

Title

Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAD Y GANG REPORT**

Borough Queens

Day mon 1a)

Date 8-5-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR					<i>[Signature]</i>	
Frank Messina	ACHR	05:00	16:30	8	2	<i>[Signature]</i>	
Edward Cotton	ACHR	05:00	16:30	8	2	<i>[Signature]</i>	
Al Aris	MR.	06:00	16:30	8	1	<i>[Signature]</i>	

ON STREET	CROSS STREET
115 <i>St</i> <i>John & Powell</i>	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	q. Ft. Lumber Lin. Ft.
Sidewalk Pour	q. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	I. n. Ft. Steel Curb, Bull Nose Pieces
Curb Form	I. n. Ft. Detectable Warning Sq. Ft.
Curb Pour	I. n. Ft. Expansion Joints 20' Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	C. Yds. Caulking Tube
Backfill	C. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	C. Yds. Stone Cu. Yds.
Landing	c. Ft. Other: Plywood (6) Sheets
Pointing/Caulking/Patching	I. n. Ft. 20' 2x4 lumber
Step Replacement	I. n. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: 0289	Mason Dump Truck Truck #:	Excavator Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: 0267

Other:

Comments: Turned 170' into a back form, made the form on back used 6 sheets plywood w/ 1 (20) 2x4, back filled form, cleared up location w/ a set soft. ~~0267~~ went back to the yard and cleared up truck. 0267.

I CERTIFY THAT THE TIME ON THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

(Signature)

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Monday

Date 8-5-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Frederick Robbins	HR	5:00	16:2	8	3	<i>[Signature]</i>	

ON STREET

<i>W 115th Street</i>	<i>CROSS STREET</i>
<i>108th Street</i>	<i>Clayton Powell Avenue</i>

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	Lin. Ft.
PREP & CAVE-IN		MATERIALS USED	
Debris Removal	Cu. Yds.	Snap Caps	Lin. Ft.
Backfill	Cu. Yds.	Caulking	Tube
Asphalt Patch	Cu. Yds.	Sealant Spray	Gal.
	Tons	Sand	Cu. Yds.
STEP STREETS		MATERIALS USED	
Landing	Cu. Yds.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Sq. Ft.	Other:	
Step Replacement	Lin. Ft.		
	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <i>1672</i>
Other:				

COMMENTS:

*went to location
assisted crew in various
tasks*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Crew Leader _____

Supervisor _____

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Tue

Date 7-6-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Frederick Robbins	HR	5:20	16:22	8	3	<i>FHR</i>	

ON STREET

CROSS STREET

<i>W 115th</i>	<i>ADAM CLAYTON</i>
<i>108</i>	<i>AVENUE</i>

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <i>1672</i>
Other:				

COMMENTS:

went to location

assisted crews on various tasks

tasks

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Supervisor

Title

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Wednesday

Date 8-7-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3	<i>[Signature]</i>	Went to location
Fevrin Agenord	ACHR	06:00	16:30		2	<i>[Signature]</i>	Crew was pouring concrete. All looks good.
Frank Messina	ACHR	06:00	16:30		2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
							J.T.

ON STREET

115 St At Av C Powell

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep		Ready Mix Concrete	6 Cu. Yds.
Sidewalk Pour		Ft. Lumber	Lin. Ft.
Curb Prep		Ft. Steel Curb, Straight	Lin. Ft.
Curb Form		I. Ft. Steel Curb, Bull Nose	Pieces
Curb Pour	175' I. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	20 Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cy Yds.	Caulking	Tube
Backfill	Cy Yds.	Sealant Spray	4 Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	I. Ft.	Other:	
Pointing/Caulking/Patching	I. Ft.		
Step Replacement	I. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Hackhoe	Large Dump Truck	Light Duty Truck
Truck #: 0287	Truck #: 0003	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Driver	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:	#:	Truck #: #:	#:	Truck #: 0267

Other:

COMMENTS:

Poured 175' unit curb, cleaned up location and routes so dry

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough S. I.

Day wednesday

Date 8/17/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Douglas Olson	CM	6:00	16:30	7	3	<i>SJL</i>	

ON STREET

ON STREET	CROSS STREET
<i>ADAM Clayton Powell SR Blvd</i>	<i>mejel 300</i>

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
PREP & CAVE-IN		Expansion Joints	Lin. Ft.
Debris Removal	Cu. Yds.	Snap Caps	Lin. Ft.
Backfill	Cu. Yds.	Caulking	Tube
Asphalt Patch	Tons	Sealant Spray	Gal.
STEP STREETS		Sand	Cu. Yds.
Landing	Sq. Ft.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	Other:	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>991-835</i>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

*POURED 6 yards of concrete with mejal
gang .5" Slump on concrete mix ((Curb))*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

SJL

Title

Crew Leader

Approved By

Title

Supervisor

DOT
DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Fax: 718-353-6381

Aug 9 2013 07:10am P003/008

Borough Queens

Day Wednesday

Date

8/7/13

dup

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	16:30	8	3	<i>Taranto</i>	

ON STREET

College Point yard (Qu)
Adam J. Powell Blvd & 115 St (man)

CROSS STREET

158 Ave at 101 St (Qu)

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight	Lin. Pt.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Lin. Ft.
Backfill	Cu. Yds.	Sealant Spray	Tube
Asphalt Patch	Tons	Sand	Gal.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

Crew Cab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

checked on crews at locations worked on city time,

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

✓ Webster

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day THURSDAY

Date 8-8-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	O/H Hrs.	Signature	Supervisor's Remarks
Salvatore Russello	CMT	600	1530	7	2	<u>Salvatore Russello</u>	

ON STREET	CROSS STREET	SOY, SSS
<u>Webster Av</u>	<u>CLAY ST</u>	
<u>AC Powell</u>	<u>SR 6115 ST</u>	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep Ft.	Lumber Lin. Ft.
Sidewalk Pour Ft.	Steel Curb, Straight Lin. Ft.
Curb Prep I. Ft.	Steel Curb, Bull Nose Pieces
Curb Form I. Ft.	Detectable Warning Sq. Ft.
Curb Pour I. Ft.	Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal Cu. Yds.	Caulking Tube
Backfill Cu. Yds.	Sealant Spray Gal.
Asphalt Patch Tons	Sand Cu. Yds.
STEP STREETS	Stone Cu. Yds.
Landing Ft.	Other:
Pointing/Caulking/Patching Lin. Ft.	
Step Replacement I. Ft.	

VEHICLES & EQUIPMENT				
CrewCab Mason Truck Truck #: <u>3859</u>	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Teamster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

WENT TO THE ABOVE LOCATION
TO INSPECT PREVIOUS WORK

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader
Salvatore Russello

Supervisor

**DOT/SI: I/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day THURSDAY

Date 8-8-2013

SIGN IN

Name	Title	In	Out	Re.	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castronovo	CM	6:00	15:30		9	2	<u>M. Castronovo</u>	

ON STREET

ADAM C. POWELL JR. BLVD

CROSS STREET

W 115 ST

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep

Sidewalk Pour

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete

Cu. Yds.

Sq. Ft.

Lumber

Lin. Ft.

Sq. Ft.

Steel Curb, Straight

Lin. Ft.

Lin. Ft.

Steel Curb, Bull Nose

Pieces

in. Ft.

Detectable Warning

Sq. Ft.

in. Ft.

Expansion Joints

Lin. Ft.

Snap Caps

Lin. Ft.

cu. Yds.

Caulking

Tube

cu. Yds.

Sealant Spray

Gal.

Tons

Sand

Cu. Yds.

cu. Yds.

Stone

Cu. Yds.

Sq. Ft.

Other:

in. Ft.

in. Ft.

VEHICLES / EQUIPMENT

CrewCab Mason Truck Truck #: <u>7033</u>	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Teamster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

ON THE ABOVE LOCATION ALL WORK IS
ON SCHEDULE.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Michele Castronovo

Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Thursday

Date 9-8-13

SIGN IN

Name	Title	In	Out	Rep.	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	14:30			1	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	14:30				<i>[Signature]</i>	
Frank Messina	ACHR	06:00	14:30				<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	14:30				<i>[Signature]</i>	

ON STREET	CROSS STREET
115 st	<i>Adrian C Powell</i>

WORK PERFORMED	MATERIALS USED		
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.		
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	in. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	in. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	in. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.		
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	in. Ft.		
Step Replacement	in. Ft.		

VEHICLES		EQUIPMENT		
CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>0209</i>	Truck #: <i>0002</i>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <i>0262</i>
Other:				

COMMENTS:

*Went to location and striped yesterday's pour.
Then went to Adrine and helped install manhole.
Went back to yard and cleaned up truck.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]
Title Crew Leader

Title

Approved By

[Signature]
Title Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Brooklyn

Day Fri.

Date 8-9-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Lawrence Johnson	MGO	5:00	1480	8	1	<i>L. Johnson</i>	
Julio Samayoa	ACHR	5:00	1430	8	1	<i>Julio Samayoa</i>	
T Thomas	HHR	600	1430	8			

ON STREET	CROSS STREET
<i>ADAM CLAYTON POWELL JR & 115 ST</i>	

WORK PERFORMED	MATERIALS USED		
SIDWALK & CURB	Ready Mix Concrete Cu. Yds.		
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.		
Debris Removal	6 Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	40 Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	Truck# 0006	Truck#736T <i>7517</i>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#5004	Truck #:
Other:				

COMMENTS:

EXCAVATION & SPREADING STONE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/ CITYWIDE CONCRETE
DAD Y GANG REPORT**

Borough

Queens

Day

Friday

Date

8-9-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	14:30	8		<u>MM</u>	
Fevrin Agenord	ACHR	06:00	14:30	8		<u>Fevrin Agenord</u>	
Frank Messina	ACHR					<u>Frank Messina</u>	
Edward Cotton	ACHR	06:00	14:30	8		<u>Edward Cotton</u>	S/L

ON STREET

CROSS STREET

115th Adam Powell

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep		Ft. Lumber	Lin. Ft.
Sidewalk Pour		Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	I. n. Pt.	Steel Curb, Bull Nose	Pieces
Curb Form	I. n. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	I. n. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cy Yds.	Caulking	Tube
Backfill	Cy Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cy Yds. Stone	Cy Yds.
Landing	I. n. Ft.	Other:	
Pointing/Caulking/Patching	I. n. Ft.		
Step Replacement	I. n. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Teamster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>0267</u>

Other:

COMMENTS:

Setup site. Ice melt at gang. Spread 40 cabs
800 stone. clear up debris and needed
snow.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Supervisor

Title

**DOT/SIM CITYWIDE CONCRETE
DAD Y GANG REPORT**

Borough Queens

Day Monday

Date 8/12/13

SIGN IN

Name	Title	In	Out	Reg.	Is.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8		3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	8		2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	8		2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	8		2	<i>[Signature]</i>	

ON STREET

CROSS STREET

115 82nd Avenue (Blank)

WORK PERFORMED

SIDEWALK & CURB

		MATERIALS USED	
Sidewalk Prep	sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	sq. Ft.	Lumber 4x6x6 (8) 2x4	Lin. Ft.
Curb Prep	lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	Lin. Ft.

PREP & CAVE-IN

Debris Removal	C Yds.	Caulking	Tube
Backfill	C Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
	C Yds.	Stone	Cu. Yds.
STEP STREETS			
Landing	ft.	Other: 10 Br. 2 W.	
Pointing/Caulking/Patching	in. Ft.		
Step Replacement	in. Ft.		

VEHICLES / EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>0289</i>	Truck #: <i>02003</i>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Excavator	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <i>0267</i>

Other:

COMMENTS:

*formed out inner part of Island, used 4x6x6 & 2x4.
cycled and Tamped, cleaned up location and
resurfaced surface.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By *[Signature]*

Title Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Tues. Aug

Date 8-13-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	14:30			<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	14:30			<i>[Signature]</i>	
Frank Messina	ACHR	06:00	14:30			<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	14:30			<i>[Signature]</i>	

ON STREET	CROSS STREET
<i>Adam Clayton Powell Blvd & 155th</i>	

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	in. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	in. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	in. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	C Yds.	Caulking	Tube
Backfill	C Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		C Yds.	Cu. Yds.
Landing	sq. Ft.	Stone	Cu. Yds.
Pointing/Caulking/Patching	in. Ft.		
Step Replacement	in. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Excavator #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Jobmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <i>0267</i>

Other:

Comments: *Plan Day went to location needed safety unit back to yard cleaned up truck, debris removed from 44 Drive.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By *[Signature]*

Title Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough S.I.

Day Wed

Date 8/14/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Douglas Olson	CM	6:00	16:30	7	3	<i>SAC</i>	<i>Rejected 1st Krug's Truck Over 90 min from plant</i>

ON STREET	CROSS STREET
<i>Adam Clayton Powell Jr Blvd</i>	<i>115 St</i>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete <u>8</u> Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>991-835</u>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

Comments: Poured 8 yds of concrete with Miguel Gang. 5" Slump on concrete mix.

I CERTIFY THAT THE TIME OF THE EMPLOYEE RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

SAC

Title

Crew Leader

Approved By

Title

Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queen

Day Wed, 25 July.

Date 6-14-13

SIGN IN

Name	Title	In	Out	Reg	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:50	16:30		10	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:50	16:30		10	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30		10	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:20	16:30		10	2	<i>[Signature]</i>	

ON STREET	CROSS STREET
115 th Astor C Penalt	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete 8 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour 300'	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	in. Ft. Steel Curb, Bull Nose Pieces
Curb Form	in. Ft. Detectable Warning (1) 2x4 mat. Sq. Ft.
Curb Pour	in. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	C. Yds. Caulking Tube
Backfill	C. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	C. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	in. Ft.
Step Replacement	in. Ft.

VEHICLES		EQUIPMENT		
CrewCab Mason Truck Truck #: 0289	Mason Dump Truck Truck #: 0203	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #: 4:	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck Truck #: 0267

Other:

Comments: Poured 8 curbs and cement. Side walk in the restaurant used 1x4x5 warning mat cleaned up location and洒水器 (洒水器)

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor


**DOT/SIN // CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Wednesday

Date 8/14/13

SIGN IN

Name	Title	In	Out	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	15:30	8	2		

ON STREET

College Point Yard (Q) U
Columbus Ave & 110 St - 73rd
Ashen C Powell Jr Blvd & 115th

CROSS STREET

Queensplant (Q)

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Cu. Yds.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Cu. Yds.

PREP & CAVE-IN

Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.

Asphalt Patch

Asphalt Patch	Tons	Sand	Cu. Yds.
---------------	------	------	----------

STEP STREETS

Step Streets	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		

Step Replacement

Step Replacement	Lin. Ft.		
------------------	----------	--	--

VEHICLE & EQUIPMENT


CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #: <u>1190871</u>
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	#:	#:	Truck #:

Other:

COMMENTS: Helped Justin (iv) with layout on Columbus Ave. Checked on Crews & Locations.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature


Title Crew Leader

Title

Approved By

Title


Title Supervisor

**DOT/SU CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Thursday

Date 8-15-13

SIGN IN

Name	Title	In	Out	Re.	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30			3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:20	16:30			2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30			2	<i>[Signature]</i>	
Edward Cordon	ACHR	05:00	16:30			2	<i>[Signature]</i>	

ON STREET

115 Avenue C Park St

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep 280'

Sidewalk Pour 325'

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete

7 Cu. Yds.

Sq. Ft.

Lumber

Lin. Ft.

Sq. Ft.

Steel Curb, Straight

Lin. Ft.

Lin. Ft.

Steel Curb, Bull Nose

Pieces

Lin. Ft.

Detectable Warning

Sq. Ft.

Lin. Ft.

Expansion Joints

Lin. Ft.

Snap Caps

Lin. Ft.

u. Yds.

Caulking

Tube

u. Yds.

Sealant Spray

2 Gal.

Tons

Sand

Cu. Yds.

u. Yds.

Stone

Cu. Yds.

Sq. Ft.

Other: 1 sheet Plywood

Lin. Ft.

3) 2x4 lumber

Lin. Ft.

① 2x6 lumber

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #: <u>0283</u>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u></u>	#:	Truck #:	#:	Truck #: <u>0287</u>

Other:

COMMENTS:

Worked 7 hours. Cement. 325 sq ft. Smashed Sealant.
Formed for tomorrow Pour, 280' 5 ft. Side walk. used 1 set.
Repaired and ③ 2x4 ① 2x6, cleaned up work area.
Received Safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Approved By

Title

Crew Leader

Supervisor

**DOT/SE U/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough QUEENS

Day THURSDAY

Date 8-15-2013

SIGN IN

Name	Title	In	Out	Re.	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castronovo	CM	6:00	16:30		7	3	<i>Michele Castronovo</i>	

ON STREET

ADAM C. POWELL JR. BLVD

CROSS STREET

W 165 ST

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep

Sidewalk Pour

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete

7 Cu. Yds.

Sq. Ft. Lumber

Lin. Ft.

Sq. Ft. Steel Curb, Straight

Lin. Ft.

Lin. Ft. Steel Curb, Bull Nose

Pieces

Lin. Ft. Detectable Warning

Sq. Ft.

Lin. Ft. Expansion Joints

Lin. Ft.

Snap Caps

Lin. Ft.

Cu. Yds. Caulking

Tube

Cu. Yds. Sealant Spray

Gal.

Tons Sand

Cu. Yds.

Cu. Yds. Stone

Cu. Yds.

Sq. Ft. Other:

in. Ft.

in. Ft.

in. Ft.

VEHICLES		EQUIPMENT		
Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>703B</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

ON LOCATION POUR 7 CU.YDS. OF READY
MIX FOR MIGUEL MOREL CREW.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Ralph C. A.

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BKLYN

Day Tue

Date 8-15-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Lawrence Johnson	MGO	5:00	1630	8	3	<u>L. Johnson</u>	
Julio Samayo	ACHR	5:00	1630	8	3	<u>Julio Samayo</u>	
<u>T. Thomas</u>	<u>HR</u>	<u>6:00</u>	<u>1630</u>	<u>8</u>	<u>2</u>		
<u>J. James</u>	<u>HR</u>	<u>6:00</u>	<u>1630</u>	<u>8</u>	<u>2</u>		

ON STREET	CROSS STREET
<u>COLUMBUS AV & W 109 ST N & S</u>	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	44 Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone 22 Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#: 0006	Truck #: 736 T 751T-784T	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	Truck #:	Truck #:	#: 5004	Truck #:

Other:

COMMENTS: EXCAVATION & SPREADED STONE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BKlyn

Day Fri

Date 8-10-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Lawrence Johnson	MGO	5:00	16:30	8	3	L. Johnson	
Julio Samayo	ACHR	5:00	16:30	8	3	Julio Samayo	
ROBERT MASIE	ACMR	6:00	16:30	8	0		

ON STREET	CROSS STREET
<u>ADM C. POWELL JR BLVD</u>	
<u>ALEXANDER AVE</u>	

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	20 Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

VEHICLES & EQUIPMENT				
CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #: 0006	Large Dump Truck Truck #: 736 T	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #: 5004	Utility Service Truck Truck #:
Other:				

Other

COMMENTS:

EXCAVATION

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Little

Approved by

11

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Bronx

Day Friday

Date 8.16.2013

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Denochy Cowan	HR	5:40:00	15:30	9	3	<i>Denochy Cowan</i>	
Isiah Hodge	HR	5:00	15:30	8	2	<i>Isiah Hodge</i>	
Robert Masi	ACHR	6:00	14:30	8		<i>Robert Masi</i>	

ON STREET

Boston Road yard
135 St & Alexander Ave
116 St & Adam Clayton Powell Blvd

CROSS STREET

Union Square west of E 14th St
Boston Road yard

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	20 Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 5897 ✓	Truck #:	#:	Truck #: 163 FF ✓	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:				
Other:				

COMMENTS:

Sent Rob to 116 St & Adam Clayton Powell to run debris, he also went to 135 St & Alexander Ave to run debris

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Denochy Cowan

Approved By

Approved By

Supervisor

Title

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough QUEENS

Day Fri. 12/4

Date 8-16-2013

SIGN IN

Name	Title	In	Out	Reg.	Ex.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castronovo	CM	6:20	16:30			3	<i>M. Castronovo</i>	

ON STREET

ADAM C. PAGE JR. BOUND

CROSS STREET

W 115 ST

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	in. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	in. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	in. Ft.	Expansion Joints	Lin. Ft.

PREP & CAVE-IN

Debris Removal	C Yds.	Caulking	Tube
Backfill	C Yds.	Sealant Spray	Gel
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	C Yds.	Stone	Cu. Yds.
Landing	in. Ft.	Other:	
Pointing/Caulking/Patching	in. Ft.		
Step Replacement	in. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>703 B</i>	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Excavator Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:

Other:

COMMENTS: ON LOCATION POUR 6 CU.YD. OF READY MIX
FOR MIGUEL MO ELC CREW

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT. THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader *Miguel Lopez*

Title

Approved By

Supervisor *Miguel Lopez*

Title

Signature

Title

Approved By

Signature

Title

Supervisor

Title

Signature

Title

**DOT/SI/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Fri Aug 16

Date 8-16-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30		3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30		2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30		2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30		2	<i>[Signature]</i>	

ON STREET

115 St Bronx C travel

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
		Ready Mix Concrete	(6) Cu. Yds.
Sidewalk Prep	175	Sq. Ft. Lumber <u>4x4</u>	Lin. Ft.
Sidewalk Pour	350	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep		in. Ft. Steel Curb, Bull Nose	Pieces
Curb Form		in. Ft. Detectable Warning	Sq. Ft.
Curb Pour		in. Ft. Expansion Joints	4 Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	. Yds.	Caulking	Tube
Backfill	. Yds.	Sealant Spray	2 Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES / EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0209</u>	Truck #: <u>02003</u>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#	Truck #:	#:	Truck #: <u>0367</u>

Other:

COMMENTS:

Placed (6) curbs, cement 350 cu ft Sidewalk.
trucks out 175 cu ft. Sidewalk, wood 4x4 cleated up
bottom ends new 12 Slat Ax.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Approved By

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Bronx

Day Friday

Date 8/16/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Darius Hunter	HR	4:00	15:30	8	3	<u>D. Hunter</u>	on location, every member
Tafari Malcolm	ACHR	5:00	15:30	8	2	<u>T. Malcolm</u>	of the crew
Thomas Myers	HR	6:00	16:30	8	2	<u>T. Myers</u>	is on site, con-
Ahmed Taitt	ACHR	5:00	15:30	8	2	<u>A. Taitt</u>	went well
							<u>Depot Co</u>
							11:00 AM

ON STREET	CROSS STREET
<u>116</u>	<u>Ad. Th Ave</u>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete <u>3</u> Cu. Yds.
Sidewalk Prep <u>60</u> Sq. Ft.	Lumber Lin. Ft.
Sidewalk Pour Sq. Ft.	Steel Curb, Straight Lin. Ft.
Curb Prep Lin. Ft.	Steel Curb, Bull Nose Pieces
Curb Form Lin. Ft.	Detecable Warning Sq. Ft.
Curb Pour Lin. Ft.	Expansion Joints <u>50</u> Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal Cu. Yds.	Caulking Tube
Backfill Cu. Yds.	Sealant Spray Gal.
Asphalt Patch Tons	Sand Cu. Yds.
STEP STREETS Cu. Yds.	Stone Cu. Yds.
Landing Sq. Ft.	Other: <u>2 4ft mats</u>
Pointing/Caulking/Patching Lin. Pt.	
Step Replacement Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>2634 ✓</u>	Truck #: <u>248 ✓</u>	#:	Truck #: <u>248 ✓</u>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u>6004 ✓</u>	#:	Truck #:	#:	Truck #:

Other: 6004 ✓

COMMENTS:

placed 3yd of concrete with the pump. Also broke out job of help load stone. Cleaned up jobsite and made area safe

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

D. Hunter

Title

Crew Leader

Approved By

Depot Co

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough SI

Day Monday

Date 8/19/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR	500	1530	8	0	<i>F. Cammalleri</i>	
Jason James	HR	600	1430	8	0	<i>J. James</i>	Worked WITH JOE
Alvaro Arias	HR	600	1430	8	0	<i>A. Arias</i>	"Arias"

ON STREET JASON
Guyor Ave

CROSS STREET AL
Adam C Powell 115
E Roc.

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: <i>754 T</i> <i>752 T</i>	Light Duty Truck Truck #: <i>6836</i>
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

all location safe

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader
F. Cammalleri
Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Monday

Date 8-19-13

SIGN IN

Name	Title	In	Out	Reg. H.	OT Hrs.	Signature /	Supervisor's Remarks
Salvatore Russello	CM	600	1620	7	3	<u>Salvatore Russello</u>	

ON STREET	CROSS STREET
115 ST AC	Powell JR
116 ST AC	Powell JR

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	S Ft. Lumber Lin. Ft.
Sidewalk Pour	S Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	L Ft. Steel Curb, Bull Nose Pieces
Curb Form	L Ft. Detectable Warning Sq. Ft.
Curb Pour	L Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu Yds. Caulking Tube
Backfill	Cu Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu Yds. Stone Cu. Yds.
Landing	S Ft. Other:
Pointing/Caulking/Patching	L Ft.
Step Replacement	L Ft.

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>3859</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Teamster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:		Truck #:	#:	Truck #:

Other:

COMMENTS:

Pour for MORNAL PREC
AND ALSO Help DANIE'S CREWS
AT 116 ST Powell JR.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT, THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Crew Leader Salvatore Russello
Supervisor _____

**DOT/SW/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Mo Day

Date 8-19-13

SIGN IN

Name	Title	In	Out	R Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	3	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	3	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	3	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	3	2	<i>[Signature]</i>	

ON STREET

115th Ave Pavell.

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	360 Sq. Ft.	Lumber (2) 2x6	3 Cu. Yds.
Sidewalk Pour	200 Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	30' Lin. Ft.

PREP & CAVE-IN

Debris Removal	1. Yds.	Caulking	Tube
Backfill	1. Yds.	Sealant Spray	2 Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
		Stone	Cu. Yds.
STEP STREETS	1. Yds.	Other:	
Landing	Sq. Ft.		
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #: <u>0003</u>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>0267</u>

Other:

COMMENTS: Paved 30' curb & concrete. Poured 200 Sq. Ft. sidewalk, formed out 360' ft. sidewalk. Sprayed sealant on finished concrete. Cleaned up location leveled sandy.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature [Signature]

Title Crew Leader

Approved By [Signature]

Title Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Monday

Date 8/19/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	16:30	8	3		
Gadiel Salas	ACHR	5:00	16:30	8	3	<i>G. Salas</i>	

ON STREET	CROSS STREET
<i>Adam C Power Jr.</i>	<i>116 St</i>

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal <i>20</i>	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Cu. Yds.
Landing	Sq. Ft.	Stone	
Pointing/Caulking/Patching	Lin. Ft.	Other:	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#: <i>0004</i>	Truck #: <i>737</i>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#: <i>5009</i>	Truck #:

Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Bronx

Day Monday

Date 8/19/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Darius Hunter	HR	5:00	16:30	8	3	<u>D. Hunter</u>	
Tafari Malcolm	ACHR	6:00	16:30	9	2	<u>T. Malcolm</u>	
Thomas Myers	HR	0	0	7	0	<u>T. Myers</u>	Out
Ahmed Taitt	ACHR	6:00	16:36	9	2	<u>A. Taitt</u>	Out

ON STREET	CROSS STREET
116th Street	7 Ave
138th Street	Alexander Avenue

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete 2 Cu. Yds.
Sidewalk Prep 100 Sq. Ft.	Lumber Lin. Ft.
Sidewalk Pour Sq. Ft.	Steel Curb, Straight Lin. Ft.
Curb Prep Lin. Ft.	Steel Curb, Bull Nose Pieces
Curb Form Lin. Ft.	Detectable Warning Sq. Ft.
Curb Pour Lin. Ft.	Expansion Joints 80 Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal Cu. Yds.	Caulking Tube
Backfill Cu. Yds.	Sealant Spray Gal.
Asphalt Patch Tons	Sand Cu. Yds.
STEP STREETS Cu. Yds.	Stone Cu. Yds.
Landing Sq. Ft.	Other:
Pointing/Caulking/Patching Lin. Ft.	
Step Replacement Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 2634 ✓	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck

Other:

COMMENTS:

Went to location on 116 & 7 Ave to pour 2 yd of concrete. Also put expansion joints around ramp + used 2 mats. Also went to 938th to help out with form

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

D. Hunter

Title

Crew Leader

Approved By

Donovan

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Bronx

Day Monday

Date 8/19/2013

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Denochy Cowan	HR	5:00	16:30	8	3	<i>Denochy Cowan</i>	
Isiah Hodge	HR	5:00	15:30	5	2	<i>Isiah Hodge</i>	
Robert Masi	ACHR					<i>Robert Masi</i>	

ON STREET

Boston Road yard
116th street & Adam Clayton Powell Blvd
135 St & Alexander Ave

CROSS STREET

Boston Road yard
Douglas Street
College Point yard

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>5897</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:		Truck #: #:		Truck #: #:
Other:				

COMMENTS:

Went to Various
crews and do
locations to check on
mark out with Mehdji

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Denochy Cowan

Title

Approved By

Title

Supervisor

**DOT/S.M/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queen

Day To due

Date 8-20-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	06:00	16:30	8	3		
Fevrin Agenord	ACHR	06:00	16:30	8	2		
Frank Messina	ACHR	06:00	16:30	8	2		
Edward Cotton	ACHR	06:00	16:30	8	2		

ON STREET

115^{s+} ~~P~~ ¹₂ m C Powell

CROSS STREET

WORK PERFORMED

MATERIALS USED

WORKING ORDER		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	3	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	50' Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	3 Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Cu. Yds.	Other: Poured 40 Sq. Ft. road base.	
Pointing/Caulking/Patching	Sq. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

VEHICLES & EQUIPMENT				
CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
0289	0003			
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
				0267
Other:				

COMMENTS:

Powered (?) by yard cement - ~~30' soft~~ 30' soft. used
50 wt exp. in base, also powered 40 soft. Road base
powered with sealant. Cleaves up (concrete needed soft
but back to yard cleared up pick up -

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

**DOT/SID /CITYWIDE CONCRETE
DA LY GANG REPORT**

Borough Queens.

Day TUES DAY.

Date 8-20-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Salvatore Russello	CM	060	1630	7	3	Salvatore Russello	

ON STREET

ON STREET	CROSS STREET
115 ST A 2 FORBIDDEN TR # PLUMBING BY 116	41 POST

WORK PERFORMED

SIDEWALK & CURB	MATERIALS USED	
Sidewalk Prep	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	cu. Ft. Lumber	Lin. Ft.
Curb Prep	cu. Ft. Steel Curb, Straight	Lin. Pt.
Curb Form	1 cu. Ft. Steel Curb, Bull Nose	Pieces
Curb Pour	1 cu. Ft. Detectable Warning	Sq. Ft.
	1 cu. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN		
Debris Removal	Susp Caps	Lin. Ft.
Backfill	cu. Yds. Caulking	Tube
Asphalt Patch	cu. Yds. Sealant Spray	Gal.
STEP STREETS		
Landing	Tons Sand	Cu. Yds.
Pointing/Caulking/Patching	cu. Yds. Stone	Cu. Yds.
Step Replacement	cu. Yds. Other:	
	cu. Yds.	
	cu. Yds.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Bulkhoe	Large Dump Truck	Light Duty Truck
Truck #: 2859	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Teamster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

Help with pour man at end
and also help Alzate crews with
pour.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader
Salvatore Russello

Title

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough S.I.

Day Tues

Date 8/20/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Douglas Olson	CM	6:00	16:30	7	3	<i>SJL</i>	

ON STREET	CROSS STREET	Region
<i>Adam Clayton Powell Jr Blvd</i>	<i>115 St</i>	<i>SMJ</i>

WORK PERFORMED	MATERIALS USED	
SIDEWALK & CURB	Ready Mix Concrete	7 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>991-855</i>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS: *Poured 7 yds of sidewalk with misur gang. 5" Slump on concrete mix.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

SJL

Title

Crew Leader

Approved By

Title

Supervisor

DOT
DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Aug 27 2013 11:54am P003/012

Borough Bronx

Day Tuesday

Date 8/26/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Darius Hunter	HR	5:00	16:35	8	3	<u>A. Hunter</u>	
Tafari Malcolm	ACHR	6:00	16:30	7	2	<u>T. Malcolm</u>	
Thomas Myers	HR	6:00	16:30	8	2	<u>T. Myers</u>	
Ahmed Tait	ACHR	6:00	16:30	8	2	<u>A. Tait</u>	

ON STREET	CROSS STREET
<u>115th</u>	<u>7 Ave</u>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	12.0 Sq. Ft. Lumber Cu. Ft.
Sidewalk Pour	Sc. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sc. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

Crew/Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>2634 ✓</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>8247-0248 ✓</u>

Other:

COMMENTS: We're to location opened up job that was done yesterday put safety meeting on the side. Also went across the road to from new forcing cut a sour out from the ridge. This location is not safety nearly.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature J. Braxton
Title Crew Leader
Approved By A. Hunter
Title Supervisor

**DOT/SI /CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens)

Day Thursday

Date 8-22-13

SIGN IN

Name	Title	In	Out	R. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACFR	05:50	16:30	10	3	<i>[Signature]</i>	
Fevrin Ageord	ACHR	06:00	16:30	10	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	10	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	10	2	<i>[Signature]</i>	

ON STREET

115 Adam C. Powell

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete <i>(4)</i>	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber <i>2x4</i>	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	40' Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	10' Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Track	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>0289</i>	Truck #: <i>02203</i>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <i>0267</i>	#:	Truck #:	#:	Truck #:

Other:

Comments: *Saw cut. 2 Pcs ramp. used 20' wide steel. also saw cut 6' laid as into asphalt. cleaned up location and reset soffit.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By *[Signature]*

Title Supervisor

Aug 23 2013 06:54am

Fax:718-353-6381

DOT

PO12/016

Borough BronxDay ThursdayDate 8/22/13

SIGN IN

Name	Title	In	Out	Reg. Hrs	OT Hrs	Signature	Supervisor's Remarks
Darius Hunter	HR	15:40	16:40			A. Hunter	
Tafari Maisoir	ACRH	16:40	16:40				
Thomas Myers	HR	16:40	16:40				
Ahmed Taitt	ACRH	16:40	16:40				

ON STREET

116 St

CROSS STREET

7 A.M.

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	20 Lin. Ft.
Sidewalk Pour	190 Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detachable Warning	Sc. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	70 Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tubs
Backfill	Cu. Yds.	Sealant Spots	Gal
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sc. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>2684 ✓</u>	Truck #:		Truck #: <u>0004 ✓</u>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>0248 ✓</u>
Other:				

COMMENTS:

Went to location, fresh frames were poured, back of grade of concrete pour was too cleaned up, got back and over side pipe failed to come connected.

NOTE: Was told to post job by operation supervisor even though the truck was 90 min. late.

Signature

A. Hunter

Title

Crew Leader

Approved By

John Williams

Title

Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAR BY GANG REPORT**

Borough Queens

Day FRIDAY

Date 8-23-13

SIGN IN

Name	Title	In	Out	Reg.	hrs.	OT Hrs.	Signature	Supervisor's Remarks
Ruth Cen	CN	600	1630	7	3		Lobato	

ON STREET

116 ST AC

CROSS STREET

Powell JR

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep

Sidewalk Pour

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete

Cu. Yds.

Ft. Lumber

Lin. Ft.

Ft. Steel Curb, Straight

Lin. Ft.

Ft. Steel Curb, Bull Nose

Pieces

Ft. Detectable Warning

Sq. Ft.

Ft. Expansion Joints

Lin. Ft.

Snip Caps

Lin. Ft.

Yds. Caulking

Tube

Yds. Sealant Spray

Gal.

Tons Sand

Cu. Yds.

Yds. Stone

Cu. Yds.

Ft. Other:

Ft.

Ft.

Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>3859</u>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Frontmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

POUR FOR DRIES, 6 PUGED
OF CONCRETE ALSO Help with
Forming.

**DOT/SIW/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Fri Aug -

Date 8-23-13

SIGN IN

Name	Title	In	Out	Rg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	5	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	3	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	3	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	

ON STREET

<u>115th AdamConnell</u>	CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds. <u>(2)</u> 2x6 Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	20' Lfts. Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	<u>(1)</u> 3' pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	<u>(10)</u> Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	cu. Yds.	Caulking	Tube
Backfill	cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Yds. Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #: <u>0003</u>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>0267</u>
Other:				

COMMENTS:

*Perf. (1) 3' R. Bull nose and (1) 30' left street curb
Cut out Piping, form & pour out side of street curb,
lowered Catch Basin, cleaned up location and reset
piping*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature [Signature]

Title Crew Leader

Approved By [Signature]

Title Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day FRIDAY

Date 8/23/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Gregory Duran	IMGD	0500	14:30	8			
Edward Harston	ACHR	0500	14:30	8		Eduardo Harston	
JULIO SAMAYOA	ACHR	0700	14:3	8		Julio Samayoa	

ON STREET

CROSS STREET

E 116 ST AND ADAM CLANDON POWELL.

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURE		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sc. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sc. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sc. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sc. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
		0006	735T/736T	
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
			5004	

Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title: Crew Leader: _____

Approved By

Title: Supervisor: _____

**DOT/SII CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day monday.

Date 8-26-13

SIGN IN

Name	Title	In	Out	Re	Mrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30		3			
Fevrin Agenord	ACHR	06:00	16:30		2			
Frank Messina	ACHR	06:00	16:30		2			
Edward Cotton	ACHR	06:00	16:30		3	2		

ON STREET

115 st Adam C. Powell

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep

Sidewalk Pour

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete

Cu. Yds.

Sq. Ft. Lumber

Lin. Ft.

Sq. Ft. Steel Curb, Straight

Lin. Ft.

Lin. Ft. Steel Curb, Bull Nose

Pieces

Lin. Ft. Detectable Warning

Sq. Ft.

Lin. Ft. Expansion Joints

40 Lin. Ft.

Snap Caps

Lin. Ft.

1. Yds. Caulking

Tube

1. Yds. Sealant Spray

Gal.

Tons Sand

Cu. Yds.

1. Yds. Stone

Cu. Yds.

Sq. Ft. Other: (2) plywood (1) 2x10

VEHICLES **EQUIPMENT**

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #: <u>0003</u>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u></u>	#:	Truck #:	#:	Truck #: <u>0267</u>

Other:

COMMENTS:

formed out all curb, 80' cult.
and 12' cult of curb by Pedramp, used (2) plywood
and (1) 2x10, cleaned up location and reseted
safely.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

John L. Mora

Title

Crew Leader

Approved By

John L. Mora

Title

Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Mon Day

Date 8-26-13

SIGN IN

Name	Title	In	Out	Reg.	Ex.	OT Hrs.	Signature	Supervisor's Remarks
S RUSSELLO	CM	600	1630	T		3	S. RUSSELLO	

ON STREET

8 Avenue
COLUMBUS ave
NE POINT

CROSS STREET

14 ST MANHATTAN
W. 110 ST
115 ST

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep

MATERIALS USED

Ready Mix Concrete

Cu. Yds.

ft. Lumber

lin. Ft.

Sidewalk Pour

ft. Steel Curb, Straight

lin. Ft.

Curb Prep

ft. Steel Curb, Bull Nose

Pieces

Curb Form

ft. Detectable Warning

Sq. Ft.

Curb Pour

ft. Expansion Joints

lin. Ft.

PREP & CAVE-IN

Snap Caps

lin. Ft.

Debris Removal

C Yds. Caulking

Tube

Backfill

C Yds. Sealant Spray

Gal.

Asphalt Patch

Tons Sand

Cu. Yds.

STEP STREETS

C Yds. Stone

Cu. Yds.

Landing

ft. Other:

Pointing/Caulking/Patching

ft.

Step Replacement

ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Excavator	Large Dump Truck	Light Duty Truck
Truck #: <u>3859</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Excavator	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u></u>	#:	#:	#:	Truck #:
Other:				

COMMENTS:

We at The above Locations
Checking Framing.

**DOT/SI W/CITYWIDE CONCRETE
DILY GANG REPORT**

Borough Queens

Day Tuesday

Date 8/26/13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	16:30	8	3	<i>John Taranto</i>	

ON STREET

College Point yard (Qn)
Queens plant (Qn)
44th Drive (Qn) (Qn)

CROSS STREET

Adam C. Powell Blvd (15 St) (Man)

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
	Lin. Ft.	Expansion Joints	Lin. Ft.

PREP & CAVE-IN

Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.

STEP STREETS

Landing	Cu. Yds.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Checked on crews at locations. Begun city time.
Picked up supplies from engine, fielded up truck at
Queens plant. Turned to yard to do paperwork.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

001
DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Fax: 718-325-4229

AUG 28 2013 04:15PM PU06/U13

Borough Bronx

Day Monday

Date 8/26/13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Darius Hunter	HR	6:00	14:30	8	1	<u>D. Hunter</u>	
Tafari Malcolm	ACHR	6:00	14:30	8	0	<u>Tafari</u>	
Thomas Myers	HR	6:00	14:30	8	0	<u>Thomas</u>	
Ahmed Taitt	ACHR	6:00	14:30	8	0	<u>Ahmed</u>	

ON STREET

ON STREET	CROSS STREET
1452	8 Ave
116 St	7 Ave

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Steel Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>2634 ✓</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>0248 ✓</u>

Other:

COMMENTS:

Wait for 116 & 7 Ave for pick-up safety + open job.
Also made area safe. Also needs little asphalt. Then went
to 1452 145th to do job but power washer didn't work.
Wait to 44 Ave to get one that was working.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

D. Hunter

Title Crew Leader

Approved By

D. Hunter C

Title Supervisor

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough BK

Day Tuesday

Date Aug-27-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0500	1530	8	2	<i>Milagros Lopez</i>	
Sean Thomas	ACHR	0600	1530	8	1	<i>Sean Thomas</i>	
Rohan Wilkinson	ACHR	0600	1530	8	1	<i>Rohan Wilkinson</i>	
Nicholas Depaola	ACHR	WORKED WITH CABEZA				<i>CABEZA</i>	

ON STREET	CROSS STREET
ALEXANDER AVE (Bronx)	138TH STREET
ADAM CLAYTON Powell (Bronx)	116ST
NAASSAU AVE (Brooklyn) Gouverneur ST	

WORK PERFORMED	MATERIALS USED		
SIDEWALK & CURB			
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
PREP & CAVE-IN			
Debris Removal	Cu. Yds.	Snap Caps	Lin. Ft.
Backfill	Cu. Yds.	Caulking	Tube
Asphalt Patch <u>2</u>	Tons	Sealant Spray	Gal.
STEP STREETS	Cu. Yds.	Sand	Cu. Yds.
Landing	Sq. Ft.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	Other:	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: PICKUP 7087	Light Duty Truck Truck #: 0014 F HOT BOX
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: 0244

Other:

COMMENTS:

Rohan W. Drove TO HARPER SHAWNS HOME. Drove TO CABEZA LOCATION TO DROP OFF ROLLER, GANG then met up AT THREE LOCATION AC PAND PAVED ALL REQUIRED PREP MADE SURF "Mutape Super" ALL LOCATIONS WAS CLEAN AND SAFE, WENT BACK TO YARD, CLEANED OUT HOT BOX.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

HWD

**DOT/SU CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Tuesday

Date 8-27-13

SIGN IN

Name	Title	In	Out	Re.	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30		3	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30		2	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00					<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30		3	2	<i>[Signature]</i>	

ON STREET

115 ft Adam Powell

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	Sq. Ft.	Lumber	3 Cu. Yds.
---------------	---------	--------	------------

Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
---------------	---------	----------------------	----------

Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
-----------	----------	-----------------------	--------

Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
-----------	----------	--------------------	---------

Curb Pour	Lin. Ft.	Expansion Joints	10' Lin. Ft.
-----------	----------	------------------	--------------

PREP & CAVE-IN		Snap Caps	Lin. Ft.
----------------	--	-----------	----------

Debris Removal	Yds.	Caulking	Tube
----------------	------	----------	------

Backfill	Yds.	Sealant Spray	2 Gal.
----------	------	---------------	--------

Asphalt Patch	Tons	Sand	Cu. Yds.
---------------	------	------	----------

STEP STREETS	Yds.	Stone	Cu. Yds.
--------------	------	-------	----------

Landing	Sq. Ft.	Other:	
---------	---------	--------	--

Pointing/Caulking/Patching	Lin. Ft.		
----------------------------	----------	--	--

Step Replacement	Lin. Ft.		
------------------	----------	--	--

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>0207</i>	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: <i>0267</i>

Other:

Comments: *Poured 80' ft Curb, used 3 cu.yds cement.
Sprayed sealant (2 gal.) cleaned up location
and reset 2 sets.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By *[Signature]*

Title Supervisor

Fax: 718-353-6381

Aug 28 2013

06:08am P009/018

DOT

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day TUESDAY

Date 8-27-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
S Russell	CUR	600	1430	7	5	R. Colletti	

ON STREET	CROSS STREET
A.C. Powell	115 ST
8 AV	14 ST

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	1/2 Ft. Lumber Lin. Ft.
Sidewalk Pour	1/2 Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	1/2 Ft. Steel Curb, Bull Nose Pieces
Curb Form	1/2 Ft. Detectable Warning Sq. Ft.
Curb Pour	1/2 Ft. Expansion Joints Lin. Ft.
PREP & CAVI-EN	Snap Caps Lin. Ft.
Debris Removal	C. Yds. Caulking Tube
Backfill	C. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	C. Yds. Stone Cu. Yds.
Landing	1/2 Ft. Other:
Pointing/Caulking/Patching	1/2 Ft.
Step Replacement	1/2 Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Digger	Large Dump Truck	Light Duty Truck
Truck #: 3359	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Wimmer	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

WENT AND POUR 3 rugged of concrete
for No Rail. Curb and also went to Dales Location
and do the ~~open~~ float job

Fax: 718-353-6381

Aug 28 2013 06:07AM

P005/018

DOT

**DOT/SI /CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Greens

Day Wednesday

Date 8-28-03

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	11	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	10	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	10	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	10	3	<i>[Signature]</i>	

ON STREET

115th Avenue Pavement

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	60 sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour		Lumber <u>7) 2 x 6</u>	Lin. Ft.
Curb Prep		Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Form		in. Ft. Steel Curb, Bull Nose	Pieces
Curb Pour		in. Ft. Detectable Warning	Sq. Ft.
		in. Ft. Expansion Joints	<u>19</u> Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	cu. Yds.	Caulking	Tube
Backfill	cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		cu. Yds. Stone <u>16 cu yard.</u>	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>0289</u>	Mason Dump Truck Truck #: <u>5503</u>	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: <u>0267</u>
Other:				

COMMENTS:

formed out 60' sq ft of sidewalk, used 7) 2x6.
Spread and tamped 16 cu yard stone. Put up stops
for pour tomorrow, cleaned up location and reset safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough Queens

Day Thursday

Date 8-29-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3	<i>[Signature]</i>	
Fevrin Achord	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	

ON STREET	CROSS STREET
115 th Street A	Adam C. Powell
115 th Street	St. Nicholas
College Point	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete 5 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	255' Sq. Ft. Steel Curb, Bright Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bright Nose Pieces
Curb Form	Lin. Ft. Detectable Warning 2 mats (2x4) Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints 40' Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray 2 Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0289	Truck #: 0003	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:		Truck #: 0267

Other:

Comments: Poured 5 cu.yds, 255 sq. ft. side walls with two Red rags. Welded 2 2x4 mats, sprayed with sealant. Cleared up location and restored safety.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By *[Signature]*

Title Supervisor

DAILY GANG REPORTBorough QUEENSDay THURSDAYDate 8-29-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Manager	Supervisor's Remarks
S Russell	EM	600	1630	7	3	Robert Miller	

ON STREET	CROSS ST	ST
A C Powell TR	W 1 S ST	

WORK PERFORMED	MATERIAL	USED
SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, B	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, B	Pieces
Curb Form	Lin. Ft. Detectable V	Sq. Ft.
Curb Pour	Lin. Ft. Expansion J	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spr	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>3859</u>	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Townmaster Truck #:	Tag-A-Long Trailer	Utility Service Truck Truck #:
Other:				

COMMENTS: _____

POUR FOR MORTL CREW 5 cu yd
OF CONCRETE ALSO WAIT INSPECT AL247e Pour

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BronxDay ThursdayDate 8. 29. 2013**SIGN IN**

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Denochy Cowan	HR	5:00	10:30	8	3	<i>Denochy Cowan</i>	
Isiah Hodges	HR	5:00	15:30	3	2	<i>Isiah Hodges</i>	

ON STREET

Boston Road yard
Long Fellow & Bruckner Blvd
116th Street & Adam Clayton Powell

CROSS STREET

Boston Road yard

WORK PERFORMED

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detachable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>5897</i>	Truck #:		Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:		Truck #:	#:	Truck #:

Other:


Comments: Went to check various locations. Isiah help crews in the morning to load & unload trucks and work in the yard

I CERTIFY THAT THE TIME OF THE EMPLOYEE'S RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC
 Signature _____

Title

Crew Leader

Approved By



Title

Supervisor

DAILY GANG REPORT

Borough QUEENS.

Day Fri 06/9

Date 2 - 30-13

SIGN IN

ON STREET	CROSS STREET
AC Powell Jr R	115 ST

WORK PERFORMED	MATERIAL USED
SIDEWALK & CURB	Ready Mix Concrete
Sidewalk Prep	Sq. Ft. Lumber
Sidewalk Pour	Sq. Ft. Steel Curb, Sight
Curb Prep	Lin. Ft. Steel Curb, Lip Nose
Curb Form	Lin. Ft. Detectable V. Ring
Curb Pour	Lin. Ft. Expansion Joints
PREP & CAVE-IN	Snap Caps
Debris Removal	Cu. Yds. Caulking
Backfill	Cu. Yds. Sealant Spray
Asphalt Patch	Tons Sand
STEP STREETS	Cu. Yds. Stone
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>3859</i>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer	Utility Service Truck Truck #:
Other:				

COMMENTS:

Pour 5 cu yd of concrete
for masonry erec.

DOT
DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT


Sep 4 2013 04:02pm P025/050

Borough: Queens

Day Friday

Date 18/30/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	16:30	8	3		8

ON STREET	CROSS STREET
College Point Yard (Q) Adam Powell Blvd & 115th (Man) 55 Water St (Man)	Queens Plaza (Q)

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

went to 55 winter street to drop off Misael Radio / phone went to Queens Plaza to get fuel checked on crews locations

I CERTIFY THAT THE TIME OF THE EMPLOYEE'S RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Fri. 2/1

Date 8-30-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	06:50	16:30	8	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:30	16:30	8	2	<i>[Signature]</i>	
Frank Messina	ACHR	06:00	16:00	8	1	<i>[Signature]</i>	
Edward Cotton	ACHR	06:00	16:00	8	2	<i>[Signature]</i>	

ON STREET	CROSS STREET
<i>115 St Adam C Powell</i>	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	
Sidewalk Prep	Ready Mix Concrete 5 Cu. Yds.
Sidewalk Pour	Sq. Ft. Lumber Lin. Ft.
	260 Sq. Ft. Steel Curb, straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning (1) 2x4 mat. Sq. Ft.
Curb Pour	Lin. Ft. Expansion joints 40' Lin. Ft.
PREP & CAVE-IN	
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray 2 Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0289	Truck #: <i>[Redacted]</i>	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:	Truck #: #:	Truck #: #:		Truck #: 0267
Other:				

COMMENTS:

landscaped, painted, spray painted, sandblasted, cleaned up, leveled, located and leveled, set up, sent Fevrin and Eddie to gas station to get sharper yard.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *[Signature]*

Title Crew Leader

Approved By *[Signature]*

Title Supervisor

DAILY GANG REPORTBorough QueensDay TUESDAYDate 9-3-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Manager	Supervisor's Remarks
S Rizzello	CN	600	1630	7	3	Stephen M	

ON STREET	CROSS STR.	ET
AC Paseo Dr.	JR	W 15 St

WORK PERFORMED	MATERIAL	USED
SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, S	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, H	Pieces
Curb Form	Lin. Ft. Detectable W	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 3859	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:	Truck #: #:	Truck #: #:	Truck #: #:	Truck #: #:

COMMENTS:

POUR FORM WORK PRECUT
 ALSO WENT TO INSPECT K24T AND RESTING
 POUR

DOT/SIM/CITYWIDE : CONCRETE
DAILY GANG REPORT

Borough Queens

Day Monday

Date 9-3-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3	<i>[Signature]</i>	
Fevrin Agenord	ACHR	06:00	16:30	8	2	<i>[Signature]</i>	
Frank Messina	ACHR					<i>[Signature]</i>	
Edward Cotton	ACHR					<i>[Signature]</i>	

ON STREET

Address	CROSS ST	STREET
115 Adam C Powell		

WORK PERFORMED

Work Category	Material / Item	Quantity / Unit	Used
SIDEWALK & CURB	Ready Mix Concrete	3 Cu. Yds.	
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.	
Sidewalk Pour	140 Sq. Ft. Steel Curb, Right	Lin. Ft.	
Curb Prep	Lin. Ft. Steel Curb, Bell Nose	Pieces	
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.	
Curb Pour	Lin. Ft. Expansion Joints	40 Lin. Ft.	
PREP & CAVE-IN	Snap Caps	Lin. Ft.	
Debris Removal	Cu. Yds. Caulking	Tube	
Backfill	Cu. Yds. Sealant Spray	Gal.	
Asphalt Patch	Tons Sand	Cu. Yds.	
STEP STREETS	Cu. Yds. Stone	Cu. Yds.	
Landing	Sq. Ft. Other:		
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>0289</u>	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #: <u>0267</u>
Other:				

COMMENTS:

*Poured 3 curbs 140' ft. Ped ramp and
sidewalk, cleaned up curb and recessed
soffit.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Miguel Morel

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough S.I.

Day Tues

Date 9/3/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Douglas Olson	CM	6:00	16:30	7	3	<i>SJC</i>	

ON STREET	CROSS STREET
<i>Adam Clayton Powell Jr Blvd</i>	<i>M. St Sandy</i>

WORK PERFORMED	MATERIALS USED		
SIDEWALK & CURB	Ready Mix Concrete	3	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps		
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>991-875</i>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS: *Poured 3 yards of sidewalk with
Misael Sandy. 5" Slump on concrete
mix.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

SJC

Title

Crew Leader

Approved By

Title

Supervisor

Borough QueensDay WednesdayDate 9/4/13✓ Columbus
SOY

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	16:30	8	3		

ON STREET

CROSS STREET

College Point yard (av)
 Adam & Powell blvd & 115 St (men)
 Columbus Ave & 106 St - 73 St (men)

→ SOY, SSS

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Cui	Lin. Ft.
Curb Prep	Lin. Ft. Steel Cui	Pieces
Curb Form	Lin. Ft. Detecto	Sq. Ft.
Curb Pour	Lin. Ft. Expansive Joints	Lin. Ft.
PREP & CAVE-IN	Snap Cui	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other	
Pointing/Caulking/Patching	Lin. Pt.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

checked on crews at locations, finished city time
 & paperwork, cleaned up office

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Approved By

Supervisor



**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**
Borough GreenDay WednesdayDate 9-4-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	05:00	16:30	8	3		
Fevrin Agenford	ACHR	05:00	16:30	8	2		
Frank Messina	ACHR						
Edward Cotton	ACHR	05:00	16:30	8	2		

ON STREET

115 Allen Street

CROSS ST:

ET

WORK PERFORMED

		MATERIAL	USED
Sidewalk Prep	Sq. Ft	Ready Mix Concrete	1 Cu. Yds.
Sidewalk Pour	Sq. Ft	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bent	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
PREP & CAVE-IN	Lin. Ft.	Expansion Joint	20 Lin. Ft.
Debris Removal	Cu. Yds.	Snap Caps	Lin. Ft.
Backfill	Cu. Yds.	Caulking	Tube
Asphalt Patch	Tons	Sealant Spray	1 Gal.
STEP STREETS	Cu. Yds.	Sand	Cu. Yds.
Landing	Sq. Ft.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	Other	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tug-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #: <u>0267</u>

COMMENTS:

Broke out Red pump with W
 pump with no working part
 Caulkies Island used (16) tubes, cleaned up and reset safety -
 Went to 23rd and B.Wayne and Prince A Lafayette to see next job.

I CERTIFY THAT THE TIME ON THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Approved By

Supervisor

Title

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Wednesday

Date 9/4/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	17:30	8	4		
Gadiel Salas	ACHR	5:00	17:30	8	4	<i>G. Salas</i>	

ON STREET

① Adam C Power Jr. CROSS STREET
② Tiffany St 115 St
③ Greenwich Morris

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	20	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Cu. Yds.
Landing	Sq. Ft.	Stone	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Excavated at three different locations

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Wednesday

Date 9-4-18

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
John Roberts	ACHR	5:00	11:20	6	13	J. Roberts	
Michael Graf	ACHR	6:00	work in yard			Michael Graf	
	ACHR						
	ACHR						

ON STREET

41-15
115th Street
Boston Rd.

CROSS STREET

19th AVENUE
Adam Clayton Powell II
E. 233

WORK PERFORMED

SIDEWALK & CURB

	MATERIALS USED	
Sidewalk Prep.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Lumber	Lin. Ft.
Curb Prep.	Steel Curb, Straight	Lin. Ft.
Curb Form	Steel Curb, Bull Nose	Pieces
Curb Pour	Detectable Warning	Sq. Ft.
	Expansion Joints	Lin. Ft.
	Snap Caps	Lin. Ft.

PREP & CAVE-IN

Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
		Stone	Cu. Yds.
STEP STREETS	Cu. Yds.		
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Townmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Today I work with Millies. We had about 45 tons of Asphalt
2.5 Ton on 115 & 7th we Tamped did AC and performed Safety
And also Scraping out 2 Ton in the Bronx Yards

I CERTIFY THAT THE TIME OF THE ACTIVITIES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

John Roberts

Title

Crew Leader

Approved By

Noel Bick

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BK

Day Wednesday Date 9-4-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0600	1630	8	3	JULIA LOPEZ	
Sean Thomas	ACHR	0600	1630	8	3	Sean Thomas	
Rohan Wilkinson	ACHR	0600	1630	8	2	ROHAN WILKINSON	
Nicholas Depaola	ACHR	—	—	—	—	Nicholas Depaola	Out

ON STREET

41-15
115 ST
BOSTON 21

CROSS STREET

19TH AVE
ADAM Clayton Power
E 223

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch <u>4</u>	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other: <u>SAVED OFF Location</u>	
Pointing/Caulking/Patching	Lin. Ft.	EXCAVATED by hand 30 FT.	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: PICK UP 7087	Light Duty Truck Truck #: 0014 & HOT BOX
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility/Service Truck Truck #: 0244

Other:

Comments: Drop off my pick up for service at runway shown
I picked me up Rohan W. and Rohan R. met us
at location, we squared off 30 feet of asphalt, then
paved and re-graded area... clean cut 2 tons of
asphalt spray asphalt at Boston Renovation
yard, location was clean and safe.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Title

Supervisor

SL

Borough QUEENS

Day WEDNESDAY

Date 9-4-2013

SIGN-IN

Name	Title	Hrs	Ovt	Reg Hrs	OT hrs	Supervisor's Signature	Supervisor's Remarks
Michael Chimento	CM	6.00	00:00	7	3	<u>Bob</u>	

ON STREET

ON STREET	CROSS STREET
ADAM C. POWELL JR. BLVD	C-115 ST

WORK PERFORMED

SHEDWALK & CURB	MATERIALS USED
	Ready Mix Concrete
Sidewalk Prep	Sq. Ft. Lumber
Sidewalk Pour	Sq. Ft. Steel Curb, St
Curb Prep	Lin. Ft. Steel Curb, Bi
Curb Repair	Lin. Ft. Detectable Wa
Curb Pour	Lin. Ft. Expansion Joint
PREP & GATE IN	Steel Caps
Debris Removal	Cu. Yds. Caulking
Backfill	Cu. Yds. Sealant Spray
Asphalt Patch	Tons Sand
STEP STREETS	Cu. Yds. Stone
Landing	Sq. Ft. Other
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Doms. Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck # <u>7038</u>	Truck #	#	#	Truck #
Medium Dump Truck	Hydraulic Excavator	Tomahawk	Ag-A-Long Tractor	Utility Service Truck
Truck #	#	Truck #	#	Truck #

Other:

COMMENTS: ON LOCATION - POUR FOR MILEAGE MONEY C.R.

CO-OP OF READY MIX

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK

PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC.

Signature

Name

Approved By

Title

Crew Leader

Robert C. Chimento

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Wednesday

Date 9-4-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Horace Johnson	HR	5:00	18:30	8	5	<i>H. Johnson</i>	
Tyrone Thomas	HR	6:00	16:30	8	2	<i>T. Thomas</i>	
Thakadial Jamanram	ACHR	—	—	—	Out	<i>Jamanram EFB</i>	
Willie Smith	SST	8:00	16:30	7	4½	<i>Willie Smith</i>	

ON STREET	CROSS STREET
① 29th St Yrd	58th St Yd.
② Adam C Powell & 115th St	
Bruckner Ave and 106th St	
Keah St and Tiffany Ave	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft. Out-Pali-Larry-Robbie-Soto
Step Replacement	Lin. Ft. Nick-Buzzell

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	#: <i>Zim-Mixer 20C</i>	Large Dump Truck Truck #:	Light Duty Truck Truck #: 1169717
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

I paved with the Zim-Mixer at three (3) location,
Willie on of the College Pt Yd. Tyrone took stone to three (3) locations

DOT/SIM/CITYWIDE CONCRETE

[REDACTED] - DAILY GANG REPORT

Borough QUEENS 44-12Day ThursdayDate 9/5/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STORES	ACHER	6:00	2:30	8		JF	

from 44-12 M.

ON STREET	104 th St. Columbus Ave 70 th St. Columbus Ave 115 th St. 7 th Ave Lafayette & Prince St. PEN TO 44-12 M.	CROSS STREET	104 th St. Columbus Ave 70 th St. Columbus Ave 115 th St. 7 th Ave Lafayette & Prince St.
-----------	---	--------------	--

75% SSS
 " 6 Hours of
 Reg Time

WORK PERFORMED

MATERIALS USED

Cobblestone/Pavers	Ready Mix Concrete	Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone	Sq. Ft.
Pavers	Sq. Ft. Pavers	Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks	Ea.
Steps & Walls	Lumber	Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking	Tube
Step Replacement	Lin. Ft. Cement	Bags
Wall Forming	Sq. Ft. Mortar Mix	Bags
Wall Installing	Sq. Ft. Sand	Cu. Yds.
Prep & Cave-In	Stone	Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints	Lin. Ft.
Backfill	Cu. Yds. Detectable Warning	Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other: MINI RACK TRUCK #0367 - SSS

COMMENTS:

SET UP SAFETY ON COLUMBUS AVE 104TH NORTH & SOUTH, 70TH ST., REMOVES Jersey barriers from 115TH 7TH AVE, PLACED 10 Jersey barriers on LAFAYETTE PRINCE ST.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

JF

Title

Crew Leader

Approved By

Ned ZK

Title

Supervisor

**DOT/SI CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Thurs Day

Date 8-5-13

SIGN IN

Name	Title	In	Out	Reqs.	Irs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	06:00	16:30			3	<u>MM</u>	
Fevrin Agenord	ACHR	06:00	16:30			2	<u>FA</u>	
Frank Messina	ACHR						<u>FM</u>	
Edward Cotton	ACHR	06:00	14:30			0	<u>EC</u>	

ON STREET

115 Adam Powell
Prince & Lafayette

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep

Sidewalk Pour

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete

Cu. Yds.

q. Ft. Lumber

Lin. Ft.

q. Ft. Steel Curb, Straight

Lin. Ft.

n. Ft. Steel Curb, Bull Nose

Pieces

n. Ft. Detectable Warning

Sq. Ft.

n. Ft. Expansion Joints

Lin. Ft.

Snap Caps

Lin. Ft.

C Yds. Caulking

Tube

C Yds. Sealant Spray

Gal.

Tons Sand

Cu. Yds.

C Yds. Stone

Cu. Yds.

q. Ft. Other:

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Lokhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0289</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Wmster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:	Truck #: #:	Truck #: #:	Truck #: #:	Truck #: <u>02-67</u>

Other:

COMMENTS:

went to 115 Adam Powell Parked up safety
and opened up for Red, Then took safety - To Prince
and Lafayette, Break out crew open up Birth ramp
I cut out two Red runs in the steel. Heared up and set safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT / I CERTIFY THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queen,

Day Thursday:

Date 8-5-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR	06:00	16:30	8	3		
Fevrin Agenord	ACHR	06:00	16:30	8	2		
Frank Messina	ACHR						
Edward Cotton	ACHR	06:00	14:30	8	0		

ON STREET

115 Main Street
Prince & Lafayette.

CROSS ST^ET EET

WORK PERFORMED

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, I-Beams	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, II Nose	Pieces
Curb Form	Lin. Ft.	Detectable Vibration	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>0289</u>	Mason Dump Truck Truck #:	Backhoe #: .	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer	Utility Service Truck Truck #:
Other:				<u>0267</u>

COMMENTS:

went to 115th Asian (Powell), checked up Safety,
and opened up for Red. Then took safety - To Prince
and Ladyside, Break out green open up Both ramps
+ cut out ~~red~~ two Red

I CERTIFY THAT THE TIME OF THE EMPLOYEE'S RECORDING ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC
Signature _____
Title _____

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Bronx

Day Friday

Date 9.6.2013

SIGN IN

Name	Title	In	Out	Reg Hrs	OT Hrs	Signature	Supervisor's Remarks
Denochy Cowan	IHR	8:00	15:30	8	3	<i>Denochy Cowan</i>	
Isiah Hodge	IHR	5:00	15:30	8	2	<i>Isiah Hodge</i>	

ON STREET

144 Drive yard
46 St & Queens Blvd
115 Adam Clayton Powell Blvd

CROSS STREET

168 St & clay ave
Boston Road yard

WORK PERFORMED

WORK PERFORMED		MATERIALS USED		
SIDEWALK & CURE		Ready Mix Concrete		
Sidewalk Prep	Sq. Ft.	Lumber		Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight		Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose		Pieces
Curb Form	Lin. Ft.	Detectable Warning		Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints		Lin. Ft.
PREP & CAVE-IN		Snap Caps		
Debris Removal	Cu. Yds.	Caulking		Tube
Backfill	Cu. Yds.	Sesame Spray		Gal.
Asphalt Patch	Tons	Sand		Cu. Yds.
STEP STREETS		Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other: went to 168 St & clay ave		
Pointing/Caulking/Patching	Lin. Ft.	To help with pour		
Step Replacement	Lin. Ft.			

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: ✓ 5897	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tug-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

Comments: Check Various location

I CERTIFY THAT THE TIME OF THE EMPLOYEE IS RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

*Crew Leader: Denochy Cowan
Supervisor: Isiah Hodge*

001
I Q A T I D U S S U O U I
DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough QUEENS

Day TUESDAY

Date 09-10-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Miguel Morel	ACHR						
Fevrin Agenord	ACHR	5:20	16:30	8	3	<i>Fevrin Agenord</i>	
Frank Messina	ACHR					<i>Frank Messina</i>	
Edward Cotton	ACHR	6:00	14:30	8		<i>Edward Cotton</i>	

ON STREET <u>ADAM C. Powell</u> <u>PRINCE</u> <u>W-28 ST</u>	CROSS STREET <u>W-115</u> <u>LAFAYETTE</u> <u>WAY</u>
--	---

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Wall Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	7
Backfill	Cu. Yds.	Sealant Spray	Tube
Asphalt Patch	Tons	Sand	Gal.
STEP STREETS		Cu. Yds. Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	140	Lin. Ft.	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #: 0289
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer	Utility Service Truck Truck #: 0267
Other:				

COMMENTS:

Went to W-115 St / AC Powell get curbing done (35 lin ft) And go down Prince St / LAFAYETTE CAULKING 105 lin ft, striped clean-up location and set up safety. Bring more safety to W-28 st 3 ways Post for Wednesday.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK (PERFORMED) WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

[Handwritten Signature]

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
COBBLESTONE PROGRAM - DAILY GANG REPORT**

Borough

Bx

Day

WEEKEND

Date

9/11/13

SIGN IN

Name	Title	Ir.	10w.	Reg. Hrs	OT Hrs	Signature	Supervisor's Remarks
Michael O'Hare	Bricklayer	0500	1600	7	3 1/2	✓	
Chris Carrasquillo	HR	0530	1600	8	2	✓	
Jose Ortiz	HR	0530	1600	8	2	✓	

ON STREET

116TH

CROSS STREET

Adam Clayton Powell

WORK PERFORMED

MATERIALS USED

Cobblestone/Pavers	Ready Mix Concrete	Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone	Sq. Ft.
Pavers	Sq. Ft. Pavers	Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks	Ea.
Steps & Walls	Lumber	Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking	Tube
Step Replacement	Lin. Ft. Cement	Bags
Wall Forming	Sq. Ft. Mortar Mix	Bags
Wall Installing	Sq. Ft. Sand	Cu. Yds.
Prep & Cave-in	Stone	Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints	Lin. Ft.
Backfill	Cu. Yds. Detectable Warning	Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #: <u>658-26-00.0</u>	#:	Truck #:	Truck #: <u>1124977</u> ✓
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

At site finished filling joints/setting stones
match mix

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE CITY OF NEW YORK

Signature

All O/H

Title

Crew Leader

Approved By

Democracy C

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BK

Day Thursday

Date 9-12-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	O/Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0300	1430	8	1	Milagros Lopez	
Sean Thomas	ACHR	OFF	OFF	—	—	Sean Thomas	
Rohan Wilkinson	ACHR	0600	1430	8	0	Rohan Wilkinson	
Nicholas Depaola	ACHR	WALKED WITH GUY	OUT	—	—		

ON STREET	CROSS STREET
115 104, 105 106	ADAM CLAYTON POWELL COLUMBUS AVE

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other: Compost	10 yards
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: Pickup 7087	Light Duty Truck Truck #: 0014
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

M Lopez, Rohan W, and Rohan R met up at location. We cleaned area, then we raked out compost with the help of Joe Barzel. We made sure all locations was clean and safe, loaded mulch on truck. Some of the safety onto truck.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Milagros Lopez

Crew Leader

Supervisor

SSS

Non SSS

DOT/SIM/CITYWIDE CONCRETE

~~CONCRETE STONE PROJECT~~ - DAILY GANG REPORTBorough QUEENS 44± DRDay THURSDAYDate 9/12/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STORES ACME		3:00PM	3:00AM	8	4	AJ	
TELECOM HOME IMP		3:00PM	3:00AM	8	4	D. Thomas	

ON STREET 115± ST 7± AveCROSS STREET 115± ST. 7± Ave106±/105± ST. COLUMBUS106±/105± ST. COLUMBUS104± ST. COLUMBUS AVE104± ST. COLUMBUS AVELONGFOLLOW & BRICKNER BLVDLONGFOLLOW & BRICKNER BLVD

WORK PERFORMED

MATERIALS USED

Cobblestone/Pavers	Ready Mix Concrete	Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone	Sq. Ft.
Pavers	Sq. Ft. Pavers	Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks	Ea.
Steps & Walls	Lumber	Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking	Tube
Step Replacement	Lin. Ft. Cement	Bags
Wall Forming	Sq. Ft. Mortar Mix	Bags
Wall Installing	Sq. Ft. Sand	Cu. Yds.
Prep & Cave-In	Stone	Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints	Lin. Ft.
Backfill	Cu. Yds. Detectable Warning	Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
<u>Other: MINI RACK TRUCK #0367</u>				

COMMENTS:

SET UP SAFETY ON LONGFOLLOW & BRICKNER AVE, REMOVE
SAFETY ON 115± 7±, 106, 105, 104± ST. COLUMBUS AVE
RETURN TO 44± DR

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Leader

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Wednesday

Date 9-17-13

ON STREET	CROSS STREET
Burlington Rd.	Keep
Adam Clayton Powell	Wells
Harper yard	

WORK PERFORMED	MATERIALS USED	
SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP. & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT				
CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #: 0249	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other: None

COMMENTS:

Today we had one sewing job in Brooklyn, then we went to
Gardiner and removed carpet from the sofa, then went to Green's
to pick up supplies at the welding store.

[Signature] I CERTIFY THAT THE PAYMENT LISTED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

卷之三

Approved By

Title

Crew Leader

~~1000~~: Decr.

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Tuesday Date 8-27-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	06:00	16:30	8	2	W Butler	
Matthew Cutietta	ACHR	06:00	16:30	8	2	M. Cutietta	

ON STREET	CROSS STREET
W 75 St	Columbus Ave

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete King's 8 Cu. Yds.
Sidewalk Prep	Lumber Lin. Ft.
Sidewalk Pour 210	Steel Curb, Straight Lin. Ft.
Curb Prep	Steel Curb, Bull Nose Pieces
Curb Form	Detectable Warning 4 mats 2'x5' Sq. Ft.
Curb Pour	Expansion Joints 60 Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Sealant Spray Gal.
Asphalt Patch	Sand Cu. Yds.
STEP STREETS	Stone Cu. Yds.
Landing	Other: Moran on job site
Pointing/Caulking/Patching	
Step Replacement	William McQuade

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0026	Truck #: .	#:	Truck #: 0026	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 0025	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

Went to location on W 75 St / Columbus Ave
Ready mix concrete with King's 8 yards sidewalk pour 210 sq ft
Detectable warning 4 mats 2'x5' Expansion joints 60 lin ft.
Clean-up and self safety.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John Doe

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough QUEENS Day TUESDAY Date 08.27.13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	8	3	<i>Q. Bovell</i>	
Paul Bovell	ACHR	6:00	16:30	8	2		
Roger Williams	ACHR	6:00	16:30	8	2	<i>R. Williams</i>	
Thomas Kelly	CM	6:00	16:30	7	3	<i>K. Williams</i>	

ON STREET	CROSS STREET
	<i>Columbus Ave & W 108 st. south.</i>

WORK PERFORMED	MATERIALS USED	
SIDEWALK & CURB	Ready Mix Concrete	<i>4263</i> Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber Lin. Ft.
<i>Islands - poured - 203</i>	Sq. Ft.	Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose — Pieces
Curb Form	Lin. Ft.	Detectable Warning — <i>(2x5)4</i> Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints — <i>21.</i> Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking Tube
Backfill	Cu. Yds.	Sealant Spray <i>1/8</i> Gal.
Asphalt Patch	Tons	Sand Cu. Yds.
STEP STREETS	Cu. Yds.	Stone Cu. Yds.
Landing	Sq. Ft.	Other:
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>1122629</i>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <i>0019-D</i>	#:	Truck #:	#:	Truck #:

Comments: We went to location on Columbus Ave & W 108 st.

Also, we poured an island with Kings concrete. We used 6 cu/yards.
Also, we used 4. (2x5) Detectables, warnings - place drums.
Crew up & secured the job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Wednesday Date 8-28-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:30	16:30	8	3	Charles Restivo	
William Butler	ACHR					W. Butler	OUT
Matthew Cutietta	ACHR	06:00	16:30	8	2	M. Cutietta	

ON STREET	CROSS STREET
W 75 St	Columbus Ave
W 74 St	
MacPhee St	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep graded & tampered 210 Sq. Ft.	Lumber Tree Pit 3-2x8" Island 7-2x6" Lin. Ft.
Sidewalk Pour Sq. Ft.	Steel Curb, Straight Lin. Ft.
Curb Prep Island framed 74 Lin. Ft.	Steel Curb, Bull Nose 3½" Radius (1) Pieces
Curb Form Lin. Ft.	Detectable Warning Sq. Ft.
Curb Pour Lin. Ft.	Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal Cu. Yds.	Caulking Tube
Backfill Cu. Yds.	Sealant Spray Gal.
Asphalt Patch Tons	Sand Cu. Yds.
STEP STREETS Cu. Yds.	Stone Cu. Yds.
Landing Sq. Ft.	Other: Mason on job site
Pointing/Caulking/Patching Lin. Ft.	William McQuade
Step Replacement Lin. Ft.	Used 1 sheet masonite

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0026	Truck #:	#:	Truck #: 0026	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 0005	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

Went to location on W 75 St & Columbus stripped Island.
Went to location on W 74 St & Columbus Framed Island 74 lin ft.
Lumber Tree pit 2-(2"x4") 3-(2x8') Steel curb Bull nose st' Radius(1) pi
Clean-up Set safety.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

Jerry R. Restivo

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Wednesday. Date 08-28-13.

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	8	3	<i>[Signature]</i>	
Paul Bovell	ACHR	6:00	16:30	8	2	<i>[Signature]</i>	
Roger Williams	ACHR	6:00	16:30	8	2	<i>[Signature]</i>	
Thomas Kelly	CM	6:00	16:30	7	3	<i>[Signature]</i>	

ON STREET	CROSS STREET
<i>Columbus Ave.</i>	<i>at w 108 st & w 107 st. (north)</i>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
<i>Formed. Islands. → 20' 3'.</i>	Sq. Ft. Lumber → 120. → Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose → 1 → Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Caulking Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other: <i>Graffiti, & Tampons. (stone)</i>
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>1122627</i>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <i>1122627</i>	#:	Truck #:	#:	Truck #:

Other: *0019-D*

COMMENTS: *We went to location on Columbus Ave. & w 108 st.*

and removed the forms & clean up. & also we moved to w 107 st. & form as the islands (north) place. DRUMS & clean up & second time job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens. Day THURSDAY, Date 08.29.13.

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	8	3	<u>Alzate</u>	
Paul Bovell	ACHR	6:00	16:30	8	2	<u>Bovell</u>	
Roger Williams	ACHR	6:00	16:30	8	2	<u>Williams</u>	
Thomas Kelly	CM	6:00	16:30	10	3	<u>Kelly</u>	

ON STREET	CROSS STREET
<u>Columbus Ave</u>	<u>W 107 st. with.</u>

WORK PERFORMED	MATERIALS USED	HOURS
SIDEWALK & CURB	Ready Mix Concrete	→ 6 → Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Poured. Islands. → 203 →	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning → (2x5) - 4 →	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints → 21 →	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Caulking	Tube
Backfill	Cu. Yds. Sealant Spray → 1/8 →	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>1122621</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u></u>	#:	Truck #:	#:	Truck #:

Other: 0019-D.

COMMENTS:

We Went to Location on Columbus Ave. & W. 107 st. and poured an Islands with Kings concrete. We used about 6 cu/yards. place drums. Color up. & Second. like job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Thursday Date 8-29-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	06:00	16:30	8	2	W Butler	
Matthew Cutietta	ACHR	06:00	16:30	8	2	M Cutietta	

ON STREET	CROSS STREET
W 74 St	Columbus Ave

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete King's 7 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	210 Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose 3 1/2' Radius (1) Piece
Curb Form	Lin. Ft. Detectable Warning 4 mats 2x5' Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints 30 Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other: Mason on job site
Pointing/Caulking/Patching	Lin. Ft. William McQuade
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0005	Truck #: #:	#:	Truck #: 0026	Truck #: #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 0005	#:	Truck #: #:	#:	Truck #: #:

Other:

COMMENTS:

Went to location on W 74 St / Columbus Ave
Ready mix concrete with King's 7 yards sidewalk pour 210 sq ft.
Steel curb, bull nose 3 1/2' radius (1) piece Detectable warning
4 mats 2x5'. Clean-up and set safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Charles Restivo

Crew Leader

Jeanne

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens, Day Friday, Date 08-30-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	3	3	<i>[Signature]</i>	
Paul Bovell	ACHR	6:00	16:30	8	2		
Roger Williams	ACHR	6:02	16:30	8	2	<i>R. Williams</i>	
	CM						

ON STREET	CROSS STREET
<i>Columbus Ave</i>	<i>107 st. north</i>
	<i>107 st. south</i>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep <i>→ 203 →</i>	Lumber <i>→ 120 →</i> Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose <i>→ 1 → 8</i> Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other: <i>GROUTED & TAMPED (stone)</i>
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT				
CrewCab Mason Truck Truck #: <i>1122627</i>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other: <i>0019-D-</i>				

COMMENTS: *We went to do on Columbus Ave & 107 st. north.
And formed an island. Also, we removed the forms on
108 st. south & clean up, place stones, & secure
the job site.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

[Signature]

Supervisor

Kelly Hernas - poured. For Rey GABERT.

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Friday Date 8-30-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	06:00	16:30	8	2	W Butler	
Matthew Cutietta	ACHR	06:00	16:30	8	2	M. Cutietta	

ON STREET	CROSS STREET
W 73 St	Columbus Ave

WORK PERFORMED		MATERIALS USED		
SIDEWALK & CURB		Ready Mix Concrete <u>Tripit Island</u> Cu. Yds.		
Sidewalk Prep	graded & tamped 210	Sq. Ft.	Lumber <u>3(2'x8')</u>	<u>7x(2x6')</u> Lin. Ft.
Sidewalk Pour		Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	74	Lin. Ft.	Steel Curb, Bull Nose	<u>3 1/2' Radius (1)</u> Pieces
Curb Form		Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour		Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps Lin. Ft.		
Debris Removal		Cu. Yds.	Caulking	Tube
Backfill		Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch		Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Stone	Cu. Yds.
Landing		Sq. Ft.	Other:	
Pointing/Caulking/Patching		Lin. Ft.		
Step Replacement		Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #: <u>0026</u>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u>0005</u>	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

Went to location on W. 73 St / Columbus Ave
Sidewalk prep graded & tamped 210 sq ft. Curb prep used 7(2x6')
lumber for Island & 3(2"x8") for the pit. Steel curb bull nose
3 1/2' Radius (1) piece. Clean up & set set 50ft tv

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John P. Hanrahan

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Tuesday Date 9 - 3 - 13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	06:00	16:30	8	2	W Butler	
Matthew Cutietta	ACHR	06:00	16:30	8	2	M Cutietta	

ON STREET	CROSS STREET
W 73 St	Columbus Ave

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete King's 7 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	210 Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning 4 mats 2x5 Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints 30 Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other: Mason on job site
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft. William McQuade

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: 0026	Light Duty Truck Truck #:
Medium Dump Truck Truck #: 0005	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Went to location on W 73 st / Columbus Ave
Ready mix concrete King's 7 yards Sidewalk pour 210 sq ft
Retractable warning + mats 2' x 5' Expansion joints 30 lin ft.
Clean-up & set safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Charles Restivo

Crew Leader

John Lavelle

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens, Day Tuesday, Date 09-03-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	8	3		
Paul Bovell	ACHR	6:00	16:30	8	2	Bover	
Roger Williams	ACHR						A/C-
Thomas Kelly	CM	6:00	13:30	7	2	TK	

ON STREET	CROSS STREET
<u>Columbus Ave</u>	<u>at 107 St South,</u>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete <u>KINGS</u> → 6 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
<u>ISLANDS Poured. 203.</u>	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning → (2x5) → 4 Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints → 21 → Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray → 1/8 → Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>1122627</u>	Mason Dump Truck Truck #: .	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #: .	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other: <u>0019-D.</u>				

COMMENTS:

We went to location on Columbus Ave.
at 107 south & pour. An Islands. with
Kings concrete. uses 6 cu. yds. & 4 mats. (2x5)
place down. clean up & secured. It the job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens, Day Wednesday, Date 09-04-13.

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	8	3		
Paul Bovell	ACHR	6:00	16:30	8	2	BOVELL	
Roger Williams	ACHR						
Thomas Kelly	CM	6:00	16:30	7	3	THOMAS	A/L -

ON STREET	CROSS STREET
COLUMBUS AVE.	X W 107 ST. SOUTH.
COLUMBUS AVE.	X W 106 ST. SOUTH.

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep → 203 →	Lumber → 140 → Lin. Ft.
Sidewalk Pour	Steel Curb, Straight Lin. Ft.
Curb Prep	Steel Curb (Bull Nose) → 1 → Pieces
Curb Form	Detectable Warning Sq. Ft.
Curb Pour	Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Sealant Spray Gal.
Asphalt Patch	Sand Cu. Yds.
STEP STREETS	Stone Cu. Yds.
Landing	Other: GRADE. & TAMPED. THE step.
Pointing/Caulking/Patching	
Step Replacement	

VEHICLES & EQUIPMENT				
CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 1122627	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other: 0019 D-				

COMMENTS: WE WENT TO LOCATION ON COLUMBUS AVE X W 107 ST SOUTH AND REMOVED THE FORMS & CLEAN UP. ALSO ON W 106 ST SOUTH. WE FORMED AN ISLAND & USED A BULL NOSE (STEEL) PLATE. DRAINS CLEAN UP & SECURED THE JOB SITE.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Wednesday Date 9-4-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	06:00	16:30	8	2	W Butler	
Matthew Cutietta	ACHR	06:00	16:30	8	2	M. Cutietta	

ON STREET	CROSS STREET
<u>W 73 St</u>	<u>Columbus Ave</u>

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	<u>Graded & Tamped 210 Sq. Ft.</u>	Lumber <u>2 - 2" x 8" Tree pit 24 Lin. Ft.</u>	
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose <u>3 1/2' Radius (1)</u>	Pieces
Curb Form	<u>74 Lin. Ft.</u>	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0005</u>	Truck #: <u>0005</u>	#: <u>0026</u>	Truck #: <u>0026</u>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u>0005</u>	#: <u>0005</u>	Truck #: <u>0026</u>	#: <u>0026</u>	Truck #:

Other:

COMMENTS:

Went to location on W 73 St / Columbus Ave
Sidewalk prep graded & tamped 210 sq ft. Framed curb
Forms 74 lin.ft., Steel Curb, bull nose 3 1/2' Radius (1) prep
Clean-up and set safety Tree Pit 7'x5' used 2-2" x 8'

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Charles Restivo

Crew Leader

Javier Lira

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Thursday Date 9-5-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	06:00	16:30	8	2	W Butler	
Matthew Cutietta	ACHR	06:00	16:30	8	2	M Cutietta	

ON STREET	CROSS STREET
W 73 St	Columbus Ave

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	King's 7 Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	210 Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	4 mats 2' x 5' Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	30 Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other: Mason on job site	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.	William McQuade	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0026	Truck #:	#:	Truck #: 0026	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 0005	#:	Truck #:	#:	Truck #:

Other:

Comments:

Went to location on W 73 St / Columbus Ave
Ready mix concrete with King's 7 yards sidewalk pour 210 sq ft
Detectable warning 4 mats 2' x 5' Expansion joints 30 lin ft.
Clean up & set safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By



Title

Supervisor

09.05.13

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough QUEENS

Day THURSDAY

Date 09-05-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	8	3	<i>J</i>	
Paul Bovell	ACHR	6:00	16:30	8	2	<i>P. Bovell</i>	
Roger Williams	ACHR						
Thomas Kelly	CM	6:00	16:30	7	3	<i>T. Kelly</i>	A/L -

ON STREET	CROSS STREET
<i>Columbus Ave. & w 106 st. west.</i>	
<i>Re-Action on Clintonville St.</i>	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	<i>KINGS</i>
Sidewalk Prep	Ready Mix Concrete <i>→ D J →</i> Cu. Yds.
Sidewalk Pour	Lumber Lin. Ft.
Curb Prep	Steel Curb, Straight Lin. Ft.
Curb Form	Steel Curb, Bull Nose Pieces
Curb Pour	Detectable Warning <i>→ (2x5) → 4</i> Cu. Ft.
PREP & CAVE-IN	Expansion Joints <i>→ 4 →</i> Lin. Ft.
Debris Removal	Snap Caps Lin. Ft.
Backfill	Caulking Tube
Asphalt Patch	Sealant Spray <i>→ 1/8 → P</i> Gal.
STEP STREETS	Sand Cu. Yds.
Landing	Stone Cu. Yds.
Pointing/Caulking/Patching	Other:
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>1122627</i>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <i>0019</i>	#:	Truck #:	#:	Truck #:

Other: *0019*

COMMENTS:

We went to location on Columbus Ave & W 106 st. north & poured an island. W/ 11 ft. Kings concrete. We used about 5 cu/yards. & (2x5) → 4 detectable warnings. place. Onwards. Clean up. & secured site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

[Signature]
Crew Leader
[Signature]
Supervisor

JOB. site

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Friday Date 9-6-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	05:00	15:30	8	2	W Butler	
Matthew Cutietta	ACHR	05:00	15:30	8	2	M Cutietta	

ON STREET	CROSS STREET
W 71 St	Columbus Ave

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Frame Island Cu. Yds.
Sidewalk Prep	Graded & Tamped 238 Sq. Ft.	Lumber Tree P't 2-2'x8'/8-2"x6"	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Frame Island 82 Lin. Ft.	Steel Curb, Bull Nose B5 Radius (1) Pieces	
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other: Mason on job site	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.	William McQuade	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #: 0026	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 0005	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

Went to location W 71 St / Columbus Ave
Side walk prep graded & tamped 238 sq ft. Curb form island 82 lin ft.
Lumber Tree P't 2-2'x8'/8-2"x6" Steel curb bull nose
B5 Radius (1) prep clean up & set safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Charles Restivo

Crew Leader

J

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough QUEENS Day Friday Date 09.06.13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	3	3		
Paul Bovell	ACHR	6:00	16:30	8	2	<i>BOVELL</i>	
Roger Williams	ACHR						
Thomas Kelly	CM	6:00	16:30	7	3		A/L-

ON STREET	CROSS STREET
<i>Columbus Ave.</i>	<i>W 106 St. south.</i>
<i>Columbus Ave.</i>	<i>W 105 St. north</i>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep → 203 → Sq. Ft.	Lumber → 120 → Lin. Ft.
Sidewalk Pour Sq. Ft.	Steel Curb, Straight Lin. Ft.
<i>Formed Islands. — 120</i> Lin. Ft.	Steel Curb, Bull Nose → 1 → Pieces
<i>Removed forms → 120</i> Lin. Ft.	Detectable Warning Sq. Ft.
Curb Pour Lin. Ft.	Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal Cu. Yds.	Caulking Tube
Backfill Cu. Yds.	Sealant Spray Gal.
Asphalt Patch Tons	Sand Cu. Yds.
STEP STREETS Cu. Yds.	Stone Cu. Yds.
Landing Sq. Ft.	Other: <i>Graded & prepared. (stone)</i>
Pointing/Caulking/Patching Lin. Ft.	
Step Replacement Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 112262	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:		Truck #:	#:	Truck #:

Other: 0019 D

COMMENTS: We went to location on Columbus Ave. & W 106 St. south

And removed tile form. Also we formed an island.

on. W 105 St. north. place. drums. Clean up & secured site.

JOB SITE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Saturday Date 9-7-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	06:00	14:190		8	Charles Restivo	
William Butler	ACHR	06:00	14:30		8	W Butler	
Matthew Cutietta	ACHR	06:00	14:30		8	M. Cutietta	

ON STREET	CROSS STREET
W 71 St	Columbus Ave

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	King's 7 Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	238 Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	4 mats (2'x5') Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	30 Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other: <i>McGon on job site</i>	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.	William McQuade	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0026	Truck #: 0026	#:	Truck #: 0026	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 0005	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

*Went to location on W 71 St / Columbus Ave
Ready mix concrete with King's 7 yards sidewalk
Detectable warning 4 mats (2'x5') Expansion joint 30 lin. ft.
Clean-up + set safety*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Charles Restivo

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough QUEENS

Day Saturday

Date 09-07-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	6:00	14:30		8	<i>J.</i>	
Paul Bovell	ACHR	6:00	14:30		8	<i>P. Bovell</i>	
Roger Williams	ACHR						
Steve Feske	ACHR	6:00	14:30		8	<i>Steve F.</i>	
Ray Cabezas	ACHR	6:00	14:30		8	<i>Ray C.</i>	
Tony McCain	CM	6:00	14:30		8	<i>Tony M.</i>	

ON STREET	CROSS STREET
<i>COLUMBUS AVE.</i>	<i>W 105 st. north</i>

WORK PERFORMED	MATERIALS USED	<i>Kings</i>
SIDEWALK & CURB	Ready Mix Concrete → 6 → Cu. Yds.	
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
<i>poured Island → 203 →</i>	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning → 4 (xx) →	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints → 21 →	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Caulking	Tube
Backfill	Cu. Yds. Sealant Spray → 1/8 → Gal.	
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT				
CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>1122620</i>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <i>0019-D</i>	#:	Truck #:	#:	Truck #:
Other: <i>0019-D</i>				

COMMENTS:

We went to do a job on Columbus Ave. & W 105 st. and poured an island with Kings concrete. We used about 6 cu. yards. & (4) Detectable warnings placed down. Clean up and secured the job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/S M/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Tuesday

Date 8/13/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	15:30	8	2	<u>J. Taranto</u>	

ON STREET

College Point yard (Qu)
204 St + Linden Blvd (Qu)
209 St at Hollis Ave

CROSS STREET

158 Ave + 101 St (Qu)
Columbus Ave - 110 St (Man)

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLE & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

went to 204 St + 209 St to take photos of job site.
went to Columbus Ave + 110 St to check future job locations.
checked on crews at location.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC


Signature

Crew Leader



Approved By

Supervisor



DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough BK

Day Tuesday

Date Aug-13-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0500	1430	8	1	<u>Milagros Lopez</u>	
Sean Thomas	ACHR	0606	1430	8	0	<u>Sean Thomas</u>	
Rohan Wilkinson	ACHR	OFF	—	OFF	—	<u>Rohan Wilkinson</u>	
Nicholas Depaola	ACHR	WORKED with Carl	—	—	—	<u>Nicholas Depaola</u>	

ON STREET	CROSS STREET
<u>Columbus Ave</u>	<u>110 St</u>

WORK PERFORMED	MATERIALS USED		
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.		
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.		
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: <u>PICKUP</u> <u>7047</u>	Light Duty Truck Truck #: <u>004U</u>
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Gang and Robby drove to location.
Helped Jerry with safety. Shawn and
Robby went to the Bronx to pick up a truck.
Milagros drove back to the yard.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Title

Supervisor

Milagros Lopez RAIN DAY

**DOT/SIM/CITYWIDE CONCRETE
~~COBBLESTONE PROGRAM~~ - DAILY GANG REPORT**

Borough Queens 44th dr

Day Tuesday

Date 8/13/13

SIGN IN

from 44th St.

ON STREET	CROSS STREET
110th St. Columbus Ave	110th St. Columbus Ave

RETURN TO 44± DR.

WORK PERFORMED		MATERIALS USED	
Cobblestone/Pavers		Ready Mix Concrete	Cu. Yds.
Cobblestone	Sq. Ft.	Cobblestone	Sq. Ft.
Pavers	Sq. Ft.	Pavers	Sq. Ft.
Concrete Roadbase	Sq. Ft.	Cinder Blocks/Bricks	Ea.
Steps & Walls		Lumber	Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft.	Caulking	Tube
Step Replacement	Lin. Ft.	Cement	Bags
Wall Forming	Sq. Ft.	Mortar Mix	Bags
Wall Installing	Sq. Ft.	Sand	Cu. Yds.
Prep & Cave-In		Stone	Cu. Yds.
Debris Removal	Cu. Yds.	Expansion Joints	Lin. Ft.
Backfill	Cu. Yds.	Detectable Warning	Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
<i>Other: Back Truck #367</i>				

Other: MIN. RACK TRUCK #0367

COMMENTS:

SET OF SAFETY FOR SAW CUT —

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

11

~~Supervisor~~

BUREAU OF STREET CONCRETE

D. ILY GANG REPORT

Borough QUEENSDay TUESDAYDate 08-13-13

SIGN IN

Name	Title	In	Out	R Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	14:30	8	1	<i>[Signature]</i>	
Thomas Kelly	Mason	7:00	15:30	7	1	<i>[Signature]</i>	
Paul Bovell	ACHR	6:00	14:30	8	—	<i>[Signature]</i>	
Roger Williams	ACHR	6:00	14:30	8	—	<i>[Signature]</i>	

ON STREET

158 Ave. K CENTERLINE 101 st. HOWARD BEACH.
QUEEN S. PLANT.

WORK PERFORMED

SIDEWALK & CURB	MATERIALS USED
Sidewalk Prep	Ready Mix Concrete Cu. Yds.
Sidewalk Pour	Sq. Ft. Lumber Lin. Ft.
Curb Prep	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Form	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Pour	Lin. Ft. Detectable Warning Sq. Ft.
PREP & CAVE-IN	Expansion Joints Lin. Ft.
Debris Removal	Snap Caps Lin. Ft.
Backfill	cu. Yds. Caulking Tube
Asphalt Patch	cu. Yds. Sealant Spray Gal.
STEP/STREETS	
Landing	Tons Sand Cu. Yds.
Pointing/Caulking/Patching	cu. Yds. Stone Cu. Yds.
Step Replacement	Lin. Ft. Other:

VEHICLES & EQUIPMENT

Crew Cab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other: <u>1260</u>	<u>48 DR</u>			

COMMENTS:

Because of the rain we went to Howard on 158 ave x 101 st. Howard Beach to check on safety. Also we went to Centerline Ave. x 110 st. We pick up 48 DR from Queens plant.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BK

Day Wednesday

Date Aug-14-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0500	1630	8	3	D. Lopez	
Sean Thomas	ACHR	0600	1630	8	2	S. Thomas	
Rohan Wilkinson	ACHR	0600	1430	8	0	R. Wilkinson	
Nicholas Depaola	ACHR	Worked with	Cali's gang		2		

ON STREET	CROSS STREET
<u>Columbus Ave</u>	<u>110 St</u> <u>115 Lin FT</u>
<u>Columbus Ave</u> <u>SOUTH & NORTH</u>	<u>197th St</u> <u>90x2 = 180 Lin FT</u>

WORK PERFORMED	MATERIALS USED		
SIDWALK & CURB	Ready Mix Concrete Cu. Yds.		
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.		
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other: <u>SAW CUT 295 Lin FT</u>	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: <u>PICK UP</u> <u>7087</u>	Light Duty Truck Truck #: <u>0244</u>
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #: <u>0D14</u>

Other:

COMMENTS:

Gang met up at location, we saw cut required areas. During the process of saw cutting, the Disk that holds the blade in place broke. In like drive to 44 Drive and picked up another disk. We were able to complete the job, made sure all locations was clean and safe....

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

IN THE MORNING BY WORK, M. LOPEZ Moved His Locker TO 297TH ST YARD

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough SI

Day Wed

Date 8-14-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR	500	1730	8	4	F. Cammalleri	
Jason James	HR	600	1630	8	2	Jason	Worked with Lacey
Alvaro Arias	HR	1000	1130	8		Alex.	Worked with Alex.

ON STREET	<u>JASON</u>	CROSS STREET	<u>ALVARO</u>
110	<u>Columbus</u>		<u>Spring Field</u>

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #: 752 754	Truck #: 6836
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

COMMENTS: Went to all location left safe

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title



Approved By

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BKLYN

Day WED

Date 8-14-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Lawrence Johnson	MGO	5:00	1630	8	3	<i>L. Johnson</i>	
Julio Samayoa	ACHR	5:00	1630	8	3	<i>Julio Samayoa</i>	
T. Thomas	HR	6:00	1630	8	2		
J. James	HR	6:00	1630	8	2		

ON STREET	CROSS STREET
<u>COLUMBUS AV</u>	<u>110TH ST & 109TH ST</u>

WORK PERFORMED	MATERIALS USED	
SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	22 Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	10 Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	# <i>0004</i>	Truck # <i>736T</i> <i>75477117</i>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	Truck #:	Truck #:	# <i>5004</i>	Truck #:

Other:

COMMENTS: EXCAVATION & SPREADED STONE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Crew Leader

[Handwritten Signature]

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
COBBLESTONE PROGRAM - DAILY GANG REPORT**

Borough Queens 44-120

Day Wednesday

Date 8/14/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STOKES	ACHR	6:00	4:30	8	2	<i>JF</i>	

from 44-120

ON STREET	CROSS STREET
110th St. Columbus Ave	110th St. Columbus Ave

Returned to 44-120

WORK PERFORMED	MATERIALS USED
Cobblestone/Pavers	Ready Mix Concrete Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone Sq. Ft.
Pavers	Sq. Ft. Pavers Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks Ea.
Steps & Walls	Lumber Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking Tube
Step Replacement	Lin. Ft. Cement Bags
Wall Forming	Sq. Ft. Mortar Mix Bags
Wall Installing	Sq. Ft. Sand Cu. Yds.
Prep & Cave-In	Stone Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints Lin. Ft.
Backfill	Cu. Yds. Detectable Warning Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
<i>Other: MINI BACK TRUCK #0367</i>				

COMMENTS:

*SET UP SAFETY FOR SAW CUT, EXCAVATION CREW —
ON 110TH ST. COLUMBUS AVE —*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

JF

Title

Crew Leader

Approved By

JF

Title

Supervisor

DAILY GANG REPORT

Borough QueensDay 17 June Day, Date 08/15/13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	7:00	16:30	8	3		
Thomas Kelly	Mason	6:00	16:30	7	3	T. Kelly	
Paul Bovell	ACHR	6:00	16:30	8	2	P. Bovell	
Roger Williams	ACHR	6:00	16:30	8	2	R. Williams	

ON STREET

CROSS STREET

Columbus Ave & 110 St.

WORK PERFORMED

SIDEWALK & CURB

prep. Islands to 266

Sidewalk Pour

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete

Cu. Yds.

Lumber → (2x6) → 130 → Lin. Ft.

Steel Curb, Straight

Lin. Ft.

Steel Curb, Bull Nose → 1 →

Pieces (35)

Detectable Warning

Sq. Ft.

Expansion Joints

Lin. Ft.

Snap Caps

Lin. Ft.

Caulking

Tube

Sealant Spray

Gal.

Sand

Cu. Yds.

Stone

Cu. Yds.

Other: Graded & prepared the stone -

Lin. Ft.

Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>112627</u>	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #: #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other: <u>126 D</u>				

COMMENTS:

We Went to location on Columbus Ave & 110 St.
 X Graded & prepared the site. Also we Foreign the refrigerated
 Islands & used a Bull nose. Please Dennis. Clean up.
 d. secured the job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT SED WALK INSPECTION MANAGEMENT
CITYWIDE CONCRETE PROGRAM - DAILY GANG REPORT**

Borough: DUPPCDate: 8-15-13 (Thur)**SIGN IN**

Name	Title	In	Out
M. Graf	ACIAA	6:00	14:30
S. Thomas	ACIAA	6:00	16:30
T. Johnson/RM	ACIAA	5:00	
R. Robinson			
Total Hrs.			

Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
8		M. Graf	
8	2	Sean Thomas	
8		Johnson/RM	
—	—	—	out A/C

Location

From	To
44 Dr	765 Columbus Ave

STEP STREETS

Coping	
Sidewalk	
Walls	
Pointing & Patching	
MATERIAL USED	
Ready Mix	
Hand Mix	
Cement	
Sand/Stone	
Lumber	
Expansion Joint	

PREP & CAVE-IN		
in. Ft.	Fill	Cu. Yd.
sq. Ft.	Debris	Cu. Yd.
in. Ft.	Opening	Sq. Yd.
in. Ft.		
CURE WORK		
cu. Yd.	Sidewalk Prep	Sq. Ft.
cu. Yd.	Sidewalk Pour	Sq. Ft.
sq. ft.	Curb Prep	Lin. Ft.
cu. Yd.	Curb Pour	Lin. Ft.
in. Ft.	Paving Block	Unit
in.	Forming	Lin. Ft.

VEHICLES	
CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator
Other: RACK 0249	RACK 0244

BACKHOE	LARGE DUMP TRUCK	LIGHT DUTY TRUCK
Truck #:	Truck #:	Truck #:
Towmaster	X-Log-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:

Comments: Loaded truck at 9 am with safety and went to location.
 At 76 ft. + Columbus ave set up safety and saw cut
 2,500 lbs. Robbie & Sean also did safety for excavation of island 5

I CERTIFY THAT THE TIME OF THE EMPLOYEE'S RECORDED ABOVE IS CORRECT AND THAT THE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF THE CITY OF NEW YORK

Signature

Title

Approved By

Title

M. Graf
Noel D. N.

Citywide Concrete Program

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Thursday

Date 8/15/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	16:30	8	3		
Gadiel Salas	ACHR	5:00	16:30	8	3	<i>M. Salas</i>	
75 Jason James	HRS	6:06	16:30	8	2		

ON STREET	CROSS STREET
<i>Colombus</i>	<i>ave</i>
	<i>76 st</i>

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	<i>60</i> Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds. Stone	<i>20</i> Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #: <i>0004</i>	Large Dump Truck Truck #: <i>754</i> <i>737</i>	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #: <i>5009</i>	Utility Service Truck Truck #:

Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BKLYN

Day Tue

Date 8-15-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Lawrence Johnson	MGO	5:00	1630	8	3	<u>Lawrence Johnson</u>	
Julio Samayo	ACHR	5:00	1630	8	3	<u>Julio Samayo</u>	
<u>T. Thomas</u>	<u>HR</u>	<u>6:00</u>	<u>1630</u>	<u>8</u>	<u>2</u>		
<u>J. James</u>	<u>HR</u>	<u>6:00</u>	<u>1630</u>	<u>8</u>	<u>2</u>		

ON STREET	CROSS STREET
<u>COLUMBUS AV & W 109 ST N & S</u>	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	44 Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone 22 Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#: 0006	Truck #: 736 T 751T-784T	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	Truck #:	Truck #:	#: 5004	Truck #:

Other:

COMMENTS: EXCAVATION & SPREADED STONE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Crew Leader

**DOT/S M/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Thursday

Date 8/15/13

SIGN IN

ON STREET

College Point yard (av)
Colubus Ave & 110st - 76 + (Plan) CRO

CROSS STREET

WORK PERFORMED

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Shap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				1190871

[COMI](#)

JOURNAL

Waited for far
charge ceiling tiles to come to the office to
test checked on crews & locations

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC
Signature

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough S I

Day Thursday

Date 8 - 15 - 13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR	5 08	1630	8	3	J-Cammalleri	
Jason James	HR	6 00	1630	8	2	J. James	
Alvaro Arias	HR	1000	1530	8	1	A. Arias	Worked with JOE

ON STREET

ALVERO

CROSS STREET

JASON

Richmond Terrace/Bay Street

Columbus

and 101 St

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB			
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
		Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: 754 T 752 T	Light Duty Truck Truck #: 6836
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

Cheeked in locations. All safe
Damon delivered supply to yard
Lauing Cheeked out yard.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

F. Cammalleri
Supervisor

**DOT/SIM/CITYWIDE CONCRETE
COBBLESTONE PROGRAM - DAILY GANG REPORT**

Borough Queens 44+

Day Friday

Date 8/16/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STOUTS ACTA		6:00	2:30	8		<i>LL</i>	

from 44+ DC

ON STREET	CROSS STREET
74± 175± st. COLUMBUS AVE	74± 175± st. COLUMBUS AVE
107± st 108± st COLUMBUS	107± 108± st. COLUMBUS ave
BAY ST. RICHMOND TERRACE	BAY ST. RICHMOND TERRACE

WORK PERFORMED	MATERIALS USED
Cobblestone/Pavers	Ready Mix Concrete Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone Sq. Ft.
Pavers	Sq. Ft. Pavers Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks Ea.
Steps & Walls	Lumber Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking Tube
Step Replacement	Lin. Ft. Cement Bags
Wall Forming	Sq. Ft. Mortar Mix Bags
Wall Installing	Sq. Ft. Sand Cu. Yds.
Prep & Cave-In	Stone Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints Lin. Ft.
Backfill	Cu. Yds. Detectable Warning Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
<i>Other: MINI BACK TRUCK #0367</i>				

COMMENTS:

*SET UP SAFETY FOR SAW CUT, EXCAVATION CREWS
ON 75± st. COLUMBUS AVE, 108± st. COLUMBUS AVE
POST SIGNAGE ON 74± - 107± st. COLUMBUS AVE
REMOVED BARRIERS FROM BAY ST. RICHMOND TERRACE 13
RETURNED TO 44± DR.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

DOCK LANE & WIDE CONCRETE
DAILY GANG REPORT

Borough OCEAN

Day FRIDAY

Date 08-16-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	3	3	<i>[Signature]</i>	
Thomas Kelly	Mason	6:00	16:30	7	3	<i>[Signature]</i>	
Paul Bovell	ACHR	6:00	16:30	8	2	<i>[Signature]</i>	
Roger Williams	ACHR	6:00	16:30	8	2	<i>[Signature]</i>	

ON STREET

CROSS STREET
<i>COLUMBUS AVE</i>
<i>110 ST</i>
<i>44 YRS</i>

WORK PERFORMED

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete <i>Kings</i> 8 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
<i>PURCHASE ISLANDS 161</i>	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints 40 Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	L. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>1122627</i>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <i>125 D. 0019</i>	#:	Truck #:	#:	Truck #:

COMMENTS:

We went to location on Columbus Ave. & 10 St and worked at Island with Kings Concrete. We used about 8 cu. yds. Also we pick up a truck from 440 4 yrs. 0019. place drums. Clean up & sign off the job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT

AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SB/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Friday

Date

8/16/13

SIGN IN

ON STREET

College point yard (sq.)
Columbus Ave at 110 St (sq.m.)

CROSS STREET

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
PREP & CAVE-IN		Expansion Joints	Lin. Ft.
Debris Removal	Cu. Yds.	Snap Caps	Lin. Ft.
Backfill	Cu. Yds.	Caulking	Tube
Asphalt Patch	Tons	Sealant Spray	Gal.
Sand		Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLE & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Went to Colum- is all & most to help Leo
Crew with po & checked on crew. 2 locations.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Tide

Approved By

Title

Aug 19 2013 06:59am P002

Fax: 718-353-6381

100

**DOT/S/C/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Bronx

Day Friday

Date 3-16-13

SIGN IN

Name	Title	In	Out	F. Hrs.	OT Hrs	Signature	Supervisor's Remarks
Charles Restivo	HR	05:30	16:30	8	3	Charles Restivo	
William Butler	ACHR	05:30	15:30	8	2	W BUTLER	
Oscar Kehoe	ACHR						
Matthew Cutieta	ACHR	05:30	15:30	8	2	Matthew Cutieta	

ON STREET

CROSS STREET

W. 76 St

Columbus Ave (South)

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep <u>Graded + Tempered 210 Sq. Ft.</u>	Lumber <u>8 - 2" x 6" / 3 - 2" x 8"</u>	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal:	Caulking	Tube
Backfill:	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other: <u>Marvin on job site</u>	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement:	Lin. Ft. <u>William McQuade</u>	

VEHICLE & EQUIPMENT

Crew Cab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #: <u>0005</u>	Hydraulic Excavator	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

Comments: Went to location on W 76 St | Columbus Ave (South)
Sidewalk prep graded + tempered 210 sq ft
Framed 30' x 1' used 8 pieces 2" x 6 and 3 pieces 2x8'
of lumber. Clos up + set safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John R. Restivo

Title

Supervisor

DOT SUD WALK INSPECTION MANAGEMENT
CITYWIDE CONCRETE PROGRAM - DAILY GANG REPORT

Borough:

Queens

Date: 8-16-13 (F)

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
M Goss	ACMR	600	1430	8		M Goss	
R Wilkinson	ACMR	600	1420	8			
Total Hrs.							

Location

From	To
44 Dr	75 th Columbus
75 th Columbus	108 th Columbus

STEP STREETS

Coping

Sidewalk

Walls

Pointing & Patching

MATERIAL USED

Ready Mix

Hand Mix

Cement

Sand/Stone

Lumber

Expansion Joint

PREP & CAVE-IN		
in. Ft.	Fill	Cu. Yd.
sq. Ft.	Debris	Cu. Yd.
cu. Ft.	Opening	Sq. Yd.
in. Ft.		

CURB WORK		
u. Yd.	Sidewalk Prep	Sq. Ft.
u. Yd.	Sidewalk Pour	Sq. Ft.
u. Yd.	Curb Prep	Lin. Ft.
u. Yd.	Curb Pour	Lin. Ft.
in. Ft.	Paving Block	Unit
in.	Forming	Lin. Ft.

VEHICLES & EQUIPMENT		
CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Large Dump Truck Truck #:
Other: RA/15 0249		Light Duty Truck Truck #:
		Towmaster Truck #:
		Tag-A-Long Trailer #:
		Utility Service Truck Truck #:

Comments: Went to 75th & Columbus ave and 108th & Columbus ave and saw cut 145 ft. of street left safety for excavation crew

I CERTIFY THAT THE TIME OF THE EMPLOYEE IS RECORDED ABOVE IS CORRECT AND THAT THE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF THE CITY OF NEW YORK


Signature

Title

Approved By

Title

Supervisor



Noel B. C.
Citywide Concrete Program

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Boro Mtn

Day Fr. day

Date 8/16/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	16:30	8	3		
Gadiel Salas	ACHR	6:00	12:30	8	2	H. Salas	

ON STREET

Columbus Ave

CROSS STREET

75 St - 108 St

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#: <u>0004</u>	Truck #: <u>735T</u> <u>737T</u>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#: <u>5009</u>	Truck #:
Other:				

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader 

Title

Approved By

Title

Supervisor

DAILY GANG REPORT

Borough Queens

Day Fri, 26

Date 8/16/13

SIGN IN

ON STREET

Feb 12, 1980 8-71-2

CROSS STREET

RECEIVED

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	Sc. F.
Sidewalk Pour	Sc. F.
Curb Prep	Lir. P.
Curb Form	Lir. P.
Curb Pour	Lir. P.
PREP & CAVE IN	
Debris Removal	Cu. Yd.
Backfill	Cu. Yd.
Asphalt Patch	Ton.
STEP STREETS	
Landing	Sc. P.
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

MATERIALS USED

Ready Mix Concrete	Cu. Yds.
Lumber	Lin. Ft.
Steel Curb, Straight	Lin. Ft.
Steel Curb, Bull Nose	Pieces
Detectable Warning	Sq. Ft.
Expansion Joints	Lin. Ft.
Snap Caps	Lin. Ft.
Caulking	Tubes
Sealant Spray	Gal.
Sand	Cu. Yds.
Stone	Cu. Yds.
Other:	

VEHICLES & EQUIPMENT

CrewCat Mason Truck	Mason Dump Truck	Backho	Large Dump Truck	Light Duty Truck
Truck #	Truck #	#	Truck #	Truck #
Medium Dump Truck	Hydraulic Excavator	Towmster	Tag-A-Long Trailer	Utility Service Truck
Truck #	#	Truck #	#	Truck #

100

COMMENTS:

Health with Charlie Price

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC.

Signature:

EMPLOYEES RECORDED ABOVE

72

Approved By:

二

~~CEASER~~ Clever MAJ

Scutellaria L. 1753

SUPERVISOR

CONCRETE

DAILY GANG REPORT

Borough QUEENSDay MondayDate 08-19-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	7	3	<i>[Signature]</i>	
Thomas Kelly	Mason	6:00	16:30	7	3	<i>[Signature]</i>	
Paul Bovell	ACHR	6:00	16:30	7	2	<i>[Signature]</i>	
Roger Williams	ACHR	6:00	16:30	7	2	<i>[Signature]</i>	DOING FOR CHARLIE

ON STREET

CROSS STREET
<i>COLUMBUS AV & 110 & 109 ST.</i>

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep *→ 203 ←*

Sidewalk Pour

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete Cu. Yds.

Lumber Sq. Ft. Lin. Ft.

Steel Curb, Straight Sq. Ft.

Steel Curb, Bull Nose Pieces

Detectable Warning Sq. Ft.

Expansion Joints Lin. Ft.

Snap Caps Lin. Ft.

Caulking Cu. Yds. Tube

Sealant Spray Cu. Yds. Gal.

Sand Tons Cu. Yds.

Stone Cu. Yds.

Other: *GNADE - stone & formwork.* Cu. Yds.

VEHICLE & EQUIPMENT

Crew Cab Mason Truck Truck #: <i>112627</i>	Mason Dump Truck Truck #: <i>11260019</i>	Backhoe	Large Dump Truck Truck #: <i>1125989</i>	Light Duty Truck Truck #: <i>1125989</i>
Medium Dump Truck Truck #: <i>11260019</i>	Hydraulic Excavator Truck #: <i>1125989</i>	Towmaster Truck #: <i>1125989</i>	Tag-A-Long Trailer Truck #: <i>1125989</i>	Utility Service Truck Truck #: <i>1125989</i>
Other: <i>11260019</i>				

COMMENTS: *We went to location on Columbus Av & 110 and removed the forms & clean up. Also we form an island on 109 S. north. place stones. Clean up & secured the job site.*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

[Signature]

Supervisor

We took back to 2 Yards (the truck # 11260019)

**DOT/S MCITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Bronx

Day Monday

Date 8-19-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	?	3	Charles Restivo	
William Butler	ACHR						
Stan Kellie	ACHR						
Matthew Cuticella	ACHR	06:00	14:30	?		John	OUT

ON STREET

76 St

CROSS STREET

Columbus Ave

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	210	Sq. Ft.	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	4 mats 2'x5' Sq. Ft.
		Expansion Joints	30 Lin. Ft.

PREP & CAVE-IN

Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.

STEP STREETS

Landing	Sq. Ft.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	Other:	Maj on on job site
Step Replacement	Lin. Ft.		

VEHICLE & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:		Truck #:	#:	Truck #:
Other:				

COMMENTS:

Went to location on 76 St / Columbus Ave
Ready mix came with King's 7 yards sidewalk prep
210 sq-ft. Detectable working + mats 2'x5' Expansion joints
30 lin-ft. Clean up + set safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John Pavao

Title

Supervisor

**DOT/SIM CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Wednesday

Date 8/19/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	14:30	8		<i>J. Taranto</i>	
W. McQuade	Ctr.						→ out

ON STREET	CROSS STREET
(College Point Yard (Av)) Columbus Ave. & 76 St (Man)	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Pt.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLE & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

went to help other festivis crew with the pour
checked on crews at locations & returned to yard to do paper work

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader
[Signature]

Title

Approved By

Supervisor
[Signature]

NEW YORK WIDE CONCRETE
DAILY GANG REPORT

Borough QUEENS

Day TODAY

Date 08-20-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	6:00	16:30	8	3		
Thomas Kelly	Mason	6:00	16:30	7	3		
Paul Bovell	ACHR	6:00	16:30	8	2		
Roger Williams	ACHR	6:00	16:30	8	2	H. Williams	
<i>CHARGE</i>	<i>HR-</i>						
<i>MMT.</i>	<i>ACHR</i>						
<i>SAL.</i>	<i>MASON</i>						

ON STREET

COLUMBUS AVE X 110 & 109 ST.

CROSS STREET

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB	Ready Mix Concrete	9	Cu. Yds.
CROSS WALK → 70	Sq. Ft.	Lumber	Lin. Ft.
ISLANDS → 203	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	(8) - (2x5) Sq. Ft.
Curb Pour	Lin. Pt.	Expansion Joints	21 Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	1/8 Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>1122627</u>	Mason Dump Truck Truck #: #	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #: #	Hydraulic Excavator #	Towmaster Truck #:	Tag-A-Long Trailer #	Utility Service Truck Truck #:
Other: <u>Q219 D.</u>				

COMMENTS:

We went to the action on Columbus Ave. x 109. And paved a crosswalk with slabs. concrete. Also we pour an island on 109. with 4x8 concrete and we used about 900 yards of detectable walkways. NYC. dreams. clean up.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Title

Approved By

Title

Supervisor

And services to job site.

**DOT/NYC/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Tuesday

Date 8-20-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACMR						Out
Sean Kehoe	ACMR						
Matthew Cutietta	ACMR	06:00	16:30	8	2	Matthew Cutietta	

ON STREET

W 76 St
W 110 St

CROSS STREET

Columbus Ave
Columbus Ave

WORK PERFORMED

SIDEWALK & CURB
Sidewalk Prep Stripped & clean 210
Sidewalk Pour
Curb Prep
Curb Form
Curb Pour

MATERIALS USED

	Cu. Yds.
Ready Mix Concrete	
Sq. Ft. Lumber	Lin. Ft.
Sq. Ft. Steel Curb, Straight	Lin. Ft.
Lin. Ft. Steel Curb, Bull Nose	Pieces
Lin. Ft. Detectable Warning	Sq. Ft.
Lin. Ft. Expansion Joints	Lin. Ft.
	Snap Caps
Cu. Yds. Caulking	Tube
Cu. Yds. Sealant Spray	Gal.
Tons Sand	Cu. Yds.
Cu. Yds. Stone	Cu. Yds.

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

	Lin. Ft.	
Cu. Yds. Caulking	Tube	
Cu. Yds. Sealant Spray	Gal.	
Tons Sand	Cu. Yds.	
Cu. Yds. Stone	Cu. Yds.	
Sq. Ft. Other:	Arist Leo's gang	
Lin. Ft. in a concrete pour		
Lin. Ft. in w/110 St & Columbus Ave		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #: <u>0826</u>	Light Duty Truck Truck #:
Medium Dump Truck Truck #: <u>0825</u>	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Went to location on W 76 St / Columbus Ave
stripped and prep 210 sq ft.

Went to location on W 110 St / Columbus Ave

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John Sosa

Title

Supervisor

**DOT/SID /CITYWIDE CONCRETE
DA LY GANG REPORT**

Borough Queens

Day TUESDAY

Date 8-20-13

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Salvatore Russello	CM	6:00	16:30	7	3	Salvatore Russello	

ON STREET

ON STREET	CROSS STREET
115 ST A 2 FOR 21 TR # PLUMBING BY 116	41 ST

WORK PERFORMED

SIDEWALK & CURB	MATERIALS USED	
Sidewalk Prep	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	cu. Ft. Lumber	Lin. Ft.
Curb Prep	cu. Ft. Steel Curb, Straight	Lin. Pt.
Curb Form	1 cu. Ft. Steel Curb, Bull Nose	Pieces
Curb Pour	1 cu. Ft. Detectable Warning	Sq. Ft.
	1 cu. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN		
Debris Removal	Susp Caps	Lin. Ft.
Backfill	cu. Yds. Caulking	Tube
Asphalt Patch	cu. Yds. Sealant Spray	Gal.
STEP STREETS		
Landing	Tons Sand	Cu. Yds.
Pointing/Caulking/Patching	cu. Yds. Stone	Cu. Yds.
Step Replacement	cu. Yds. Other:	
	cu. Yds.	
	cu. Yds.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Bulkhoe	Large Dump Truck	Light Duty Truck
Truck #: 2859	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Teamster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

Help with pour man at end
and also help Alzate crews with
pour.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader
Salvatore Russello

Title

Approved By

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Thursday

Date 8/22/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	2:30	8	1		
Gadiel Salas	ACHR	5:00	2:30	8	1	A. Salas	

ON STREET

Columbus Ave and 76th - 110th St

CROSS STREET

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft.	Other: <u>Compost 12 Cu Yds</u>	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #: <u>0004</u>	Large Dump Truck Truck #: <u>737</u>	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #: <u>5009</u>	Utility Service Truck Truck #:

Other:

COMMENTS: Drop off two bull nose

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

HLS
Crew Leader

Title
Approved By

Supervisor

**DOT/SI CITYWIDE CONCRETE
DAILY GANG REPORT**

Queens
Borough ~~Borough~~

Day Thursday

Date 8-22-13

SIGN IN

ON STREET

CROSS STREET

~~WTS St~~

Columbus Ave

WORK PERFORMED

MATERIALS USED

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB			
Sidewalk Prep	Graded + Tamped 21C	Sq. Ft.	Ready Mix Concrete Free pit Cu. Yds
Sidewalk Pour		Lumber	10-(2"x6'), 3-(2"x8') Lin. Ft.
Curb Prep		Sq. Ft.	Steel Curb, Straight Lin. Ft.
Curb Form	70	Lin. Ft.	Steel Curb, Bull Nose Pieces
Curb Pour		Lin. Ft.	Detectable Warning Sq. Ft.
		Lin. Ft.	Expansion Joints Lin. Ft.
PREP & CAVE-IN			
Debris Removal		Cu. Yds.	Snap Caps Lin. Ft.
Backfill		Cu. Yds.	Caulking Tube
Asphalt Patch		Cu. Yds.	Sealant Spray Gel
STEP STREETS		Tons	Sand Cu. Yds.
Landing		Cu. Yds.	Stone Cu. Yds.
Pointing/Caulking/Patching		Sq. Ft.	Other: 1 short masonry
Step Replacement		Lin. Ft.	

VEHICLES & EQUIPMENT

VEHICLE		EQUIPMENT		
CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #: 0026	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 0005	F	Truck #:	#:	Truck #:

Other

Comments: Went to location on W 75 St | Columbus Ave
Sidewalk prep graded & tampered 2'0" sq ft.
Such term 70' linear. Lumber fir forms 10'-0" x 6'0"

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

POMERANTZ

Signallle

Title

Appro

DAILY GANG REPORT

Borough QUEENS Day TUESDAY. Date 08-22-13.

SIGN IN

Name	Title	In	Out	Reg Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	6:30	1	3		
Thomas Kelly	Mason	6:00	11:30	7	3	CKW	
Paul Bowell	ACHR	6:00	16:30	8	2	RB BULL	
Roger Williams	ACHR	6:00	16:30	8	2	KLH	

ON STREET

COLUMBUS AV X 107 ST.

CROSS STREET

WORK PERFORMED		MATERIALS USED	
<u>SIDEWALK & CURB</u>		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	→ 203 →	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour		Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep		Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form		Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour		Lin. Ft. Expansion Joints	Lin. Ft.
<u>PREP & CAVE-IN</u>		Snap Caps	Lin. Ft.
Debris Removal		Cu. Yds. Caulking	Tube
Backfill		Cu. Yds. Sealant Spray	Gal.
Asphalt Patch		Tons Sand	Cu. Yds.
<u>STEP STREETS</u>		Cu. Yds. Stone	Cu. Yds.
Landing		Sq. Ft. Other: Graded & prepared the steps	
Pointing/Caulking/Patching		Lin. Ft.	
Step Replacement		Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other: 0019.0				

COMMENTS:

We Went to location on Columbus Ave. & 109 st. south. And removed the forms & clean up. Also we formed 109 st. south. place drums. Clean up & secured the job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Lead
JAC

Title
Approved By
Title

**DOB / DMV/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Friday

Date 08-23-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	7	3		
Thomas Kelly	Mason	7:00	16:30	7	2		
Paul Bovell	ACHR	6:00	16:30	8	2		
Roger Williams	ACHR	6:00	16:30	8	2		

ON STREET

Columbus Ave. X 109 St. South

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED		QTY/PCS
Sidewalk Prep		Ready Mix Concrete		7 Cu. Yds.
Ishard Pour - 203		Sq. Ft. Lumber		Lin. Ft.
		Sq. Ft. Steel Curb, Straight		Lin. Ft.
Curb Prep		Lin. Ft. Steel Curb, Bull Nose		Pieces
Curb Form		Lin. Ft. Detectable Warning	(275)	4 Sq. Ft.
Curb Pour		Lin. Ft. Expansion Joints		Lin. Ft.
PREP & CAVE-IN		Snap Caps		Lin. Ft.
Debris Removal		Cu. Yds. Caulking		Tube
Backfill		Cu. Yds. Sealant Spray		Gal.
Asphalt Patch		Tons Sand		Cu. Yds.
STEP STREETS		Cu. Yds. Stone		Cu. Yds.
Landing		Sq. Ft. Other:		
Pointing/Caulking/Patching		Lin. Ft.		
Step Replacement		Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: 1122627	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other: 0019 D.				

COMMENTS:

We Went to location on Columbus Ave. X 109 St. south. And poured an island with wings concrete about 7 cu.yards. place down. Clean up. Seams. fix job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

37,076

Borough S.I.

Day F.R.

Date 8/23/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Douglas Olson	CM	6:00	16:30	7	3	<i>Sjt C</i>	

ON STREET	CROSS STREET	
<i>Columbus Av</i>	<i>w 75st</i>	<i>Charlie Sang</i>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>991-835</i>	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS: *POURED 7 YARDS OF CONCRETE WITH
CHARLIE SANG ON W 75ST. 5" SLUMP ON
CONCRETE MIX*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature *Sjt C*

Title

Crew Leader

Approved By

Title Supervisor

**DOT/S M/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Tuesday

Date 8/23/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	4:00	15:30	8	3	<i>Joe Taranto</i>	
W. McFadden	C.M.						→ OUT

ON STREET

College Point Yard (Q)
Columbus Ave & 75 St (Man.)

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Cu. Yds.
Landing	Sq. Ft.	Stone	
Pointing/Caulking/Patching	Lin. Ft.	Other:	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator Truck #:	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

Helped Charles C. with there pour, checked on
Crews & locations

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title Crew Leader

Approved By

Title Supervisor

**DOT'S M/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Friday Date 8-23-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	05:00	15:30	8	2	W Butler	
Matthew Curietta	ACHR	05:00	15:30	8	2	M Curietta	

ON STREET

W 75 St

CROSS STREET

Columbus Ave

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	King's 7	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber		Lin. Ft.
Curb Prep	Sq. Ft.	Steel Curb, Straight		Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose		Pieces
Curb Pour	Lin. Ft.	Detectable Warning	4 mats (2' x 5')	Sq. Ft.

PREP & CAVE-IN

Debris Removal	cu. Yds.	Snap Caps		Lin. Ft.
Backfill	cu. Yds.	Caulking		Tube
Asphalt Patch	cu. Yds.	Sealant Spray		Gal.
	Tons	Sand		Cu. Yds.

STEP STREETS

Step Replacement	Sq. Ft.	Stone		Cu. Yds.
Landing	Sq. Ft.	Other: Mason on job site		
Pointing/Caulking/Patching	Lin. Ft.			

Mason on job site

Douglas Olson

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #: 3005	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

Went to location on W 75 St Columbus Ave
Ready mix concrete with King's 7 yards sidewalk
pour 210 sq ft. Detectable warning installed 4 mats (2x5')
Clean up and set safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John Paul

Title

Supervisor

✓ mills

**DOT/SIM/CITYWIDE CONCRETE
COBBLESTONE PROGRAM - DAILY GANG REPORT**

Borough Queens 44-02

Day Friday

Date 8/23/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STONE	ATCH	6:00	4:30	8	2	JF	
Vicki							

From 44-02

ON STREET	CROSS STREET
MILL ST. HAMILTON AVE	MILL ST. HAMILTON AVE
73 ^E ST / 74 ^E COLUMBUS AVE	73 ^E ST. 74 ^E COLUMBUS AVE
107 ^E ST COLUMBUS AVE	107 ^E ST. COLUMBUS AVE

SOYSS

RETURN TO 44-02

WORK PERFORMED	MATERIALS USED		
Cobblestone/Pavers	Ready Mix Concrete		Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone		Sq. Ft.
Pavers	Sq. Ft. Pavers		Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks		Ea.
Steps & Walls	Lumber		Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking		Tube
Step Replacement	Lin. Ft. Cement		Bags
Wall Forming	Sq. Ft. Mortar Mix		Bags
Wall Installing	Sq. Ft. Sand		Cu. Yds.
Prep & Cave-In	Stone		Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints		Lin. Ft.
Backfill	Cu. Yds. Detectable Warning		Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
<u>Other: MINI BACK TRUCK #0367 - MILL ST</u>				

COMMENTS:

SET UP SAFETY FOR EXCAVATION ON MILL ST.
HAMILTON AVE, POST NO PARKING FOR DAY
73^E / 74^E - 107^E ST. NORTH & SOUTH —

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

Neil Brewster

DAILY GANG E. REPORT

Borough QueensDay SaturdayDate 8/24/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	6:00	14:30		8	<i>[Signature]</i>	

ON STREET	CROSS STREET
(College Point Yard (QNS))	
Columbus Ave & 107 St (Man)	
Columbus Ave & 74 St (Man)	

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED
		Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Casing Straight Lin. Ft.
Curb Prep	Lin. Ft.	Steel Casing Bull Nose Pieces
Curb Form	Lin. Ft.	Deflecto Board Warning Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joint Joints Lin. Ft.
PREP & CAVE-IN		Snap Caps Lin. Ft.
Debris Removal	Cu. Yds.	Caulking Tube
Backfill	Cu. Yds.	Sealant Spray Gai.
Asphalt Patch	Tons	Sand Cu. Yds.
STEP STREETS		Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft.	Other:
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

~~Chevelon Caves at location on Columbus Ave & 107 St & 74 St~~

I CERTIFY THAT THE TIME OF THE EMPLOYEE RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
COBBLESTONE PROGRAM - DAILY GANG REPORT**

Borough Queens

Day SAT

Date 8/24/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LAKY STORES JACK		6:00	2:30		8	ft	

From 44 to 02.

ON STREET	CROSS STREET
73 rd St. Columbus Ave	73 rd St. Columbus Ave
74 th St. Columbus Ave	74 th St. Columbus Ave
107 th St. Columbus Ave	107 th St. Columbus Ave

Return to 44th St.

WORK PERFORMED	MATERIALS USED
Cobblestone/Pavers	Ready Mix Concrete Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone Sq. Ft.
Pavers	Sq. Ft. Pavers Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks Ea.
Steps & Walls	Lumber Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking Tube
Step Replacement	Lin. Ft. Cement Bags
Wall Forming	Sq. Ft. Mortar Mix Bags
Wall Installing	Sq. Ft. Sand Cu. Yds.
Prep & Cave-In	Stone Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints Lin. Ft.
Backfill	Cu. Yds. Detectable Warning Sq. Ft.

VEHICLES & EQUIPMENT


CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other: MINI BACK TRUCK #0367				

COMMENTS:


Set of safety for saw cut, excavation on 73rd St.
74th St. Columbus Ave, 107th St. Columbus Ave, Minimize
safety on 110th St. / 109th St. Columbus Ave —

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC


Signature


Crew Leader

Title


Noel Brant

Approved By


Supervisor

Title

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough S.I. Brooklyn
SIGN IN IN MANHATTAN

Day Saturday

Date 8/24/13

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Buzzell	MGO	6-1	2:30	8	8	<i>[Signature]</i>	
Luis Soto	ACHR	6-1	2:30	8	8	<i>[Signature]</i>	
Roger Williams	ACME	6-0	2:30	8	8	<i>[Signature]</i>	

ON STREET	CROSS STREET
<u>108 & COLUMBUS (SOUTH)</u>	
<u>107 & COLUMBUS (N & S)</u>	

WORK PERFORMED	MATERIALS USED	
SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	50 Cu. Yds. Caulking	Tube
Backfill <i>RCA</i>	25 Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT				
CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #: 0003	Large Dump Truck Truck #: 738T	Light Duty Truck Truck #: 751T
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #: 4	Tag-A-Long Trailer #: 6001	Utility Service Truck Truck #:

Other:

COMMENTS:

*Excavate 107 N & S Columbus for 15 Islands
Load private container at 251T. Backfill
108 (South) 107 (N & S) with RCA
Grade to specs & make soft*

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

[Signature]

Title

Crew Leader

Approved By

[Signature]

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Saturday

Date 8/24/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	6:00	14:30	—	8		
Gadiel Salas	ACHR	6:00	14:30	—	8	H. Salas	
Eddie Hairston	ACHR	6:00	14:30	—	8		

ON STREET	CROSS STREET
<u>Columbus Ave</u>	<u>74-73</u>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#: <i>0004</i>	Truck #: <i>735</i> <i>737</i>	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#: <i>5009</i>	Truck #:
Other:				

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature _____

Title _____

Approved By _____

Title _____

Crew Leader _____

Supervisor _____

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough Brooklyn

Day Saturday

Date 8/24/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Rohan Wilkinson	ACHR	6:00	14:30		8	<u>Rohman</u>	
SEAN Thomas	ACHR	6:00	14:30		8		

ON STREET

Columbus Ave

CROSS STREET

W 74st and W 73st

WORK PERFORMED

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	
Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb. Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb. Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other: <u>Saw cut</u>	160 Lin Ft
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <u>0024</u>	Truck #: <u>0024</u>	#:	Truck #: <u>0024</u>	Truck #: <u>0024</u>
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <u>0014</u>	#:	Truck #: <u>0014</u>	#:	Truck #: <u>0014</u>

Other:

COMMENTS: <u>Saw cut Island on columbus Ave and w 74st and w 73st 160 Lin Ft also spread stone..</u>


**DOF: DM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens

Day Tuesday

Date 08-26-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	8	3		
Thomas Kelly	Mason	6:00	16:30	7	3		
Paul Bovell	ACHR	6:00	16:30	8	2		
Roger Williams	ACHR	6:00	16:30	8	2	180701	K. Miller

ON STREET

COLUMBUS AV. & 109 & 108. SOUTHERN ST.

CROSS STREET

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB

Sidewalk Prep	203.	Sq. Ft.	Lumber	(2x6)
Sidewalk Pour		Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep		Lin. Ft.	Steel Curb, Bull Nose	Lin. Ft.
Curb Form		Lin. Ft.	Detectable Warning	Pieces
Curb Pour		Lin. Ft.	Expansion Joints	Sq. Ft.

PREP & CAVE-IN

Debris Removal		Cu. Yds.	Snap Caps	Lin. Ft.
Backfill		Cu. Yds.	Caulking	Tube
Asphalt Patch		Cu. Yds.	Sealant Spray	Gal.
		Tons	Sand	Cu. Yds.

STEP STREETS

Landing		Cu. Yds.	Stone	Cu. Yds.
Pointing/Caulking/Patching		Sq. Ft.	Other: GRANDED & TAMPED (STONES)	
Step Replacement		Lin. Ft.		
		Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 112268	Truck #: #	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #	#	Truck #: #	#:	Truck #:
Other: 0019 D-				

COMMENTS:

We Went to Columbus Av. & 109 st. south and removed + he form. Also, I cleaned up. Also, we formed. Also, I cleaned on 108 st. and leveled the job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT

Signature

Title

Approved By

Title

Crew Leader

Supervisor

AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

**DOT/SI CITYWIDE CONCRETE
D. ILY GANG REPORT**

Borough Queens

Day Monday

Date 8-26-13

SIGN IN

Name	Title	In	Out	R.	Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30		11	3	Charles Restivo	
William Butler	ACHR	06:00	16:30		10	2	W Butler	
Matthew Cutietta	ACHR	06:00	15:30		9	2	M Cutietta	

ON STREET

W. 75 St
Cedar St Yard

CROSS STREET

Columbus Ave

WORK PERFORMED

SIDEWALK & CURB

Sidewalk Prep Graded + Tamped 210

Sidewalk Pour

Curb Prep

Curb Form

Curb Pour

PREP & CAVE-IN

Debris Removal

Backfill

Asphalt Patch

STEP STREETS

Landing

Pointing/Caulking/Patching

Step Replacement

MATERIALS USED

Ready Mix Concrete

Sq. Ft.

Cu. Yds.

Lumber 6(2"x6") 3(2x8")

Lin. Ft.

Steel Curb, Straight

Sq. Ft.

Lin. Ft.

Steel Curb, Bull Nose

Lin. Ft.

3 1/2' Radius (1) pieces

Detectable Warning

Sq. Ft.

Sq. Ft.

Expansion Joints

Lin. Ft.

Lin. Ft.

Snap Caps

Lin. Ft.

Lin. Ft.

Caulking

Cu. Yds.

Tube

Sealant Spray

Cu. Yds.

Gal.

Sand

Cu. Yds.

Cu. Yds.

Stone

Cu. Yds.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #: 0005	Hydraulic Excavator	Towmaster Truck #:	Tag-A-Long Trailer	Utility Service Truck Truck #:

Other:

COMMENTS:

Went to location on W 75 St / Columbus Ave
Sidewalk prep graded + Tamped 210 sq ft
Formed 30' x 7' sidewalk used lumber 6 - 2"x6" x 3-2"
Steel Curb Bull nose
3 1/2' Radius (1) piece
pick-up rings for gas line

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT

AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John G. S.

Title

Supervisor

DAILY GANG REPORT

Borough QUEENSDay WednesdayDate 8-28-2013

HAMMICK & MILL

COLUMBUS

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castronovo	CM	0600	1630	7	3	Mr. Castronovo	

ON STREET

HAMILTON AV
ADAM C. POWELL JR. BLVD
COLUMBUS AV

CROSS STREET

McLE ST
W 115 ST
W 107 - W 72 ST

33Y.SSS

33Y.SSS

 $33\% = 2.5 \text{ Reg Hours}$

A 1 Hour of O.T
for each project

WORK PERFORMED

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	in. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	in. Ft.	Detachable Warning	Sq. Ft.
Curb Pour	in. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVIN-IN		Snap Caps	Lin. Ft.
Debris Removal	C. Yds.	Caulking	Tube
Backfill	C. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		C. Yds.	Cu. Yds.
Landing	in. Ft.	Stone	
Pointing/Caulking/Patching	in. Ft.	Other:	
Step Replacement	in. Ft.		

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Excavator	Large Dump Truck	Light Duty Truck
Truck #: <u>7030</u>	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Driver	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	#:	#:	Truck #:

Other:

COMMENTS:

ON THE ABOVE LOCATION AT WORK 24 SCHEDULE
AND READY FOR POUR.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT, AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader Michele Castronovo

Supervisor

DOT/SIM/CITYWIDE CONCRETE
~~COBBLESTONE PROGRAM~~ - DAILY GANG REPORT

Borough Queens

Day Wednesday

Date 8/28/13

✓ Columbus

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STOLES	ACTV	6:00	2:30	8			

from 114+ DL

ON STREET	CROSS STREET
COLUMBUS AVE 106±	COLUMBUS 106±
LONGFOLLOW	LONGFOLLOW

50% SSS

RETURN TO 114+ DL

WORK PERFORMED	MATERIALS USED
Cobblestone/Pavers	Ready Mix Concrete Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone Sq. Ft.
Pavers	Sq. Ft. Pavers Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks Ea.
Steps & Walls	Lumber Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking Tube
Step Replacement	Lin. Ft. Cement Bags
Wall Forming	Sq. Ft. Mortar Mix Bags
Wall Installing	Sq. Ft. Sand Cu. Yds.
Prep & Cave-In	Stone Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints Lin. Ft.
Backfill	Cu. Yds. Detectable Warning Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other: MINI BACK TRUCK #P367 - SSP				

COMMENTS:

SET UP SAFETY ON LONGFOLLOW + BRUCKNER BLVD
LAYOUT ON 106± S1. COLUMBUS AVE TO 72±
ST

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Noel R. T.

Title

Crew Leader

Approved By

Noel R. T.

Title

Supervisor

Borough QueensDay WednesdayDate 9/4/13✓ Columbus
SOY

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	16:30	8	3		

ON STREET

CROSS STREET

College Point yard (av)
 Adam & Powell blvd at 115 St (men)
 Columbus Ave at 106 St - 73 St (men)

→ SOY, SSS

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Cui	Lin. Ft.
Curb Prep	Lin. Ft. Steel Cui	Pieces
Curb Form	Lin. Ft. Detecto	Sq. Ft.
Curb Pour	Lin. Ft. Expansive Joints	Lin. Ft.
PREP & CAVE-IN	Snap Cui	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other	
Pointing/Caulking/Patching	Lin. Pt.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

Comments: Checked on crews at locations, finished city time & paperwork, cleaned up office.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader



Approved By

Supervisor



DOT/SIM/CITYWIDE CONCRETE

[REDACTED] - DAILY GANG REPORT

Borough QUEENS 44-12Day ThursdayDate 9/5/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STORES	ACHER	6:00	2:30	8		JF	

from 44-12 M.

ON STREET	104 th St. Columbus Ave 70 th St. Columbus Ave 115 th St. 7 th Ave Lafayette & Prince St. PEN TO 44-12 M.	CROSS STREET	104 th St. Columbus Ave 70 th St. Columbus Ave 115 th St. 7 th Ave Lafayette & Prince St.
-----------	---	--------------	--

75% SSS
 " 6 Hours of
 Reg Time

WORK PERFORMED

MATERIALS USED

Cobblestone/Pavers	Ready Mix Concrete	Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone	Sq. Ft.
Pavers	Sq. Ft. Pavers	Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks	Ea.
Steps & Walls	Lumber	Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking	Tube
Step Replacement	Lin. Ft. Cement	Bags
Wall Forming	Sq. Ft. Mortar Mix	Bags
Wall Installing	Sq. Ft. Sand	Cu. Yds.
Prep & Cave-In	Stone	Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints	Lin. Ft.
Backfill	Cu. Yds. Detectable Warning	Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other: MINI RACK TRUCK #0367 - SSS

COMMENTS:

SET UP SAFETY ON COLUMBUS AVE 104TH NORTH & SOUTH, 70TH ST., REMOVES Jersey barriers from 115TH 7TH AVE, PLACED 10 Jersey barriers on LAFAYETTE PRINCE ST.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

JF

Title

Crew Leader

Approved By

Ned ZK

Title

Supervisor

V

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Friday

Date 9/6/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Alex Shimanovsky	TO	5:00	16:30	8	3		
Gadiel Salas	ACHR	5:00	16:30	8	3	<u>G. Salas</u>	

ON STREET	CROSS STREET
<u>Lafayette</u>	<u>Prince St</u>
<u>Columbus St</u>	<u>105 St</u>

- \$501.98

WORK PERFORMED		MATERIALS USED		
SIDEWALK & CURB		Ready Mix Concrete Cu. Yds.		
Sidewalk Prep	Sq. Ft.	Lumber		Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	23	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	4	Pieces
Curb Form	Lin. Ft.	Detectable Warning		Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints		Lin. Ft.
PREP & CAVE-IN		SSS	Snap Caps	Lin. Ft.
Debris Removal	20 = 10 + 10	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray		Gal.
Asphalt Patch	Tons	Sand		Cu. Yds.
STEP STREETS		Cu. Yds.	20 = 10 + 10	SSS Cu. Yds.
Landing	Sq. Ft.	Stone		Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.			
Step Replacement	Lin. Ft.			

VEHICLES & EQUIPMENT

SSS - columbus

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader



Supervisor

Columbus

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Staten Island

Day Friday

Date 9/6/2013

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR						Frn is out
Jason James	HR	6:00	16:30	8	2		
Alvaro Arias	HR	6:00	16:30	8	2		

ON STREET

109th St
Columbus Ave

CROSS STREET

Columbus Ave
St. Paul's Ave

SOY, SSS

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		Ready Mix Concrete		Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber		Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight		Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose		Pieces
Curb Form	Lin. Ft.	Detectable Warning		Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints		Lin. Ft.
PREP & CAVE-IN		Snap Caps		Lin. Ft.
Debris Removal	Cu. Yds.	Caulking		Tube
Backfill	Cu. Yds.	Sealant Spray		Gal.
Asphalt Patch	Tons	Sand		Cu. Yds.
STEP STREETS		Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:		
Pointing/Caulking/Patching	Lin. Ft.			
Step Replacement	Lin. Ft.			

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: <u>754 T</u> <u>752 T</u>	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

Poured & debris from three locations and dumped.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Leader

Approved By

Title

Supervisor



DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough Queens

Day Tuesday

Date 9-10-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HHR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR	06:20	16:30	8	2	W Butler	
Matthew Cutieta	ACHR	06:20	16:30	8	2	M. Cutieta	

ON STREET

CROSS STREET

W 71 St

Columbus Ave

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep graded & tamped 210 Sq. Ft.	Lumber	Free Pit 3-(2"x8') Island 8-(2"x6') Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb Straight Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb Bull Nose 3½' Radii (1) Pieces
Curb Form	74 Lin. Ft.	Detectable Varnish Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking Tube
Backfill	Cu. Yds.	Sealant Sealant Gal.
Asphalt Patch	Tons	Sand Cu. Yds.
STEP STREETS	Cu. Yds.	Stone Cu. Yds.
Landing	Sq. Ft.	Other:
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 2005	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

Went to location on W 71 St / Columbus Ave
 Sidewalk prep graded & tamped 210 sq ft. Curb form 74 lin ft.
 Lumber Free pit 3-(2"x8') Island 8-(2"x6') Steel curb bull nose
 3½ Radii (1) piece Clean up & 5 ft safety

I CERTIFY THAT THE TIME OF THE EMPLOYEE'S RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John [Signature]

Title

Supervisor

✓ Columbus

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough S I

Day Tuesday

Date 9/10/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR	500	1630	8	3	<i>F. Cammalleri</i>	
Jason James	HR	600	1630	8	2		Worked with JOE
Alvaro Arias	HR	600	1630	8	2	<i>A. Arias</i>	Worked with Alex
							SSS

ON STREET	JASON ST. MARK / E. PARKWAY (BK)	CROSS STREET	ALVERO 102nd ST / COLUMBUS AV (M)	SSS

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
PREP & CAVE-IN		Expansion Joints	Lin. Ft.
Debris Removal	Cu. Yds.	Snap Caps	Lin. Ft.
Backfill	Cu. Yds.	Caulking	Tube
Asphalt Patch	Tons	Sealant Spray	Gal.
STEP STREETS		Sand	Cu. Yds.
Landing	Sq. Ft.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	Other:	
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: 754 T 752 T	Light Duty Truck Truck #: 6836
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

Went to drop off paper work and pick up supply checked on location all safe.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

F. Cammalleri

Title _____

Approved By

Supervisor

Title _____

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough SF

Day Wed.

Date 9/11/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR	500	1630	8	3	F. Cammalleri	
Jason James	HR	600	1630	8	2	J. James	
Alvaro Arias	HR	600	1530	8	7	A. Arias	Worked with Chen Worked with Chau

ON STREET <u>CeBRA Ave / St. Paul (SF)</u>	CROSS STREET <u>71st / Columbus Ave</u>	ALVERNO <u>(M)</u>

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: <u>7527</u>	Light Duty Truck Truck #: <u>6836</u>
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

Went to CeBRA helped with safety doing
work. Went to drop off paper work checked
out location on Guyon and mill all

LEFT SAFE.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader
F. Cammalleri
Supervisor

**DO/T/SW/CITY WIDE C. INCORP.
DAILY GANG REPORT**

Borough QUEENS

Day THURSDAY

Date 9-12-2013

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Michele Castrovovo	CM	6-20	16-20	7	3	R. Cato	

ON STREET	CROSS STREET
QUEENS BLVD	46 ST
COLUMBUS AV	W 1 ST

NON SSS
SSS

WORK PERFORMED	MATERIAL USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, SIGHT Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, BULL NOSE Pieces
Curb Form	Lin. Ft. Detectable V' ning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 7038	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:		Truck #:		Truck #:

Other:

COMMENTS:

ON QUEENS BLVD LOCATION INSTALLED
8 CROSSWALK TITLE P FOR PARIS HUNTER CREW.
ALSO WANT TO COLUMBUS AV 101 ST FORMING COKE
COLD LOCATION & READY FOR POUR.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader Michele Cato

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough BK

Day Thursday

Date 9-12-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	O/Hrs.	Signature	Supervisor's Remarks
Milagros Lopez	ACHR	0300	1430	8	1	Milagros Lopez	
Sean Thomas	ACHR	OFF	OFF	—	—	Sean Thomas	
Rohan Wilkinson	ACHR	0600	1430	8	0	Rohan Wilkinson	
Nicholas Depaola	ACHR	WALKED WITH GUY	OUT	—	—		

ON STREET	CROSS STREET
115 104, 105 106	ADAM CLAYTON POWELL COLUMBUS AVE

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other: Compost	10 yards
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: Pickup 7087	Light Duty Truck Truck #: 0014
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

M Lopez, Rohan W, and Rohan R met up at location. We cleaned area, then we raked out compost with the help of Joe Barzel. We made sure all locations was clean and safe, loaded mulch on truck. Some of the safety onto truck.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Milagros Lopez

Crew Leader

Supervisor

Some of the safety onto truck.

SSS

Non SSS

DAILY GANG REPORT

Borough Brooklyn

Day Thursday

Date 9/12/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
A. McGinn	CM	6:30	16:30	7	2 1/2	<i>McGinn</i>	
V. Benson	ACHR	6:00	16:30	8	2	<i>Benson</i>	
A. Landell	ACHR	6:00	16:30	8	2	<i>Landell</i>	
J. Tucker	ACHR	6:00	16:30	8	2	<i>Tucker</i>	

ON STREET

100 ft S of Columbus Ave NY

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	187 Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Lumber	100 Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Form	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Pour	Lin. Ft.	Detectable Warning	Sq. Ft.
PREP & CAYE-IN		Expansion Joints	30 Lin. Ft.
Debris Removal	Cu. Yds.	Snap Caps	Lin. Ft.
Backfill	Cu. Yds.	Caulking	Tube
Asphalt Patch	Tons	Sealant Spray	Gal.
STEP STREETS	Cu. Yds.	Sand	Cu. Yds.
Landing	Sq. Ft.	Stone	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	Other:	1 sheet mesonite
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <u>2587</u>	Mason Dump Truck Truck #: <u>0002</u>	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #: <u>5136</u>
Medium Dump Truck Truck #:	Hydraulic Excavator	Towmaster Truck #:	Tag-A-Long Trailer	Utility Service Truck Truck #:
Other:				

COMMENTS:

cleared up & made entire work area SAFE.

cc: rody
cc: rody

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Queens Day Thursday Date 9-12-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:30	16:30	8	3	Charles Restivo	
William Butler	ACHR	06:00	16:30	8	2	W Butler	
Matthew Cutierto	ACHR	06:00	16:30	8	2	M Cutierto	

ON STREET

CROSS STREET

W 71 St

Columbus Ave

WORK PERFORMED

MATERIALS USED

SIDEWALK & CURB		Ready Mix	Concrete	Cy. Yds.
Sidewalk Prep	graded & compacted 210 Sq. Ft.	Lumber	slab 8-(2'x6')	1pc ft 4'-6" x 8' in. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb	straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb	full Nose	3 1/2 Radii (1) Pieces
Curb Form	Lin. Ft.	Detachable	Forming	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion	Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps		Lin. Ft.
Debris Removal	Cu. Yds.	Caulking		Tube
Backfill	Cu. Yds.	Sealant Sp.		Gal
Asphalt Patch	Tons	Sand		Cu. Yds.
STEP STREETS		Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:		
Pointing/Caulking/Patching	Lin. Ft.			
Step Replacement	Lin. Ft.			

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 0026	Truck #: 0026	#:	Truck #: 0026	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: 0005	#:	Truck #:	#:	Truck #:

Other:

COMMENTS:

Went to location on W 71 St / Columbus Ave
Sidewalk prep graded & tamp
8-(2'x6') and Tree pit 4-
(1) piece clean up & set
safety

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

John Clark

Title

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Thursday

Date 9.12.13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Greg Duran	MGO					Out	
Eddie Hairston	Actor	5:10	16:30	8	3	Eddie Hairston	

ON STREET	CROSS STREET
29th St Yd	
Columbus Ave and 69th - 102nd St Queens Blvd & 46th St	

WORK PERFORMED	MATERIALS USED	
SIDEWALK & CURB	Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	22 Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

Drop off steel at two(2) location and got load with debris from Columbus Ave and 69th St.

DAILY GANG REPORT

Borough SI

Day Thur.

Date 9/12/13

SIGN IN

Now
~~SSS~~
~~Not~~
~~SSS~~

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR	500	1630	8	3	F. Cammalleri	
Jason James	HR	600	1630	8	2		Worked with Alex
Alvaro Arias	HR	600	1530	5	1	A. Arias	Worked with Chris

ON STREET	CROSS STREET
JASON 70th / Columbus (M)	ALVARO CeBRA Ave / ST.paul (S)

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #: 752T	Truck #: 6836
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:

Other:

Comments: Went to look at new location of mill and guyan marked out - Went to Cebra to help with safety. All left safe

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Cammalleri

Supervisor

DOT/SIM/CITYWIDE CONCRETE

~~CORPORATION PROJECT~~ - DAILY GANG REPORTBorough QUEENS 44± DRDay THURSDAYDate 9/12/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STORES ACME		3:00PM	3:00AM	8	4	AJ	
TELECOM HOME IMP		3:00PM	3:00AM	8	4	D. Thomas	

ON STREET 115± ST 7± Ave
106±/105± ST COLUMBUS
104± ST COLUMBUS AVE
LONGFOLLOW & BRICKNER BLVD

CROSS STREET 115± ST. 7± Ave
106±/105± ST. COLUMBUS
104± ST. COLUMBUS AVE
LongFollow & Brickner Blvd

WORK PERFORMED		MATERIALS USED	
Cobblestone/Pavers		Ready Mix Concrete	Cu. Yds.
Cobblestone	Sq. Ft.	Cobblestone	Sq. Ft.
Pavers	Sq. Ft.	Pavers	Sq. Ft.
Concrete Roadbase	Sq. Ft.	Cinder Blocks/Bricks	Ea.
Steps & Walls		Lumber	Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft.	Caulking	Tube
Step Replacement	Lin. Ft.	Cement	Bags
Wall Forming	Sq. Ft.	Mortar Mix	Bags
Wall Installing	Sq. Ft.	Sand	Cu. Yds.
Prep & Cave-In		Stone	Cu. Yds.
Debris Removal	Cu. Yds.	Expansion Joints	Lin. Ft.
Backfill	Cu. Yds.	Detectable Warning	Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other: MINI RACK TRUCK #0367				

COMMENTS:

SET UP SAFETY ON LONGFOLLOW & BRICKNER BLVD, REMOVE
Safety on 115± 7±, 106, 105, 104± st. COLUMBUS AVE
RETURN TO 44± DR

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Leader

Approved By


Supervisor

Title

DAILY GANG REPORT

Borough QueensDay ThursdayDate 9/12/13

SIGN IN

Name	Title	In	Out	Reg. Hrs	OT Hrs	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	16:30	8	3		

ON STREET

CROSS STREET

<u>College Point Yard (av)</u>	<u>Columbus Blvd (102 St - 72 St) (N)</u>

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED
SIDEWALK & CURB		Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel C. b, Straight Lin. Ft.
Curb Prep	Lin. Ft.	Steel C. b, Bull Nose Pieces
Curb Form	Lin. Ft.	Detector e Warning Sq. Ft.
Curb Pour	Lin. Ft.	Expans. Joints Lin. Ft.
PREP & CAVE-IN		Snap C. Lin. Ft.
Debris Removal	Cu. Yds.	Caulk Lin. Ft.
Backfill	Cu. Yds.	Sealant Spray Gal.
Asphalt Patch	Tons	Sand Cu. Yds.
STEP STREETS		Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft.	Other:
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

Crew Cab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #: <u>1190871</u>
Medium Dump Truck Truck #:	Hydraulic Excavator #	Towmaster Truck #:	Tag-A-Long Trailer #	Utility Service Truck Truck #:
Other:				


COMMENTS:

Meet with A. Piriano to
of Manhattan locations, 58th St. Yard, Staten Island

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader



Approved By

Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Staten Island

Day Fri.

Date 9/13/2013

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Frances Cammalleri	HR	500	1630	8	3	Frances Cammalleri	
Jason James	HR	600	1630	8	2	Jason James	CFOB J-Buzzell WORKED WITH LEO
Alvaro Arias	HR	600	1630	8	2		

ON STREET	JASON	CROSS STREET	ALVERA
GUYON	MILL	101 100	and COLUMBUS and COLUMBUS

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	
Sidewalk Prep	Sq. Ft.	Lumber	Cu. Yds.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: 754T 750T	Light Duty Truck Truck #: 6836
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS:

Went to drop off paper work
Checked on new location and all
Other location ALL SAFE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Frances Cammalleri

Supervisor

DAILY GANG REPORT

Borough QueensDay FridayDate 9/13/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	16:30	8	3	<i>Joseph Taranto</i>	

ON STREET College Point Yard (Q)
Columbus Ave & 102-121st (Pan)
Queens plant (IV)

CROSS STREET Raw (College point) (Q)

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detachable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Cuts	Lin. Ft.
Debris Removal	Cu. Yds.	Caulk	Tube
Backfill	Cu. Yds.	Sealant	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft.	Other	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

COMMENTS:

checked on crews at Queens plant & College point locations went for fuel & up tools from Raw M

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader
Joseph Taranto
Supervisor

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day MONDAY

Date 9/16/13

SIGN IN

Name	Title	In	Out	Reg. Hrs	OT Hrs	Signature	Supervisor's Remarks
Gregory Duran	IMGO	0500	16:30	8	3	F. Duran	
Edward Hairston	ACHR	0500	16:30	8	3	E. Hairston	{ 50%
Julio Salazar	ACHR	0500	16:30	8	3	J. Salazar	{ 50%

SSS
WwN

ON STREET

CROSS STREET

BROADWAY AND 31ST
COLUMBUS AND 104, 103, 100, 76, 75, 74, 73, 72 ST

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURE		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Shab Caps	Lin. Ft.
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill <u>COMPOST 20</u>	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS	Cu. Yds.	Stone	Cu. Yds.
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #:	#:	Truck #:	Truck #:
		20001	735T / 736T	
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	Truck #:	Truck #:	Truck #:	Truck #:
			5008	

| Other:

COMMENTS:

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader:

Supervisor

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORTBorough QueensDay MondayDate 9-16-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Charles Restivo	HR	05:00	16:30	8	3	Charles Restivo	
William Butler	ACHR					William Butler	O/H
Matthew Cuhetta	ACHR	06:00	16:30	8	2	M. Cuhetta	

ON STREET	CROSS STREET
<u>W. 70th ST</u>	<u>Columbus Ave</u>

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep <u>graded + tampered 210 Sq. Ft.</u>	Lumber Tie Pt 4-(2x8') Island 8-(2x6') Lin. Ft.
Sidewalk Pour	Steel Curb straight Lin. Ft.
Curb Prep <u>Framed 74 Lin. Ft.</u>	Steel Curb Bull Nose 3½ Radii (1) Pieces
Curb Form	Detectable warning Sq. Ft.
Curb Pour	Expansion joints Lin. Ft.
PIPE & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Sealant Spray Gal.
Asphalt Patch	Sand Tons Cu. Yds.
STEP STREETS	Stone Cu. Yds.
Landing	Other: <u>l.ason at job site</u> Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	William McQuade Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #: <u>0026</u>	Light Duty Truck Truck #:
Medium Dump Truck Truck #: <u>0005</u>	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer	Utility Service Truck Truck #:
Other:				

COMMENTS:

Went to location on W 70th St / Columbus Ave
 Sidewalk prep graded + tamper + 310 sq ft Curb formed 74 lin ft
 Lumber for Tree pit usol + -(2" x 8") + Island 8 - (2" x 6")
 Steel curb Bull Nose 3½ Radii (1) piece Clean up + Set sidewalk.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Charles Restivo

Title

Crew Leader

Approved By

Supervisor

DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough Brooklyn

Day Monday

Date 9/16/15

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
A. McLain	CM	6:00	16:30	7	3		
V. Benson	ACHR				OT	<i>Benson</i>	
A. Landell	ACHR	6:00	16:30	8	2	<i>Landell</i>	
J. Tucker	ACHR	6:00	16:30	8	2	<i>Tucker</i>	

ON STREET

W 97th St & Columbus Ave N

CROSS STREET

WORK PERFORMED

SIDEWALK & CURB		MATERIALS USED	
Sidewalk Prep	196 Sq. Ft.	Ready Mix Concrete	Cu. Yds.
Sidewalk Pour		Lumber	90 Lin. Ft.
Curb Prep		Steel Curb, Straight	Lin. Ft.
Curb Form		Steel Curb, Bull Nose	1 Pieces
Curb Pour		Detectable Warning	Sq. Ft.
		Expansion Joints	30 Lin. Ft.

PREP IN AVENUE

PREP IN AVENUE		MATERIALS USED	
Debris Removal		Caulking	Tube
Backfill		Sealant Spray	Gal.
Asphalt Patch		Sand	Cu. Yds.
STEP STREETS		Cu. Yds.	Cu. Yds.
Landing		Stone	
Pointing/Caulking/Patching		Other:	
Step Replacement			

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck # <u>2597</u>	Truck # <u>2002</u>	#	Truck #	Truck # <u>1301</u>
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #	#	Truck #	#	Truck #

Others

COMMENTS:	<u>Cleared up & made entire work area SAFE</u>
	<i>C.M.</i>
	<i>[Signature]</i>

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Brooklyn

Day Monday

Date 5/16/15

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
A. McGinn	CM	6:00	16:30	7	3	<i>Greig</i>	
V. Benson	ACHR				OT	<i>Benson</i>	
A. Landell	ACHR	6:00	16:30	8	2	<i>Landell</i>	
J. Tucker	ACHR	6:00	16:30	8	2	<i>Tucker</i>	

ON STREET	CROSS STREET
W 97 TH ST & Columbus Av N.Y.	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep 196 Sq. Ft.	Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose / Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Cu. Yds. Caulking Tube
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other:
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 2597	Truck #: 2002	#:	Truck #:	Truck #: 1301
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:	#:	Truck #:	#:	Truck #: #:
Other:				

COMMENTS:

Cleared up & made entire work area SAFE

RGM/J.C.M.

WD

DOT SIM/CITYWIDE CONCRETE
DAILY GANG REPORT

Borough QUEENS Day Monday Date 09.16.13

Sep 17 2013 06:27am P012/017

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	3	3		
Paul Bovell	ACHR	6:00	16:30	8	2		
Roger Williams	ACHR	6:00	16:30	8	2		
Thomas Kelly	CM	6:00	16:30	7	3		

ON STREET	CROSS ST	EEET
Colombus Ave	Ave X 102 st	102 st.
Colombus Ave	Ave X 103 st	103 st.

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep → 203 → Sq. Ft. Lumber Lin. Ft.	→ 120 → Lin. Ft.
REMOVED FORMS → 120 → Lin. Ft. Steel Curb straight Lin. Ft.	→ 1 → 1 → 1 → Lin. Ft.
FORMED ISLANDS → 120 → Lin. Ft. Steel Curbull Nose Detectable framing Sq. Ft.	(3 1/2 12.)
Curb Pour Lin. Ft. Expansion ints Lin. Ft.	
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal Cu. Yds. Caulking Tube	
Backfill Cu. Yds. Sealant Spray Gal.	
Asphalt Patch Tons Sand Cu. Yds.	
STEP STREETS Cu. Yds. Stone Cu. Yds.	
Landing Sq. Ft. Other: 6' 2' AVE & FAMPONIC (stone)	
Pointing/Caulking/Patching Lin. Ft.	
Step Replacement Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: 1122627	Truck #:	#:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: #:	Truck #:	Truck #:	Truck #:	Truck #:

Other: 0049-D-

COMMENTS: We went to location on Columbus Ave X w 103 st.
And REMOVED THE FORMS X C
FORM AND ISLAND ON Columbus Ave X w 102 st.
PLACE DRAWS CLEAN UP X SEWER & THE JOB SITE.

I CERTIFY THAT THE TIME OF THE EMPLOYEE'S RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

Supervisor

DAILY GANG REPORT

Borough

Queens

Day

TUESDAY

Date

09-17-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	5:00	16:30	7	3	<i>[Signature]</i>	
Thomas Kelly	Mason	6:00	16:30	10	3	<i>[Signature]</i>	
Paul Bovell	ACHR	6:00	16:30	8	2	<i>[Signature]</i>	
Roger Williams	ACHR	6:00	16:30	8	2	<i>[Signature]</i>	

ON STREET

CROSS

STREET

COLUMBUS AVE X

102 ST.

WORK PERFORMED

	MATERIALS USED	KINGS
SIDEWALK & CURB	Ready Mix Concrete	6 Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber	Lin. Ft.
<i>Islands - paved - 203</i>	Sq. Ft. Steel Cuts	Lin. Ft.
Curb Prep	Lin. Ft. Steel Cuts	Pieces
Curb Form	Lin. Ft. Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft. Expansive Nails	Lin. Ft.
PREP & CAVE-IN	Snap Caps	Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Spray	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	Cu. Yds.
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>122627</i>	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck Truck #:
Other: <i>0019-D</i>		Truck #:		

COMMENTS:

We went to work in Columbus Ave x w 102 st and joined an Island. We used Kings concrete about 3 cu yards x (275) - 4 units of detectable warning place. Drivs. & Curb up & screen. He job site

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title Crew Leader

Approved By

Title Supervisor

DOT/SIM/CITYWIDE CONCRETE

[REDACTED] - DAILY GANG REPORT

Borough Queens 44+00Day TUESDAYDate 9/17/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STORES A/C HR		3:00pm	3:30am	8	4	[Signature]	50% now
							50%
							SSS

from 44+00

ON STREET	CROSS STREET
COLUMBUS AVE SAFETY CHECK	COLUMBUS AVE SAFETY CHECK
LONGFOLLOW & BRICKNER BLVD	LONGFOLLOW & BRICKNER BLVD

RETURN TO 44+00

WORK PERFORMED	MATERIALS USED
Cobblestone/Pavers	Ready Mix Concrete Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone Sq. Ft.
Pavers	Sq. Ft. Pavers Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks Ea.
Steps & Walls	Lumber Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking Tube
Step Replacement	Lin. Ft. Cement Bags
Wall Forming	Sq. Ft. Mortar Mix Bags
Wall Installing	Sq. Ft. Sand Cu. Yds.
Prep & Cave-In	Stone Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints Lin. Ft.
Backfill	Cu. Yds. Detectable Warning Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
<u>Other: MINI BACK TRUCK #0367</u>				

COMMENTS:

SET UP SAFETY ON LONGFOLLOW & BRICKNER BLVD, REMOVED
Safety from COLUMBUS AVE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Noel Brandy

Title

Crew Leader

Approved By

Noel Brandy

Title

Supervisor

**DOT SIDEWALK INSPECTION MANAGEMENT
CITYWIDE CONCRETE PROGRAM - DAILY GANG REPORT**

Borough: BRONXDate: Thursday 19-2013**SIGN IN**

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
F. Johnson	CM	6:46	15:30	7	4	J. Johnson	7 50% SSS
							50% PON
Total Hrs.							

Location	From	To
Columbus Avenue & 67 St		
168 St + Clay Avenue		

STEP STREETS	PREP & CAVE-IN		
Coping	Lin. Ft.	Fill	Cu. Yd.
Sidewalk	Sq. Ft.	Debris	Cu. Yd.
Walls	Cu. Ft.	Opening	Sq. Yd.
Pointing & Patching	Lin. Ft.		
MATERIAL USED	CURB WORK		
Ready Mix	2 + 6.00 = ? Cu. Yd.	Sidewalk Prep	Sq. Ft.
Hand Mix	Cu. Yd.	Sidewalk Pour	Sq. Ft.
Cement	Bags	Curb Prep	Lin. Ft.
Sand/Stone	Cu. Yd.	Curb Pour	Lin. Ft.
Lumber	Lin. Ft.	Paving Block	Unit
Expansion Joint	Unit	Forming	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe Truck #:	Large Dump Truck Truck #:	Light Duty Truck Truck #: 1074632 ✓
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Townmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

Comments: Pour and finish ready mix concrete at 68 street and Columbus Avenue ~~in Manhattan~~. Then 168 Street and Clay Avenue Bronx. F. Johnson

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF THE CITY OF NEW YORK

Signature

Title

Approved By

Title

Citywide Concrete Program

**DOT/SIM/CITYWIDE CONCRETE
DAILY GANG REPORT**

Borough Staten Island

Day Tuesday

Date 9 /17/2013

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Franca Cammalleri	HR	600	1630	8	3	Franca Cammalleri	
Jason James	HR	600	1630	8	2	Jason James	Worked with Alex
Alvaro Arias	HR	600	1421	8		Alvaro Arias	Worked with Chas

ON STREET	<u>Alvoco</u>	CROSS STREET	<u>Season</u>
70th stand columbus Ave		34th	11

WORK PERFORMED		MATERIALS USED	
SIDEWALK & CURB		Ready Mix Concrete	Cu. Yds.
Sidewalk Prep	Sq. Ft.	Lumber	
Sidewalk Pour	Sq. Ft.	Steel Curb, Straight	Lin. Ft.
Curb Prep	Lin. Ft.	Steel Curb, Bull Nose	Pieces
Curb Form	Lin. Ft.	Detectable Warning	Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints	Lin. Ft.
PREP & CAVE-IN		Snap Caps	
Debris Removal	Cu. Yds.	Caulking	Tube
Backfill	Cu. Yds.	Sealant Spray	Gal.
Asphalt Patch	Tons	Sand	Cu. Yds.
STEP STREETS		Stone	
Landing	Sq. Ft.	Other:	
Pointing/Caulking/Patching	Lin. Ft.		
Step Replacement	Lin. Ft.		

ESS

VEHICLES & EQUIPMENT

CrewCab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #:	Truck #: <u>0001</u>	#:	Truck #: <u>754T</u>	Truck #: <u>6836</u>
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #:	#:	Truck #:	#:	Truck #:
Other:				

COMMENTS:

Went to Coley pt picked up pickup truck.
Went to 44 Drive picked up supply
Went to Drop off paper work at 58th st
Went to check on location all safe.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Crew Leader

Franca Cammalleri

Title

Supervisor

Borough

Oceans.

Daw

Wagner Day

20

09-18-13

SIGN IN

ON STREET

*Pteropus ac-
cidentalis*, Ag.
[Watson, 3].

CROS

STREETS

~~STREET~~
~~102 st~~
~~97 st~~

110

WORK PERFORMANCE

DESCRIPTION		MATERIALS USED		
SIDEWALK & CURB		Ready Mix Concrete		Cu. Yds.
Islands. → 203 →	Sq. Ft.	Lumber	→ 130 →	Lin. Ft.
Sidewalk Pour	Sq. Ft.	Steel C., Straight		Lin. Ft.
Reinforced, Forest. → 120 →	Lin. Ft.	Steel C. Bull Nose	→ \$ →	Pieces
Formed, Island → 130 →	Lin. Ft.	Detectors Warning		Sq. Ft.
Curb Pour	Lin. Ft.	Expansion Joints		Lin. Ft.
PREP & CAVE-IN		Snap C.		Lin. Ft.
Debris Removal	Cu. Yds.	Caulking		Tube
Backfill	Cu. Yds.	Sealant		Gal.
Asphalt Patch	Tons	Sand		Cu. Yds.
STEP STREETS		Cu. Yds. Stone		Cu. Yds.
Lending	Sq. Ft. Other:	PAVED & TAMPED (Step)		
Pointing/Caulking/Patching	Lin. Ft.			
Step Replacement	Lin. Ft.			

VEHICLES & EQUIPMENT

EXCAVATORS & EQUIPMENT		
CrewCab' Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:
Other: 0019-A		

Large Dump Truck Truck #:	Light Duty Truck Truck #:
Tag-A-Long Trailer #:	Utility Service Truck Truck #:

COMMENTS:

We went to Frost's

Columbus Ave. & W 102 St. and
Also we form an ISLAND
PLACE DRUMS. Clean up.

I CERTIFY THAT THE TIME OF THE EMPLOYEE IS ACCURATE.

Signature

Title

Approved By:

Title

Crew Leader

ABOVE IS CORRECT

DOT/SIM/CITYWIDE CONCRETE

[REDACTED] - DAILY GANG REPORT

Borough Queens 44th flr.Day WednesdayDate 9/18/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STORES ACHIEVEMENT		3:10PM	11:30AM	8		[Signature]	

from 44th flr.

ON STREET	CROSS STREET
COLUMBUS AVE SAFETY Removal LONGFOLLOW & BRUCKNER BLVD	COLUMBUS SAFETY Removal LONGFOLLOW & BRUCKNER BLVD

RETURN TO 44th flr.

WORK PERFORMED	MATERIALS USED
Cobblestone/Pavers	Ready Mix Concrete Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone Sq. Ft.
Pavers	Sq. Ft. Pavers Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks Ea.
Steps & Walls	Lumber Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking Tube
Step Replacement	Lin. Ft. Cement Bags
Wall Forming	Sq. Ft. Mortar Mix Bags
Wall Installing	Sq. Ft. Sand Cu. Yds.
Prep & Cave-In	Stone Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints Lin. Ft.
Backfill	Cu. Yds. Detectable Warning Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other: MINI BACK TRUCK #0367

COMMENTS:

SET UP SAFETY ON LONGFOLLOW & BRUCKNER BLVD, REMOVED
SAFETY ON COLUMBUS AVE

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Leader

Approved By

Title

Supervisor

DOT/SIM/CITYWIDE | ONCRETE
DAILY GANG REPORT

Borough

Queens

Day

Hudson

Date

09-19-13

SIGN IN

Name	Title	In	Out	Reg Hrs	OT Hrs	Signature	Supervisor's Remarks
Leonardo Alzate	ACRH	5:00	16:30	8	3	<i>R. Alzate</i>	
Paul Bovell	ACRH	6:00	16:30	8	2	<i>P. Bovell</i>	
Roger Williams	ACRH	6:00	16:30	8	2	<i>R. Williams</i>	
Thomas Kelly	CM						A/L
<i>Franzellie</i>	C.M.						

ON STREET	CROSS STREETS	FEET
	<i>Columbus Ave & a.</i>	<i>97th Street</i>

WORK PERFORMED	MATERIALS USED	KMCS
SIDEWALK & CURB	Ready Mix Concrete	→ 7 → Cu. Yds.
<i>Poured Islands - D 20' S. →</i>	Sq. Ft. Lumber	Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb straight	Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb full Nose	Pieces
Curb Form	Lin. Ft. Detectable Earning → (2x5) - 4 →	Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints	Lin. Ft.
PREP & CAVE-IN	Snap Caps	→ Lin. Ft.
Debris Removal	Cu. Yds. Caulking	Tube
Backfill	Cu. Yds. Sealant Sp	Gal.
Asphalt Patch	Tons Sand	Cu. Yds.
STEP STREETS	Cu. Yds. Stone	Cu. Yds.
Landing	Sq. Ft. Other:	
Pointing/Caulking/Patching	Lin. Ft.	
Step Replacement	Lin. Ft.	

VEHICLES & EQUIPMENT

Crew Cab Mason Truck	Mason Dump Truck	Backhoe	Large Dump Truck	Light Duty Truck
Truck #: <i>1122627</i>	Truck #:	Truck #:	Truck #:	Truck #:
Medium Dump Truck	Hydraulic Excavator	Towmaster	Tag-A-Long Trailer	Utility Service Truck
Truck #: <i>0019-A</i>	Truck #:	Truck #:	Truck #:	Truck #:

COMMENTS:

We went to Locust on Columbus Ave & W 97th. And, poured an island. With 4 bags concrete, we used 7 cu.yards x (2x5) of mats. place drums. clean up of seconds. The job set.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Crew Lead

Approved By

Title

Jean Burke

Supervisor

DAILY GANG REPORT

Borough QueensDay ThursdayDate 9/19/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Joseph Taranto	HR	5:00	16:30	8	3	<i>[Signature]</i>	50% COL 10/18/13
							100%
							34TH &
							14TH

ON STREET	CROSS STREET
College Point Yards (Av)	
Calvin's Ave at 97st	69st (man)
111st at 34 Av (CQ)	

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
Sidewalk Pour	Sq. Ft. Steel Curb, Straight Lin. Ft.
Curb Prep	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Warning Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Cuts Lin. Ft.
Debris Removal	Cu. Yds. Caulk Tubing
Backfill	Cu. Yds. Sealant Spray Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other
Pointing/Caulking/Patching	Lin. Ft.
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
Other:				

COMMENTS: Checked on crews of locations, returned to yard to do paperwork

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

[Signature]

Supervisor

**DOT SIDEWALK INSPECTION MANAGEMENT
CITYWIDE CONCRETE PROGRAM - DAILY GANG REPORT**

Borongh: BronxDate: Thursday 19-2013**SIGN IN**

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
F. Johnson	CM	6:00	15:30	7	4	J. Johnson	50% SSS
							50% PON
Total Hrs.							

Location	From	To
Columbus Avenue & 67 St		
168 St + Clay Avenue		

STEP STREETS	PREP & CAVE-IN		
Coping	Lin. Ft.	Fill	Cu. Yd.
Sidewalk	Sq. Ft.	Debris	Cu. Yd.
Walls	Cu. Ft.	Opening	Sq. Yd.
Pointing & Patching	Lin. Ft.		
MATERIAL USED	CURB WORK		
Ready Mix	2 + 6 = 8 Cu. Yd.	Sidewalk Prep	Sq. Ft.
Hand Mix	Cu. Yd.	Sidewalk Pour	Sq. Ft.
Cement	Bags	Curb Prep	Lin. Ft.
Sand/Stone	Cu. Yd.	Curb Pour	Lin. Ft.
Lumber	Lin. Ft.	Paving Block	Unit
Expansion Joint	Unit	Forming	Lin. Ft.

VEHICLES & EQUIPMENT


CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #: 1074632 ✓
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other:

Comments: Pour and Finish ready mix concrete at 68 street and Columbus Avenue to Manhattan. Then 168 Street and Clay Avenue Bronx. J. Johnson

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF THE CITY OF NEW YORK

Signature



Title

Supervisor

Approved By

Title

Citywide Concrete Program

**DOT SIDEWALK INSPECTION MANAGEMENT
CITYWIDE CONCRETE PROGRAM - DAILY GANG REPORT**

Borough: BRONXDate: Thursday 19. 2013**SIGN IN**

Name	Title	In	Out	Reg Hrs	OT Hrs	Signature	Supervisor's Remarks
F. Johnson	CM	6:45	15:30	7	4	<u>F. Johnson</u>	
Total Hrs.							

Location	From	To
Columbus Avenue & 67 St 168st + Clay Avenue		

STEP STREETS		PREP & CAVE-IN	
Coping	Lin. Ft.	Fill	Cu. Yd.
Sidewalk	Sq. Ft.	Debris	Cu. Yd.
Walls	Cu. Ft.	Opening	Sq. Yd.
Pointing & Patching	Lin. Ft.		
MATERIAL USED		CURB WORK	
Ready Mix	2 + 6 = 8 Cu. Yd	Sidewalk Prep	Sq. Ft.
Hand Mix	Cu. Yd.	Sidewalk Pour	Sq. Ft.
Cement	Bags	Curb Prep	Lin. Ft.
Sand/Stone	Cu. Yd.	Curb Pour	Lin. Ft.
Lumber	Lin. Ft.	Paving Block	Unit
Expansion Joint	Unit	Forming	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe	Large Dump Truck Truck #:	Light Duty Truck Truck # 1024632 ✓
Medium Dump Truck Truck #:	Hydraulic Excavator #	Towmaster Truck #:	Tag-A-Long Trailer Truck #:	Utility Service Truck Truck #:
Other:				

Comments: Pour and finish ready mix concrete at 68st and Columbus Avenue ~~in Manhattan~~, then 168 Street and Clay Avenue Bronx. Formed

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF THE CITY OF NEW YORK

Signature

Title

Approved By

Title

Citywide Concrete Program

DOT/SIM/CITYWIDE CONCRETE

- DAILY GANG REPORT

Borough Queens 44ton

Day friday

Date 9/20/13

SIGN IN

from 44 to 48

ON STREET	CROSS STREET
Columbus Ave Safety Removal Longfellow & Bricker Rd Blw	Columbus Ave Safety Removal Longfellow & Bricker Rd Blw

RETURN TO 44bok

WORK PERFORMED	MATERIALS USED	
Cobblestone/Pavers	Ready Mix Concrete	Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone	Sq. Ft.
Pavers	Sq. Ft. Pavers	Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks	Ea.
Steps & Walls	Lumber	Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking	Tube
Step Replacement	Lin. Ft. Cement	Bags
Wall Forming	Sq. Ft. Mortar Mix	Bags
Wall Installing	Sq. Ft. Sand	Cu. Yds.
Prep & Cave-In	Stone	Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints	Lin. Ft.
Backfill	Cu. Yds. Detectable Warning	Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:

Other: MINI RACER TRUCK #0367

COMMENTS:

SET up safety on longfellow's buckner blvd
Removed safety from columbus ave —

I CERTIFY THAT THE TIME OF THE EMPLOYEE'S RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Title

Approved By

Title

Crew Leader

17

Supervisor

Supervisor

Borough Queens

Day Friday

Date 09-20-13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
Leonardo Alzate	ACHR	7:00	16:30	8	3	<i>SP</i>	
Paul Bovell	ACHR	6:00	16:30	8	2	<i>Boyle</i>	
Roger Williams	ACHR	8:00	16:30	8	2	<i>Williams</i>	
Thomas Kelly	CM						A/C -

ON STREET

CROSS STREET

41 DR YARD
Centurion Bus Inv # W12 To 104 st.
Springfield

WORK PERFORMED	MATERIALS USED
SIDEWALK & CURB	Ready Mix Concrete Cu. Yds.
Sidewalk Prep	Sq. Ft. Lumber Lin. Ft.
	Sq. Ft. Steel Curb, Raft Lin. Ft.
<i>strip - 130</i>	Lin. Ft. Steel Curb, Bull Nose Pieces
Curb Form	Lin. Ft. Detectable Strung Sq. Ft.
Curb Pour	Lin. Ft. Expansion Joints Lin. Ft.
PREP & CAVE-IN	Snap Caps Lin. Ft.
Debris Removal	Caulking Tube
Backfill	Cu. Yds. Sealant Sp. Gal.
Asphalt Patch	Tons Sand Cu. Yds.
STEP STREETS	Cu. Yds. Stone Cu. Yds.
Landing	Sq. Ft. Other: <i>Paint the steel</i>
Pointing/Caulking/Patching	Lin. Ft. <i>Pick up the safety & Rem forms</i>
Step Replacement	Lin. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #: <i>1122627</i>	Mason Dump Truck Truck #: <i>1</i>	Backhoe Truck #: <i>1</i>	Large Dump Truck Truck #: <i>1</i>	Light Duty Truck Truck #: <i>1</i>
Medium Dump Truck Truck #: <i>1</i>	Hydraulic Excavator	Towmaster Truck #: <i>1</i>	Tag-A-Long Trailer	Utility Service Truck Truck #: <i>1</i>
Other: <i>0019-D</i>				

COMMENTS:

We went to location on Colum Bus Ave. & W 110 Ave. & removed the forms & cleanup. Also we painted the steel form. W 110 st. up to W 103 on Colum Bus Ave. & pick up the safety. Cleaned up & secured the job site.

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature

Crew Leader

Approved By

Supervisor

DOT/SIM/CITYWIDE CONCRETE

~~COLUMBUS AVE PROJECT~~ - DAILY GANG REPORTBorough Queens 44+OK Day FridayDate 9/20/13

SIGN IN

Name	Title	In	Out	Reg. Hrs.	OT Hrs.	Signature	Supervisor's Remarks
LARRY STORES ACHIEV		3:00PM	3:30AM	8	4	<i>[Signature]</i>	50% SSS
							50% NON

FROM 44+OK

ON STREET	CROSS STREET
COLUMBUS AVE SAFETY REMOVAL LONGFELLOW & BRUCKNER BLVD	COLUMBUS AVE SAFETY REMOVAL LONGFELLOW & BRUCKNER BLVD

RETURN TO 44+OK

WORK PERFORMED	MATERIALS USED
Cobblestone/Pavers	Ready Mix Concrete Cu. Yds.
Cobblestone	Sq. Ft. Cobblestone Sq. Ft.
Pavers	Sq. Ft. Pavers Sq. Ft.
Concrete Roadbase	Sq. Ft. Cinder Blocks/Bricks Ea.
Steps & Walls	Lumber Lin. Ft.
Pointing/Caulking/Patching	Lin. Ft. Caulking Tube
Step Replacement	Lin. Ft. Cement Bags
Wall Forming	Sq. Ft. Mortar Mix Bags
Wall Installing	Sq. Ft. Sand Cu. Yds.
Prep & Cave-In	Stone Cu. Yds.
Debris Removal	Cu. Yds. Expansion Joints Lin. Ft.
Backfill	Cu. Yds. Detectable Warning Sq. Ft.

VEHICLES & EQUIPMENT

CrewCab Mason Truck Truck #:	Mason Dump Truck Truck #:	Backhoe #:	Large Dump Truck Truck #:	Light Duty Truck Truck #:
Medium Dump Truck Truck #:	Hydraulic Excavator #:	Towmaster Truck #:	Tag-A-Long Trailer #:	Utility Service Truck Truck #:
<u>Other: MINI RACK TRUCK #0367</u>				

COMMENTS:

SET UP SAFETY ON LONGFELLOW & BRUCKNER BLVD,
REMOVED SAFETY FROM COLUMNS AVE —

I CERTIFY THAT THE TIME OF THE EMPLOYEES RECORDED ABOVE IS CORRECT AND THAT THE ABOVE WORK PERFORMED WAS EXCLUSIVELY FOR THE BENEFIT OF NYC

Signature



Title

Crew Leader

Approved By



Title

Supervisor

NYC DEPARTMENT OF TRANSPORTATION

CONCRETE PROGRAM

Adam Clayton Powell Jr. Blvd (M)

6/13/13 - 9/17/13

REGULAR LABOR

CIVIL ENGINEER II @ \$50.79/HR FOR	Hrs.	\$	-
MASON @ \$40.46/HR FOR	171 Hrs.	\$	6,919
MGO @ \$50.70/HR FOR	35 Hrs.	\$	1,775
ACHR @ \$22.03/HR FOR	1413 Hrs.	\$	31,128
TRACTOR OPERATOR @ \$50.70/HR FOR	59 Hrs.	\$	2,991
BRICKLAYER @ \$40.05/HR FOR	42 Hrs.	\$	1,682
HR @ \$39.46/HR FOR	337 Hrs.	\$	13,298
SHR @ \$35.73/HR FOR	Hrs.	\$	-
CLERICAL ASSOCIATE@ \$13.62/HR FOR	Hrs.	\$	-
	SUB-TOTAL	\$	<u>57,793</u>

OVERTIME

CIVIL ENGINEER II @ \$76.19/HR FOR	Hrs.	\$	-
MASON @ \$80.92/HR FOR	75 Hrs.	\$	6,069
MGO @ \$76.05/HR FOR	9 Hrs.	\$	684
ACHR @ \$33.05/HR FOR	377 Hrs.	\$	12,460
TRACTOR OPERATOR @ \$76.05/HR FOR	19 Hrs.	\$	1,445
BRICKLAYER @ \$60.08/HR FOR	24 Hrs.	\$	1,442
HR @ \$59.19/HR FOR	94 Hrs.	\$	5,564
SHR @ \$53.60/HR FOR	Hrs.	\$	-
CLERICAL ASSOCIATE@ \$20.43/HR FOR	Hrs.	\$	-
	SUB-TOTAL	\$	<u>27,664</u>

FRINGE \$ 37,395INDIRECT \$ 28,209TOTAL PS COSTS \$ 151,061VEHICLES/EQUIPMENT

D/RACK/MASON TRUCKS @ \$60/DAY FOR	119 Days	\$	7,140
PICK-UPS @ \$35/DAY FOR	76 Days	\$	-
BACKHOE @ \$110/DAY FOR	11 Days	\$	1,210
SEDANS/VANS @ \$16/DAY FOR	Days	\$	-
FF TRUCKS @ \$140/DAY FOR	11 Days	\$	1,540
ZIM MIXER @ \$220/DAY FOR	Days	\$	-

TOTAL VEHICLE COST \$ 9,890MATERIALCONCRETE @ \$130/CY \$ 10,010STEEL CURB @ \$20/LF \$ -DETECTABLE WARNING TILE @ \$17/PC \$ -DEBRIS REMOVAL @ \$25.00/CY \$ 3,850DEBRIS CONTAINERS \$ -STONE @ \$26.50/ CY \$ -LUMBER @ \$10.00/LF \$ -TOTAL MATERIAL COST \$ 13,860TOTAL PROJECT COST \$ 174,811
